



"ইলগাস ভবন", এইচ-সি ব্লক, সেক্টর-৩, বিধাননগর, কলকাতা-৭০০ ১০৬, পশ্চিমবঙ্গ "ILGUS BHAVAN", H-C Block, Sector - III, Bidhannagar, Kolkata - 700 106, West Bengal

SUDA- 23/2014(MPR-1)	17.08.2018
ক্ৰমিক নং	তারিখ

To: Commissioner/ Chairperson,
......Municipal Corporation/ Municipality

(Asansol/ Chandernagar/ Howrah/ Jalpaiguri/ Berhampore/ Barrackpore/ Halisahar/ Habra/ Bhatpara/ Bankura/ Uttarpara/ Englishbazar/ Titagarh/ Rajpur-Sonarpur/ Mahestala/ Tamralipta/ Arambag/ Barasat/ North Dum Dum/ Jiaganj-Azimganj/ Balurghat/ Tarakeswar/ Madhyamgram/ Dum Dum/ Naihati/ Kaliyaganj/ Beldanga/ Islampur/Santipur/ Katwa)

Sub: Minutes of review meeting on Physical & Financial Progress of sanctioned Shelter units under the scheme Shelter for Urban Homeless (SUH) under DAY-NULM on 09.08.2018 at Conference Hall of SUDA

Madam/Sir,

Kindly find enclosed herewith a copy of minutes of review meeting on Physical & Financial Progress of sanctioned Shelter units under the scheme Shelter for Urban Homeless (SUH) under DAY-NULM on 09.08.2018 at Conference Hall of SUDA for information and necessary action.

Enclo: As stated

Yours faithfolly,

Deputy Director, SUDA

Memo No. 23/2014(MPR-1)/800/1(3) Copy forwarded with a copy of minutes to

Date: 17.08.2018

- 1. Jt. Secretary (S. Das), UD & MA Dept./ Additional Mission Director, WBSULM for information
- 2. Chief Engineer MED for information & with the request sent the minutes to the concerned Superintendent/ Executive Engineers of MED for information and necessary action.
- 3. SMM-S & S I, WBSULM, SUDA for information and necessary action.

Deputy Director, SUDA

Tel: 2358 6403/5767, Fax: 2358 5800, E-mail: wbsudadir@gmail.com

Minutes of the review meeting on physical & financial progress of sanctioned shelter units under the scheme Shelter for Urban Homeless (SUH) under DAY-NULM held on 09.08.2018 at Conference Hall, SUDA

Official Present:

1) Sr. D.P. Karanam, IAS	Director, SUDA
2) Sri Ashis Saha	Deputy Director, SUDA
3) Sri Amit Das,	
4) Sri Soumen De	SMM- S & SI, WBSULM, SUDA
5) Sri Saumya Bandhyopadhay	AE, Chief Engineer office, MED

Others Present:

- 1) Superintendent Engineers & Executive Engineers, MED
- 2) ULB representatives (Commissioner/ Chairperson/ City Mission Manager/ Municipal Engineer)

Sri. D.P. Karanam, Director, SUDA was on the chair

Agenda: Present physical & financial progress of ongoing work of SUH & Tentative date of completion of ongoing project.

Director, SUDA reviewed the progress of SUHs, ULB wise and discussed about the progress with ULB representatives and Superintendent Engineers & Executive Engineers concerned Divisions of MED. A detail deliberation was made in the meeting regarding the civil construction work, Electrification work & procurement of furniture & utensils of SUH. Each ULB informed about their status of work & tentative time line of completion of work as fixed by the ULBs.

Howrah Municipal Corporation: It was informed by the Executive Engineer, HMC that, work order for electrical works has been issued and it is expected that it will be completed within 31 st August, 2018 the, shelter unit will be made functional. Director, SUDA suggested to complete the work within the due time and also asked about the progress of other SUHs. It was informed by the EE, HMC that alternative land was identified, but it is occupied by existing old building. Further four lands were identified by the Corporation for SUH and it is under consideration of Corporation. Director, SUDA suggested that Corporation may take steps immediately to arrange the alternative land for another sanctioned SUH. He also directed to inform to this office if land identification is not possible for another SUH, if so.

Jalpaiguri Municipality: It was informed by the CMM of NULM that the shelter unit is functional and final UC is yet to be submitted. It is also informed that the final bills are under process and it will be submitted by 31 st, Aug. The representative of ULB said that an additional amount is required for additional work in SUH. In response to this Director SUDA informed that after submission of full UC of received fund the proposal of additional fund will be placed before state level project sanction Committee for consideration.

Berhampore Municipality: It was informed by the ULB that, the construction work of SUH is in progress and work order has been issued for electrical work. UC submitted by the ULB. It was mentioned by the ULB representatives that it is expected the shelter unit will be completed by December, 2018. ULB was advised to complete other necessary works and formalities so that Building can be made functional once it is completed.

Barrackpore Municipality: It appears in the meeting that no representative is present from the ULB. Executive Engineer MED informed about the progress of the work at Barrackpore that physical progress is 50% and the construction work expected to be completed by January, 2019. Director, SUDA suggested to send a letter to the concerned ULB to submit their plan for functionalization of SUH.

Chandernagar Corporation: It was informed by the Commissioner, Chandernagar Corporation that for electrical work tender has been floated 2 nd time and tentative date of completion of SUH is rescheduled and it is 3 rd week of September 2018. Already review meeting was done at ULB level for monitoring of progress of work with the concerned Executive Engineer and contractor. Selection of NGO for Operation & maintenance is under process. Director, SUDA suggested that effort should be made to start the shelter home before winter.

Halisahar Municipality: It was informed by the representative of municipality that the civil work is under process and electrical work tender will be initiated after vetting of estimate. It is expected that the construction work will be completed by February, 2019 and it will be made operational.

Asansol Corporation: Assistant Engineer, AMC informed about the progress of the work at Jamuria is 90% & electrical work tender is in process, at Raniganj 30% and at Kulti 25 % in progress. It was suggested by the Director to emphasise the work and to submit the updated UC and to submit up dated status report of all sanctioned shelters regularly. It was recalled in the meeting that Corporation has submitted a proposal for alternative land for SUH at Asansol and it appears from the proposal that the land is private property and as per record of land different owner involved. Director, SUDA suggested submit proper documents regarding the proposed land and feasibility report also.

Bhatpara Municipality: It was informed by the ULB as well as EE, MED that work order issued on May, 2018 and due to poor site condition work was started behind schedule, recently site was developed by sand filling and earth work in excavation. Already a letter was sent to the ULB from Executive Engineer, MED for proper implementation of work. It was suggested by the Director, SUDA to expedite the work as the project was sanctioned on 2017.

Bankura Municipality: It was informed by the representative of ULB and Executive Engineer, MED that due to repeated change of site and detailed design & drawing work is delayed, now 15 % work has been done. Now piling work is completed and further soil test has been done to explore the present bearing capacity of soil. It was also informed that it is expected the work will be completed by March, 2019.

Habra Municipality: It was informed by the representative of municipality that the civil work is under process (50%) and work order for electrical work has been issued to the concerned agency. It is expected that the construction work completed by December, 2018 and all the corresponding work for functionalization of shelter will be done accordingly.

Uttarpara- kotrang Municipality: It was informed by the ULB official due to some local problem progress of work is very slow and it is expected it will be resolved shortly. Now the progress of the work is 30%. It was recalled in the meeting the work was started on November, 2017. Director, SUDA suggested that Municipality should resolve the issue at the earliest and completer work.

Titagarh: It was informed by the ULB official that Tender for the construction work was floated but due to non availability of eligible bidder and it was cancelled. Now it is 2 nd call of Tender and Technical Bid opened and it was sent to Executive Engineer, MED for further process. Director, SUDA requested to Chief Engineer, MED to earliest action for this.

Rajpur- Sonarpur: It was informed by the ULB official that construction work is in under progress (50%) and tender has been floated for electrical work. Director, SUDA requested to ULB representative to submit the UC of 1 st instalment.

Mahestala: It was informed by the ULB official that construction works is in under progress and tender for electrical work has been initiated. It was mentioned by the ULB officials that construction work will be completed by December, 2018.

Tamralipta: It was informed by the ULB official that the construction work now is at ground level & it is under process and tender will be floated soon for electrical work. Director, SUDA requested to expedite tnder process and start the work at earliest.

Arambag: It was informed by the ULB official that finishing work is going on in SUH and it is expected that the work will be completed in all respect by September, 2018. The shelter unit will be made functional by Oct, 2018. It was suggested to the ULB to take necessary actions for corresponding works of functionalization of SUH at the earliest.

North Dum Dum: It was informed by the ULB official that Tender was floated but due to Technical reason and further 2 calls were cancelled due to insufficient number of eligible bidder. On 21.07.2018 Technical bid was opened and it was sent to the concerned Executive Engineer, MED.

Barasat: It was informed by the ULB official due to some local problem the work is not started till now. ULB officials informed that alternative land has been identified by the ULB and soil investigation work is under process. Director, SUDA suggested to send the report at the earliest as the shelter unit was sanctioned one year ago.

Santipur: It was informed by the ULB official due to poor bearing capacity of soil, identified land of SUH has been changed. New land has been identified and soil test report with relevant documents has been sent to the Director, SUDA. It was informed by the Executive Engineer, MED that detailed preparation of design & drawing, estimate is under process and it will be sent to the ULB at the earliest. Director, SUDA requested the Chief Engineer, MED to earliest action for this

Jiaganj-Ajimganj: SAE of concerned ULB informed about the progress of the work. Now progress of the work is 30% and forelectrical work vetting is under process. Director, SUDA

suggested to expedite the work and to sent a letter to the concerned execution agency for implementation of the work as per schedule.

Balurghat: It was informed by the ULB official that construction work is going on (50%) & final bid opened for electrical work and it is expected that the work will be completed on Dec, 2018.

Tarakeswar: It was informed by the ULB official that construction work is going on (60%) & tender has been floated for electrical works and it is expected that the work will be completed on Dec, 2018. Director, SUDA requested to submit the subsequent UC of SUH.

Madhyamgram: It was informed by the ULB official that construction work is going on (40%) as the SUH building is converged with a market complex on ground floor therefore after completion of work at ground floor rest part of the building will be constructed and it is expected that it will be completed by March, 2019.

Dum Dum: It was informed by the ULB official that detailed design drawing is prepared and estimate preparation is prepared and submitted to Executive Engineer, MED for further approval. After the approval tender will be floated. It was suggested to the ULB to float an integrated tender for civil & electrical work. Director, SUDA requested to Chief Engineer, MED to earliest action for this.

Naihati: It was informed by the ULB official that Tender has been floated for civil work and technical bid will be opened on 20.08.2018.

Kaliyaganj: It was informed by the concerned Executive Engineer, MED that soil test report is yet to be received by the MED and after this detail design & drawing estimate will be prepared accordingly. Kaliyaganj Municipality is requested to send that report.

Beldanga: It was informed by the concerned Executive Engineer, MED that soil investigation report is yet to be received by the MED and after this detail design & drawing estimate will be prepared accordingly.

Islampur: It was informed by the ULB official that vetted copy of detailed design, drawing and estimate are yet to be received from MED and tender will be floated accordingly.

Katwa: It was informed by the concerned Executive Engineer, MED that Tender has been floated for civil work and electrical works estimate is under preparation.

It was recalled by Director, SUDA that the State Level Monitoring Committee has been suggested to functional the under construction shelters before the upcoming winter session to cover the homeless population and to provide them shelters. Proposal for additional fund of different ULBs will be placed before SLPSC after completion of the work and submission of full UC of the work and fund will be released accordingly. Director SUDA suggested to the all ULBs to process the other works i.e. procurement of furniture, formation of Shelter Management Committee, identification of homeless person for mobilization of them before functionalization of SUH.

The meeting ended with a vote thanks to and from the Chair.

D.P. Karanam, IAS Director, SUDA





"ইলগাস ভবন", এইচ-সি ব্লক, সেক্টর-৩, বিধাননগর, কলকাতা-৭০০ ১০৬, পশ্চিমবঙ্গ "ILGUS BHAVAN", H-C Block, Sector - III, Bidhannagar, Kolkata - 700 106, West Bengal

-			4 1
ক্রমিক	नः SUDA23/2014(MPR-1	1890	(29)

তারিখ 06:08:2018-----

From: Director, SUDA

& Mission Director, WBSULM

To: Commissioner/ Chairperson,

......Municipal Corporation/ Municipality

(Asansol/ Chandernagar/ Howrah/ Jalpaiguri/ Berhampore/ Barrackpore/ Halisahar/ Habra/ Bhatpara/ Bankura/ Uttarpara/ Englishbazar/ Titagarh/ Rajpur-Sonarpur/ Mahestala/ Tamralipta/ Arambag/ Barasat/ North Dum Dum/ Jiaganj-Azimganj/ Balurghat/ Tarakeswar/ Madhyamgram/ Dum-Dum/ Naihati/ Kaliyaganj/ Beldanga/ Islampur/Santipur)

Sub: Review meeting on Physical & Financial Progress of sanctioned Shelter units under the scheme Shelter for Urban Homeless (SUH) under DAY-NULM

Madam/Sir.

In partial modification of vide memo no. SUDA-23/2014(MPR1)/880(33) dated: 02.08.2018 of this office, I would like to inform you that the review meeting on physical & financial progress of sanctioned shelter units under the scheme Shelter for Urban Homeless (SUH) would be held on Conference Hall, SUDA on **09.08.2018 at 02.00 PM** instead of 11.00 AM.

This is for your kind information.

Yours faithfully,

Director, SUDA

& Mission Director, WBSULM

Date: 06.08.2018

Memo No. 23/2014(MPR-1)/890(29)/1(4)

Copy forwarded to

1. Jt. Secretary (S. Das), UD & MA Dept./ Additional Mission Director, WBSULM for information

2. Chief Engineer MED with the request to attend the meeting and to inform to the concerned Superintendent/ Executive Engineers of MED to attend the meeting.

3. Deputy Director, SUDA

& SMM-S & S I, WBSULM, SUDA.

Director, SUDA 6/8/00

& Mission Director, WBSULM

Minutes of the review meeting on physical & financial progress of sanctioned shelter units under the scheme Shelter for Urban Homeless (SUH) under DAY-NULM held on 09.08.2018 at Conference Hall, SUDA

Official Present:

1) Sr. D.P. Karanam, IAS	Director, SUDA
2) Sri Ashis Saha	Deputy Director, SUDA
3) Sri Amit Das,	Chief Engineer, MED
4) Sri Soumen De	SMM- S & SI, WBSULM, SUDA
5) Sri Saumya Bandhyopadhay	AE, Chief Engineer office, MED

Others Present:

- 1) Superintendent Engineers & Executive Engineers, MED
- 2) ULB representatives (Commissioner/ Chairperson/ City Mission Manager/ Municipal Engineer)

Sri. D.P. Karanam, Director, SUDA was on the chair

Agenda: Present physical & financial progress of ongoing work of SUH & Tentative date of completion of ongoing project.

Director, SUDA reviewed the progress of SUHs, ULB wise and discussed about the progress with ULB representatives and Superintendent Engineers & Executive Engineers concerned Divisions of MED. A detail deliberation was made in the meeting regarding the civil construction work, Electrification work & procurement of furniture & utensils of SUH. Each ULB informed about their status of work & tentative time line of completion of work as fixed by the ULBs.

Howrah Municipal Corporation: It was informed by the Executive Engineer, HMC that, due to repeated sender for Electrical Work and new work order has been issued by HMC. It was also informed by Executive Engineer, HMC that it is expected that the electrical work will be completed within Quays and by 31 st August, 2018 the shelter unit will be made functional. Director, SUDA suggested to complete the work within the due time a also asked about the progress of other SUHs. It was informed by the EE, HMC that alternative land was identified & but it is occupied by existing old building. Further four lands were identified by the Corporation for SUH and it is under consideration of Corporation. Director, SUDA suggested that Corporation may take steps immediately to arrange the alternative land for another sanctioned SUH. He also directed to inform to this office if land identification is not possible for another SUH, it so.

I black order for Electrical works has been usued and it
is expected that it ---

Jalpaiguri Municipality: It was informed by the CMM of NULM that the shelter unit is functional and final UC is yet to be submitted. It is also informed that the final bills are under process and it will be submitted by 31 st, Aug. Discalso informed to the representatives of ULB that an additional amount is required for additional work in SUH. In response to this Director SUDA informed that after submission of full UC of received fund the proposal of additional fund will be considered: placed to fine state well project to receive for Committee for Committe

Berhampore Municipality: It was informed by the ULB that, the construction work of SUH is in progress and work order has been issued for electrical work. It was also informed the UC subsubmitted by the ULB. It was mentioned by the ULB representatives that it is expected the shelter unit will be completed by December, 2018. ULB was advited to complete other hearing works and formetter for Building on be patterned to the hearing works and formetter for the land on the patterned to the hearing works and formetter formed the Barrackpore Municipality: It appears in the meeting that no representative is present from

the ULB. Executive Engineer MED informed about the progress of the work at Barrackpore. The Utwas also informed that the progress of the work 50% and the construction work be completed by January, 2019. Director, SUDA suggested to sent a letter to the concerned ULB to submit their plan for functionalization of SUH.

Chandernagar Corporation: It was informed by the Commissioner, Chandernagar Corporation that for electrical work tender has been floated 2 nd time and tentative date of completion of SUH is rescheduled and it is 3 rd week of September 2018. Already review meeting was done at ULB level for monitoring of progress of work with the concerned Executive Engineer and contractor. Selection of NGO for Operation & maintenance is under process. Director, SUDA supposed that effort should be made to that the Melter home higher winter

Halisahar Municipality: It was informed by the representative of municipality that the civil work is under process and electrical work tender will be initiated after vetting of estimate. It is expected that the construction work will be completed by February, 2019 and it will be made operational.

Asansol Corporation: It was informed by the representative Assistant Engineer, AMC informed about the progress of the work at Asansol It was also informed that progress of work at Jamuria is 90% & electrical work tender is in process, at Raniganj 30% and at Kulti 25 % in progress. It was suggested by the Director to emphasise the work and to submit the updated UC and to submit up dated status report of all sanctioned shelters regularly. It was recalled in the meeting that Corporation has submitted a proposal for alternative land for SUH at Asansol and it appears from the proposal that the land is private property and as per record of land different owner involved. Director, SUDA suggested submit proper documents regarding the proposed land and feasibility report also.

Bhatpara Municipality: It was informed by the ULB as well as EE, MED that work order issued on May,2018 due to poor site condition work was started behind schedule. The recently site was developed by sand filling and earth work in excavation. Already a letter was sent to the ULB from Executive Engineer, MED for proper implementation of work. It was suggested by the Director, SUDA to expedite the work as the project was sanctioned on 2017.

Bankura Municipality: It was informed by the representative of ULB and Executive Engineer, MED that due to repeated change of site condition and detailed design & drawing work is delayed, now 15 % work has been done. Now piling work is completed and further soil test has been done to explore the present bearing capacity of soil. It was also informed that it is expected the work will be completed by March, 2019.

板

Habra Municipality: It was informed by the representative of municipality that the civil work is under process (50%) and work order for electrical work has been issued to the concerned agency. It is expected that the construction work completed by December, 2018 and all the corresponding work for functionalization of shelter will be done accordingly.

Uttarpara- kotrang Municipality: It was informed by the ULB official due to some local problem progress of work is very slow and it is expected it will be resolved shortly. Now the progress of the work is 30%. It was recalled in the meeting the work was started on November, 2017. Director, SUDA suggested that the decision should be taken by the municipality for clearance of land at the earliest for necessary implementation of work.

Titagarh: It was informed by the ULB official that Tender for the construction work was floated but due to non availability of eligible bidder and it was cancelled. Now it is 2 nd call of Tender and Technical Bid opened and it was sent to Executive Engineer, MED for further process. Director, SUDA requested to Chief Engineer, MED to earliest action for this.

Rajpur- Sonarpur: It was informed by the ULB official that construction work is a under progress (50%) and tender has been floated for electrical work. Director, SUDA requested to ULB representative to submit the UC of 1 st instalment.

Mahestala: It was informed by the ULB official that construction works is a under progress and tender for electrical work has been initiated. It was mentioned by the ULB officials that construction work will be completed by December, 2018.

Tamralipta: It was informed by the ULB official that the construction work now is at ground level & it is under process and tender will be floated soon for electrical work. Director, SUDA requested to expedite the work and to complete the work on scheduled time. Tender process and atomt the work at entirest.

Arambag: It was informed by the ULB official that finishing work is going on in SUH and it is expected that the work will be completed in all aspect of September, 2018. The shelter unit will be made functional by Oct, 2018. It was suggested to the ULB to take necessary actions for corresponding works of functionalization of SUH at the earliest.

North Dum Dum: It was informed by the ULB official that Tender was floated but due to Technical reason and further 2 calls were cancelled due to insufficient number of eligible bidder. On 21.07.2018 Technical bid was opened and it was sent to the concerned Executive Engineer, MED.

Barasat: It was informed by the ULB official due to some local problem the work is not started till now. ULB officials informed that alternative land has been identified by the ULB and soil investigation work is under process. Director, SUDA suggested to process the report at the earliest as the shelter unit was sanctioned one year ago.

Santipur: It was informed by the ULB official due to poor bearing capacity of soil, identified land of SUH has been changed. New land has been identified and soil test report with relevant documents has been sent to the Director, SUDA. It was informed by the Executive Engineer, MED that detailed preparation of design & drawing, estimate is under process and it will be sent to the ULB at the earliest. Director, SUDA requested Chief Engineer, MED to earliest action for this.

Jiaganj-Ajimganj: SAE of concerned ULB informed about the progress of the work. Now progress of the work is 30% and electrical work, vetting is under process. Director, SUDA

suggested to expedite the work and to sent a letter to the concerned execution agency for implementation of the work as per schedule.

Balurghat: It was informed by the ULB official that construction work is going on (50%) & final bid opened for electrical work and it is expected that the work will be completed on Dec, 2018.

Tarakeswar: It was informed by the ULB official that construction work is going on (60%) & tender has been floated for electrical works and it is expected that the work will be completed on Dec, 2018. Director, SUDA requested to submit the subsequent UC of SUH.

Madhyamgram: It was informed by the ULB official that construction work is going on (40%) as the SUH building is converged with a market complex on ground floor therefore after completion of work at ground floor rest part of the building will be constructed and it is expected that it will be completed by March, 2019.

Dum Dum: It was informed by the ULB official that detailed design drawing is prepared and estimate preparation is prepared and submitted to Executive Engineer, MED for further approval. After the approval tender will be floated. It was suggested to the ULB to float an integrated tender for civil & electrical work. Director, SUDA requested to Chief Engineer, MED to earliest action for this.

Naihati: It was informed by the ULB official that Tender has been floated for civil work and technical bid will be opened on 20.08.2018.

Kaliyaganj: It was informed by the concerned Executive Engineer, MED that soil test report is yet to be received by the MED and after this detail design & drawing estimate will be prepared accordingly. Kaliyagunj muniupally is hegulists send that lepot

Beldanga: It was informed by the concerned Executive Engineer, MED that soil investigation report is yet to be received by the MED and after this detail design & drawing estimate will be prepared accordingly.

Islampur: It was informed by the ULB official that vetted copy of detailed design, drawing and estimate are yet to be received from MED and tender will be floated accordingly.

Katwa: It was informed by the concerned Executive Engineer, MED that Tender has been floated for civil work and electrical works estimate is under preparation.

It was recalled by Director, SUDA that the State Level Monitoring Committee has been suggested to functional the under construction shelters before the upcoming winter session to cover the homeless population and to provide them shelters. It was informed by Director SUDA that proposal for additional fund of different ULBs will be considered after completion of the work and submission of full UC of the work and fund will be released accordingly. Director SUDA suggested to the all ULBs to process the other works i.e. procurement of furniture, formation of Shelter Management Committee, identification of homeless person for mobilization of them before functionalization of SUH.

The meeting ended with a vote thanks to and from the Chair.





"ইলগাস ভবন", এইচ-সি ব্রক, সেক্টর-৩, বিধাননগর, কলকাতা-৭০০ ১০৬, পশ্চিমবঙ্গ "ILGUS BHAVAN", H-C Block, Sector - III, Bidhannagar, Kolkata - 700 106. West Bengal

ক্রমিক নং 🤉	SUDA23/2014	(MPR-1)/
-------------	-------------	--------	----

তারিখ ০৫.08.2018-----

From: Director, SUDA

& Mission Director, WBSULM

To: Commissioner/ Chairperson,

......Municipal Corporation/ Municipality

(Asansol/ Chandernagar/ Howrah/ Jalpaiguri/ Berhampore/ Barrackpore/ Halisahar/ Habra/ Bhatpara/ Bankura/ Uttarpara/ Englishbazar/ Titagarh/ Rajpur-Sonarpur/ Mahestala/ Tamralipta/ Arambag/ Barasat/ North Dum Dum/ Jiaganj-Azimganj/ Balurghat/ Tarakeswar/ Madhyamgram/ Dum Dum/ Naihati/ Kaliyaganj/ Beldanga/ Islampur/Santipur)

Sub: Review meeting on Physical & Financial Progress of sanctioned Shelter units under the scheme Shelter for Urban Homeless (SUH) under DAY-NULM

Madam/Sir.

In partial modification of vide memo no. SUDA-23/2014(MPR1)/880(33) dated: 02.08.2018 of this office, I would like to inform you that the review meeting on physical & financial progress of sanctioned shelter units under the scheme Shelter for Urban Homeless (SUH) would be held on Conference Hall, SUDA on 09.08.2018 at 02.00 PM instead of 11.00 AM.

This is for your kind information.

Yours faithfully,

Director, SUDA

& Mission Director, WBSULM

Date: 06.08.2018

Memo No. 23/2014(MPR-1)/

Copy forwarded to

1. Jt. Secretary (S. Das), UD & MA Dept./ Additional Mission Director, WBSULM for information

2. Chief Engineer MED with the request to attend the meeting and to inform to the concerned Superintendent/ Executive Engineers of MED to attend the meeting.

3. Deputy Director, SUDA

3. SMM- S & S I, WBSULM, SUDA.

& Mission Director, WBSULM

দূরভাষ : ২৩৫৮ ৬৪০৩ / ৫৭৬৭, ফ্যাক্স : ২৩৫৮ ৫৮০০

Tel: 2358 6403/5767, Fax: 2358 5800, E-mail: wbsudadir@gmail.com



রাজ্য নগর উন্নয়ন সংস্থা



STATE URBAN DEVELOPMENT AGENCY

''ইলগাস ভবন''. এইচ-সি ব্রক. সেক্টর-৩, বিধাননগর, কলকাতা-৭০০ ১০৬, পশ্চিমবঙ্গ "ILGUS BHAVAN", H-C Block, Sector - III, Bidhannagar, Kolkata - 700 106, West Bengal

-	-		-	in.	
d		40	-	1	

SUDA- 23/2014(MPR-1) / 880 (33)

02.08.2018 তারিখ

From: Director, SUDA

& Mission Director, WBSULM

To: Commissioner/ Chairperson,

......Municipal Corporation/ Municipality

(Asansol/ Chandernagar/ Howrah/ Jalpaiguri/ Berhampore/ Barrackpore/ Halisahar/ Habra/ Bhatpara/ Bankura/ Uttarpara/ Englishbazar/ Titagarh/ Rajpur-Sonarpur/ Mahestala/ Tamralipta/ Arambag/ Barasat/ North Dum Dum/ Jiaganj-Azimganj/ Balurghat/ Tarakeswar/ Madhyamgram/ Dum Dum/ Naihati/ Kaliyaganj/ Betdanga/ Islampur / San hiper

Sub: Review meeting on Physical & Financial Progress of sanctioned Shelter units under the scheme Shelter for Urban Homeless (SUH) under DAY-NULM

Madam/Sir.

This is to inform you that, a review meeting on Physical & Financial Progress of sanctioned Shelter units under the scheme Shelter for Urban Homeless (SUH) under DAY-NULM will be held on 09.08.2018 at Conference Hall of SUDA at 11 AM onwards.

In this regard you are requested to attend the meeting along with the concerned municipal engineer with a present status report.

Yours faithfully.

Director, SUDA & Mission Director, WBSULM

Memo No. 23/2014(MPR-1)/880(33)/1(4

Copy forwarded to

at a since I

1. Jt. Secretary (S. Das), UD & MA Dept./ Additional Mission Director, WBSULM for information

2. Chief Engineer MED with the request to attend the meeting and to inform to the concerned Superintendent/ Executive Engineers of MED to attend the meeting.

3. Deputy Director, SUDA

3. SMM- S & S I, WBSULM, SUDA.

& Mission Director, WBSULM

Date: 02.08.2018





''ইলগাস ভবন''. এইচ-সি ব্লক. সেক্টর-৩, বিধাননগর, কলকাতা-৭০০ ১০৬, পশ্চিমবঙ্গ "ILGUS BHAVAN", H-C Block, Sector - III, Bidhannagar, Kolkata - 700 106, West Bengal

•	SUDA-	23/2014	(MPR-1)
0			

02.08.2018

তারিখ

ক্ৰামক নং From: Director, SUDA

& Mission Director, WBSULM

To: Commissioner/ Chairperson,

......Municipal Corporation/ Municipality

(Asansol/ Chandernagar/ Howrah/ Jalpaiguri/ Berhampore/ Barrackpore/ Halisahar/ Habra/ Bhatpara/ Bankura/ Uttarpara/ Englishbazar/ Titagarh/ Rajpur-Sonarpur/ Mahestala/ Tamralipta/ Arambag/ Barasat/ North Dum Dum/ Jiaganj-Azimganj/ Balurghat/ Tarakeswar/ Madhyamgram/ Dum Dum/ Naihati/ Kaliyaganj/ Be;danga/ Islampur /santleun)

Sub: Review meeting on Physical & Financial Progress of sanctioned Shelter units under the scheme Shelter for Urban Homeless (SUH) under DAY-NULM

Madam/Sir.

This is to inform you that, a review meeting on Physical & Financial Progress of sanctioned Shelter units under the scheme Shelter for Urban Homeless (SUH) under DAY-NULM will be held on 09.08.2018 at Conference Hall of SUDA at 11 AM onwards.

In this regard you are requested to attend the meeting along with the concerned municipal engineer with a present status report.

Yours faithfully,

Director, SUDA

& Mission Director, WBSULM

Memo No. 23/2014(MPR-1)/880(33)/(4)

Copy forwarded to

1. Jt. Secretary (S. Das), UD & MA Dept./ Additional Mission Director, WBSULM for information

2. Chief Engineer MED with the request to attend the meeting and to inform to the concerned Superintendent/ Executive Engineers of MED to attend the meeting.

3. Deputy Director, SUDA


3. SMM- S & S I, WBSULM, SUDA.


Date: 02.08.2018

& Mission Director, WBSULM


One day Capacity Building Training cum workshop for Operation & Maintenance of Shelter for Urban Homeless (SUH) for the staff & functionaries and ULB official

Total 43 shelters were sanctioned under the scheme Shelter for Urban Homeless (SUH) under DAY-NULM within the state of West Bengal. So far 8 shelters (Haldia, Krishnanagar, Nabadwip, Durgapur, Bongaon, Jalpaiguri, Coochbehar & Midnapore) are functional now within the state under DAY-NULM. Two shelter units are ready to functional & further two units will be functional soon. As per operational guidelines of SUH a Capacity Building Training cum workshop for Operation & Maintenance of Shelter for Urban Homeless (SUH) for the staff & functionaries and ULB official has been arranged by the SMMU, WBSULM, West Bengal on 20.07.2018. This training programme was facilitated by the Administrative Training Institute, Govt. of West Bengal. 30 participants from 12 different ULBs were participated in this training programme. A brief discussion on O & M and a hand holding training on shelter registers were provided in this training. Project Officer, Health of NUHM discussed about the Health & Hygiene of Shelters and its inmates. A detailed discussion was made in the training on Role of Shelter Management Agency and Role of Urban Local Bodies for Shelter for Urban Homeless. This training was very helpful for the participator for better management of SUH.

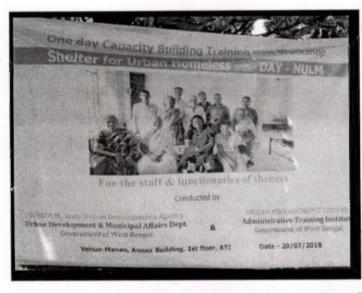

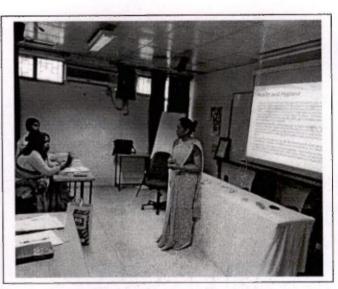



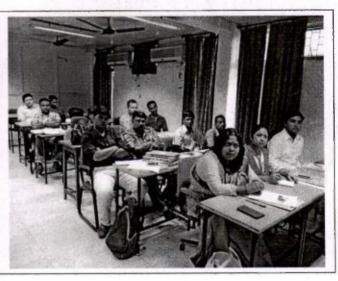



Director SULM <wbsulm@gmail.com>

URGENT-Information for fortnightly Newsletter of the Ministry

1 message

MAYANK MOHAN MISHRA <mayank.nulm@gmail.com>

Wed, Jul 25, 2018 at 11:59 AM

To: hudd-jk@nic.in, State Mission Manager <smmu.hudd@gmail.com>, MD MEPMA <mdmepma@apmepma.gov.in>, SULM CG <sulmchhattisgarh@gmail.com>, bihar_sulm@yahoo.com, SULM Bihar <daysulmbihar@gmail.com>, Sandesh Sail <gsuda.apo@gmail.com>, "DY DIRECTOR G.U.L.M." <nulm.gujarat@gmail.com>, suda haryana <suda.haryana@yahoo.co.in>, suda haryana <sudsh7@yahoo.co.in>, SULM Himachal Pradesh <himachal.sulm@gmail.com>, jharkhandsulm@gmail.com, KARNATAKA DAY NULM <karnataka.sulm@gmail.com>, NULM Kerala SMMU <nulmkerala@gmail.com>, Kerala SULM <kerala.sulm@gmail.com>, Madhya Pradesh SULM <madhyapradesh-sulm@mpurban.gov.in>, NULM - MAHARASHTRA <nulmmaharashtra@gmail.com>, suda odisha <sudaodisha1990@gmail.com>, Punjab PSULM <punjabsulm@gmail.com>, pddlb dlb <pdlsgrajasthan@gmail.com>, Tnulm Ho <tnulmho@gmail.com>, Mdmepma Telangana <mdmepma.ts@gmail.com>, Suda Uk <directorsudauk@gmail.com>, SMMU NULM <nulmsudauk@gmail.com>, SUDA NULM <nulmup@gmail.com>, Director SULM <wbsulm@gmail.com>, assam.sulm@gmail.com, Taring Darang <jdcumse@gmail.com>, muda imphal <mudamanipur@gmail.com>, Director MUDA <meghalaya.sulm@gmail.com>, Mizo SMMU NULM <mizonulm@gmail.com>, nagaland.sulm@gmail.com, DirectorUrban Tripura <directorurbantripura@gmail.com>, udhdsikkim udhd <udhdsikkim@gmail.com>, urban development <sikkim.sulm@gmail.com>, odfreeportblair@gmail.com, joint secretary <jspwdud@gmail.com>, NULM Chandigarh <nulm.chd@gmail.com>, Dnhpda Dnhpda <dnhpda@gmail.com>, atpdaman@gmail.com, dirlad.pon@nic.in, "Sh.J.P. Agrawal" <mc.samajiksuvidhasangam@gmail.com>, Anupama Pandey <spldoc.sss@gmail.com>, tncdwho@yahoo.co.in, Telangana Telangana <amd_mepma@telangana.gov.in>, Telangana Telangana <smc_susv_mepma@telangana.gov.in>, SUDA SUDA <apdsuda@gmail.com>, Sunil Kumar Mahajan <ce2.dusib@gmail.com>, puda.pon@nic.in, mizoramdaynulm@gmail.com, State Urban Development Agency Nagaland <suda_nagaland@yahoo.com>, NULM ASSAM <nulmassam@gmail.com>, SMMU Sikkim <smmu.sikkim@gmail.com>, NULM BIHAR <pmc.nulmbihar@visioneis.org>, Ahmed Tahreem <ahmed.tahreem@gmail.com>, haryana.sulm@yahoo.com Cc: Rakesh Ranjan <rakessh.nulm@gmail.com>, meghaiec.nulm@gmail.com, dir-nulm <dir-nulm@nic.in>, NIRAJ KUMAR <neeraj.kumar3@gov.in>, Sanjay Kumar <jsupa-mhupa@gov.in>

Dear All,

As required by the Mission Directorate, you are requested to share news/activities on SUSV and SUH component along with good photographs pertaining to functioning of shelters, street vendors survey, city vending plan, vendor market development, training and capacity building of street vendors, shelter inmates and concerned stakeholders, best practices, innovations etc under the Mission on regular basis for fortnightly Newsletter of the Ministry.

For any technical support pls. feel free to contact Mr. Rakesh Ranjan Barik, NMM-C&KM(Mobile no. 8800554039).

Information pertaining to above may be mailed on regular basis at meghaiec.nulm@gmail.com, daynulm.news@gmail.com, rakessh.nulm@gmail.com with copy to dir-nulm@nic.in, neeraj.kumar3@gov.in and mayank.nulm@gmail.com.

This may be accorded TOP PRIORITY,pls.

With Regards,

Mayank Mohan Mishra

With Regards.



Mayank Mohan Mishra

National Mission Manager, DAY-NULM
National Mission Management Unit (NMMU),
Ministry of Housing & Urban Affairs (MoHUA),
Room No- 646A, Nirman Bhawan,
Government Of India, New Delhi

Mobile: +91 7905760137

E.mail: mayank.nulm@gmail.com

Web- www.nulm.gov.in
http://mohua.gov.in/cms/contact.php

The information contained in this e-mail message, and any attachment thereto, is confidential and may not be disclosed without our express permission. If you are not the intended recipient or an employee or agent responsible for delivering this message to the intended recipient, you are hereby notified that you have received this message in error and that any review, dissemination, distribution or copying of this message, or any attachment thereto, in whole or in part, is strictly prohibited. If you have received this message in error, please immediately notify us by telephone or e-mail and delete the message and all of its attachments. Thank you. Every effort is made to keep our network free from viruses. You should, however, review this e-mail message, as well as any attachment thereto, for viruses. We take no responsibility and have no liability for any computer virus which may be transferred via this e-mail message.





"ইলগাস ভবন", এইচ-সি ব্লক, সেক্টর-৩, বিধাননগর, কলকাতা-৭০০ ১০৬, পশ্চিমবঙ্গ "ILGUS BHAVAN", H-C Block, Sector - III, Bidhannagar, Kolkata - 700 106, West Bengal

SUDA-23/2014 (MPR-1)/675

11.07.2018

ক্রমিক নং

From: Director, SUDA

& Mission Director, WBSULM

To: Chief Engineer,

Municipal Engineering Directorate

Sub: Review meeting for the scheme Shelter for Urban Homeless (SUH) under DAY-NULM

Sir,

This is to inform you that, a review meeting for Shelter for Urban Homeless (SUH) under DAY-NULM will be held on 17.07.2018 at Conference Hall of SUDA at 02.30 PM.

In this regard you are requested to kindly make it convenient to attend the review meeting.

Yours faithfully,

Director, SUDA & Mission Director, WBSULM

Pecalived withbut verification of the Chief Engineer, M. E. Dar Bikash Bhevan, (South Block) Lat Floor, Salt Leve. 401-41

Government of West Bengal
Department of Urban Development & Municipal Affairs
'Nagarayan, DF-8, Sector- I,
Salt Lake, Kolkata – 700 064

No.586-UDMA-13014(13)/5/2018-BDG-MA

Dated, Kolkata, the 7th day of May 2018

From : Special Secretary to the Government of West Bengal

To :The Director, State Urban Development Agency, ILGUS Bhavan, Block HA, Sector III, Salt Lake, Kolkata 700 106

Sub: Construction of 50 bedded 4 storied Shelter for Urban Homeless at Bhatpara Municipality - Acceptance of tender regarding

Sir,

With reference to above, I am directed to convey concurrence of acceptance of tender during 3rd Call by the qualified L1 bidder @ 2% above regarding ' Construction of 50 bedded 4 storied Shelter for Urban Homeless at Bhatpara Municipality under National Urban Livelihood mission (NULM)" in relaxation of normal tender rules subject to observance of other financial norms.

This is issued with the concurrence of Finance Department UO No. Group T/2018-2019/0100 dated 04.05.2018

Enclo. As Stated

Yours faithfully,

52/

Special Secretary to the Government of West Bengal

No.586/1UDMA-13014(13)/5/2018-BDG-MA

Dated, Kolkata, the 7th day of May 2018

Copy forwarded to Chairman, Bhatpara Municipality for information

Special Secretary



Government of West Bengal Department of Urban Development & Municipal Affairs 'Nagarayan, DF-8, Sector- I, Salt Lake, Kolkata – 700 064

No.586-UDMA-13014(13)/5/2018-BDG-MA

Dated, Kolkata, the 7th day of May 2018

From : Special Secretary to the Government of West Bengal

To :The Director, State Urban Development Agency,

ILGUS Bhavan, Block HA, Sector III, Salt Lake, Kolkata 700 106

Sub: Construction of 50 bedded 4 storied Shelter for Urban Homeless at Bhatpara Municipality - Acceptance of tender regarding

Sir,

With reference to above, I am directed to convey concurrence of acceptance of tender during 3rd Call by the qualified L1 bidder @ 2% above regarding ' Construction of 50 bedded 4 storied Shelter for Urban Homeless at Bhatpara Municipality under National Urban Livelihood mission (NULM)" in relaxation of normal tender rules subject to observance of other financial norms.

This is issued with the concurrence of Finance Department UO No. Group T/2018-2019/0100 dated 04.05.2018

Enclo. As Stated

Yours faithfully,

Special Secretary to the Government of West Bengal

No.586/1UDMA-13014(13)/5/2018-BDG-MA

Dated, Kolkata, the 7th day of May 2018

Copy forwarded to Chairman, Bhatpara Municipality for information

Special Secretary



Workflow Based File Tracking System Government of West Bengal Finance - Group T

File No: UDMA-13014(13)/5/2018-BDG-MA SEC-Dept. of UDMA

Subject: MA/P/C-10/3S-18/2018 Shelter for Urban Homeless under NULM - Acceptance of tender rate reg.

Department: Urban Development

Group T eOffice File No.41379

We may have no objection to accord concurrence to acceptance of tender during 3rd Call by the qualified L1 bidder @ 2% above regarding "Construction of 50 bedded 4 storied Shelter for Urban Homeless at Bhatpara Municipality under National Urban Livelihood Mission (NULM)" in relaxation of normal tender rules subject to observance of other financial norms.

28/04/2018 6:10 PM PAWAN KADYAN (JS(FIN))

03/05/2018 4:08 PM H.K. DWIVEDI (ACS(FIN))

UO NO : Group T/2018-2019/0100

UO Date: 04/05/2018

Section Officer, Finanace Department, Group-T

04/05/2018



Director SULM <wbsulm@gmail.com>

List of documents for preparation of DPRs

1 message

Director SULM <wbsulm@gmail.com>

To: Kandi Municipality <kandi@yahoo.com>, kandimunicipality@yahoo.com

Thu, Jun 14, 2018 at 10:50 AM

Please find the attachment



Land Papers(1)(1).docx



HOWRAH MUNICIPAL CORPORATION

Central Office: 4, Mahatma Gandhi Road, Howrah-711-101

Tele: (91-033) 2638-3211-13, Fax: (91-033) 2641-2214/5846/5218

Grievance redressal: +91-33-26370209

Memo No: 46/NULM/Dy.Commi/2018-19

Dated. 11/05/2018

To,
The Director,
State Urban Development Agency,
ILGUS Bhavan,
H-C Block, Sector-III,
Bidhannagar, Kolkata-700106

Sub: Report on present status of Construction of SUH

Sir,

This is to inform you that the civil construction of Shelter for Urban Homeless (SUH) at 9, Koi Pukur Lane, Howrah-711102, Ward No. 32, has been completed with inner works and other fitting works.

Although it was said the inauguration will be done by March, 2018 but due to revision of estimated cost of electrification work because of GST, the process got delayed. The previous work estimate (without GST) was vetted by KMDA and it was ready for E-tendering Process, however, after the advent of GST the whole process had to be repeated, as of now the E-tender has been published for further work.

The inauguration of the SUH will be done expectedly in the first week of June, 2018.

Deputy Commissioner, Howrah Municipal Corporation

Memo No: 46/NULM/Dy.Commi/2018-19/(2)

Dated, 11/05/2018

Copy forwarded for information, to ::

1. The Hon'ble Mayor, Howrah Municipal Corporation

2. CPO, NULM, and Chairman Borough-VI, Howrah Municipal Corporation

Deputy Commissioner, Howrah Municipal Corporation

Memo No: 46/NULM/Dy.Commi/2018-19/(5)

Dated. 11/05/2018

Copy forwarded for information, to ::

- 1. The Commissioner, Howrah Municipal Corporation
- 2. Sri Pijush Kanti Bhanja, Executive Engineer, HMC
- 3. EE, Planning & Development, Howrah Municipal Corporation
- 4. Dept. NULM,
- 5. Office copy.

Deputy Commissioner, Howrah Municipal Corporation

Mithen Ka (SPE) (PWO)

Office of the Municipal Councillors, Bhatpara

[Address: 1/1, West Ghoshpara Road, P.O. Kankinara, District: North 24 Parganas. PIN-743 126]

Ph: 2581-2082, 2581-9515, 2581-9514. Fax: 2581-1318. Email: bhat_09@yahoo.com & bhatparamunicipality@gmail.com

WORK ORDER

rom: -

Sri Arjun Singh (M.L.A)
Chairman
Bhatpara Municipality

To:-

Krishna Kawatch Developer, 16A Brabourne Road,(9th floor) Kolkata, 700001

lef. No: - S-43/PWD(Bldg)/DR-2/.................

Date: - .. 16.1.5./2018

Subject: Work Order for "Construction of 50 beded four storied shelter for urban homeless at Bhatpara, under NULM"

Ref.: e-NIO No:- MAD/ULB/BHATPARA/DR-2/3555, Dated-05/09/2017
Tender ID No.2017 MAD 127476 1

Schedule rates -1,03,99,038.00, 02% above which comes to total amount Rs.1,06,07,019.00

ir,

In reference to your tender for the above-mentioned work amounting to Rs.1,06,07,019.00 only has been accepted by the undersigned as mentioned in the tender on behalf of the Board Councilors of Bhatpara funicipality.

You are hereby directed to start the work immediately as per direction of Engineer-in-Charge. The date of ommencement of work shall be reckoned with effect from the date of this order and time of the whole work llotted to you shall be limited to 12 Month, there after this order will be cancelled without giving you farther utimation.

lo new items or substituted item of work or any excess quantity over tendered quantity or deviation from rawing/specification of work shall be undertaken without the prior permission of Engineer-in-Charge of this work nd subject to the approval of undersigned.

The name and address of your authorized representative who will be always available at the site of the work for eceiving working instruction, receiving materials if any attending to measurement etc. on your behalf must be

ubmitted to the Engineer-in-Charge as well as to the Municipality.

You shall also submit a programme of work in-conformity with the time of completion as per executed greement to the Engineer-in-Charge. The measurement will be taken by the officers of the Municipality from time the time which will be binding on you, if you or your authorized agent fails to attend during measurement then ction will be taken as per executed agreement and condition of contract. You shall have to maintain a site order ook at the site for receiving instruction from the supervising officers of the department from time to time. You nust maintain a stock register of materials and the daily receipts, use and balance of materials shall be shown there 1. This register shall be produced by the contractor to the Engineer-in-Charge or his representative whenever equired for verification of stock.

In case of delay of work to start the work at site without assigning any reason the Municipal Authority may

ake action as per provision of Law.

Yours faithfully,

-Aguary

Chairman,

Bhatpara Municipality



NOTE SHEET



It may be noted that total 35 shelters were Sanctimoed under the scheme Snelter for urban Horelass under num in allterent ULB. +THE most out of trese 35 smelters, & smelters are functionaly one snelton unit is completed and nest at the snettens are tamone stages of construction and tender process, It has boon observed from me report atallable of this affice trat progress of some snelters in different ULB are very short and process of Tendering is word in many ULBS. Et may be mentioned frat as per opposit suff the time period of completion of construction is one year from the commence ment of work Under these circumstaxes a mether neeting may be held to restirt the progress of the HORK of SUH, on 19.12.17 with ULBS where progress of work is very show. necessary logistic amangements may be made for this meeting on that day and arrangement of conference nort on 19.12.19

A draft letter may be sent to the UZBS for the vertilen meeting to placed the Draft for the same is submitted for your

kind perusal.





"**ইলগাস ভবন**", এইচ-সি ব্লক, সেক্টর-৩, বিধাননগর, কলকাতা-৭০০ ১০৬, পশ্চিমবঙ্গ "ILGUS BHAVAN", H-C Block, Sector - III, Bidhannagar, Kolkata - 700 106, West Bengal

ক্রমিক নং	তারিখ
SUDA-23/2014 (MPR)/ ///O	13.12.2017

From: Director, SUDA & Mission Director, WBSULM

To: Mayor,Municipal Corporation (Howrah/ Asansol/ Chandernagar)

Sub: Meeting to Review the Progress of Shelter for Urban Homeless under DAY-NULM

Sir.

This is to inform you that we are holding a meeting to review the progress of Shelters under the scheme of Shelter for Urban Homeless of NULM in your ULB as a matter of top priority. The details of the meeting are provided below:

1. Date: 19.12.2017 2. Time: 11.00 am

3. Venue: SUDA Conference Hall

In this regard, you are requested to send a competent Officer along with a Concerned Municipal Engineer to attend the meeting.

Yours faithfully,

Director & Mission Director, WBSULM

Date: 13.12.2017

Memo No.SUDA-23/2014(MPR)/

Copy forwarded for information to:

1. PS to Secretary UD & MA Dept., Govt of West Bengal for kind information

2. Chief Engineer, ME Directorate, Govt. of West Bengal.

Director, SUDA & Mission Director, WBSULM

List of ULBs to Attend the Meeting

SI	ULB	
No		
1	Berhampore	
2	Halisahar	
3	Barrackpore	
4	Bhatpara	
5	Bankura	
6	Uttarpara	
7	Titagarh	
8	Tamralipto	
9	North DumDum	
10	Barasat	
11	Jiaganj-Azimganj	
12	Santipur	
13	Balurghat	
14	Tarakeshwar	
15	Madhyamgram	
16	Mahestala	





"ইলগাস ভবন", এইচ-সি ব্লক, সেক্টর-৩, বিধাননগর, কলকাতা-৭০০ ১০৬, পশ্চিমবঙ্গ "ILGUS BHAVAN", H-C Block, Sector - III, Bidhannagar, Kolkata - 700 106, West Bengal

ক্রমিক নং	তারিখ
SUDA-23/2014 (MPR)/ ///O	13.12.2017
From: Director, SUDA &	
Mission Director, WBSULM	
To: Mayor,	
	Municipal Corporation
(Howrah/ Asansol/ Chandernagai	
Sub: Meeting to Review the Progr	ress of Shelter for Urban Homeless under DAY-NULM
Sir,	
This is to inform you that we ar	re holding a meeting to review the progress of Shelters under
the scheme of Shelter for Urban Ho	omeless of NULM in your ULB as a matter of top priority.
ment a sa .	1 1

Date: 19.12.2017
 Time: 11.00 am

3. Venue: SUDA Conference Hall

The details of the meeting are provided below:

In this regard, you are requested to send a competent Officer along with a Concerned Municipal Engineer to attend the meeting.

Yours faithfully,

Director, SUDA & Mission Director, WBSULM

Date: 13.12.2017

Memo No.SUDA-23/2014(MPR)/

Copy forwarded for information to:

1. PS to Secretary UD & MA Dept., Govt of West Bengal for kind information

2. Chief Engineer, ME Directorate, Govt. of West Bengal.

Director, SUDA & Mission Director, WBSULM

Tel: 2358 6403/5767, Fax: 2358 5800, E-mail: wbsudadir@gmail.com

List of ULBs to Attend the Meeting

SI No	ULB
1	Berhampore
2	Halisahar
3	Barrackpore
4	Bhatpara
5	Bankura
6	Uttarpara
7	Titagarh
8	Tamralipto
9	North DumDum
10	Barasat
11	Jiaganj-Azimganj
12	Santipur
13	Balurghat
14	Tarakeshwar
15	Madhyamgram
16	Mahestala

List of ULBs to Attend the Meeting

SI No	ULB
1	Berhampore
2	Halisahar
3	Barrackpore
4	Bhatpara
5	Bankura
6	Uttarpara
7	Titagarh
8	Tamralipto
9	North DumDum
10	Barasat
11	Jiaganj-Azimganj
12	Santipur
13	Balurghat
14	Tarakeshwar
15	Madhyamgram





"ইলগাস ভবন", এইচ-সি ব্লক, সেক্টর-৩, বিধাননগর, কলকাতা-৭০০ ১০৬, পশ্চিমবঙ্গ "ILGUS BHAVAN", H-C Block, Sector - III, Bidhannagar, Kolkata - 700 106, West Bengal

ক্রমিক নং SUDA-23/2014 (MPR)/ ///	1
-----------------------------------	---

তারিখ

From: Director, SUDA &

Mission Director, WBSULM

Sub: Meeting to Review the Progress of Shelter for Urban Homeless under DAY-NULM

Sir.

This is to inform you that we are holding a meeting to review the progress of Shelters under the scheme of Shelter for Urban Homeless (SUH) of NULM in your ULB as a matter of top priority. The details of the meeting are provided below:

Date: 19.12.2017
 Time: 11.00 am

3. Venue: SUDA Conference Hall

In this regard, you are requested to attend the aforesaid meeting along with the concerned Municipal Engineer.

Enclosed is the list of ULBs for the review meeting.

Enclosure: As Stated

Yours faithfully.

Director, SUDA

& Mission Director, WBSULM

Date: 13.12.2017

Memo No.SUDA-23/2014(MPR)/ /// (2)

Copy forwarded for information to:

1. PS to Secretary UD & MA Dept., Govt of West Bengal for kind information

2. Chief Engineer, ME Directorate, Govt. of West Bengal.

Director, SUDA & Mission Director, WBSULM

Tel: 2358 6403/5767, Fax: 2358 5800, E-mail: wbsudadir@gmail.com





''ইলগাস ভবন'', এইচ-সি ব্লক, সেক্টর-৩, বিধাননগর, কলকাতা-৭০০ ১০৬, পশ্চিমবঙ্গ "ILGUS BHAVAN", H-C Block, Sector - III, Bidhannagar, Kolkata - 700 106, West Bengal

ক্রমিক নং	তারিখ
SUDA-23/2014 (MPR)/	13.12.2017

From: Director, SUDA &

Mission Director, WBSULM

To:	Mayor,
	Municipal Corporation
	(Howrah/ Asansol/ Chandernagar)

Sub: Meeting to Review the Progress of Shelter for Urban Homeless under DAY-NULM

Sir,

This is to inform you that we are holding a meeting to review the progress of Shelters under the scheme of Shelter for Urban Homeless of NULM in your ULB as a matter of top priority. The details of the meeting are provided below:

1. Date: 19.12.2017 2. Time: 11.00 am

3. Venue: SUDA Conference Hall

In this regard, you are requested to send a competent Officer along with a Concerned Municipal Engineer to attend the meeting.

Yours faithfully,

Director, SUDA & Mission Director, WBSULM

Date: 13.12.2017

Memo No.SUDA-23/2014(MPR)/ / / (?)

Copy forwarded for information to:

1. PS to Secretary UD & MA Dept., Govt of West Bengal for kind information

2. Chief Engineer, ME Directorate, Govt. of West Bengal.

Director, SUDA & Mission Director, WBSULM



রাজ্য নগর উন্নয়ন সংস্থা



STATE URBAN DEVELOPMENT AGENCY

"ইলগাস ভবন", এইচ-সি ব্লক, সেক্টর-৩, বিধাননগর, কলকাতা-৭০০ ১০৬, পশ্চিমবঙ্গ "ILGUS BHAVAN", H-C Block, Sector - III, Bidhannagar, Kolkata - 700 106, West Bengal

ক্রমিক	न१	SUDA-23/2014 (MPR)/	r).	4	ı
		BUDA-23/2014 (MPR)/	I L'	Ŧ	ı

ভারিখ

13.12.2017

From: Director, SUDA &
Mission Director, WBSULM

To: Chairperson,

Sub: Meeting to Review the Progress of Shelter for Urban Homeless under DAY-NULM

Sir,

This is to inform you that we are holding a meeting to review the progress of Shelters under the scheme of Shelter for Urban Homeless (SUH) of NULM in your ULB as a matter of top priority. The details of the meeting are provided below:

1. Date: 19.12.2017

2. Time: 11.00 am

3. Venue: SUDA Conference Hall

In this regard, you are requested to attend the aforesaid meeting along with the concerned Municipal Engineer.

Enclosed is the list of ULBs for the review meeting.

Enclosure: As Stated

Yours faithfully,

Director, SUDA & Mission Director, WBSULM

Date: 13.12.2017

Memo No.SUDA-23/2014(MPR)/ 1111 (2)

Copy forwarded for information to:

1. PS to Secretary UD & MA Dept., Govt of West Bengal for kind information

2. Chief Engineer, ME Directorate, Govt. of West Bengal.

Director, SUDA & Mission Director, WBSULM

Tel: 2358 6403/5767, Fax: 2358 5800, E-mail: wbsudadir@gmail.com

File No. M-13/23/2017-UPA I SECTION-MHUPA(EFS-9026963)
Government of India
Ministry of Housing and Urban Affairs
(UPA-II Section)

Nirman Bhawan, New Delhi Dated: 01.11.2017

To

The Mission Director, DAY-NULM, All States/UTs

Subject:

Uploading of information on constitution of Project Sanction Committees at State Level, City Level Executive Committees and Shelter

Management Committees at the DAY-NULM portal -regarding.

Sir.

I am directed to refer to the above mentioned subject and to say that Hon'ble Supreme Court during its hearing on 13.10.2017 of the W.P. (C) 55 of 2003 with W.P. (C) 572 of 2003 in the Supreme Court of India in the matter of E.R Kumar & ANR Vs Union of India & others has directed to upload all the details of the Committee on the computer. Accordingly, this Ministry has made provision in the DAY-NULM portal to capture the information on constitution of Project Sanction Committees at State Level, City Level Executive Committees and Shelter Management Committees, and their meetings, at the following links in the DAY-NULM portal viz. www.nulm.gov.in

- i. Project Sanction Committee at State Level: under State/UT login, under add/edit all Committee under SUH tab.
- ii. Executive Committee at City Level: under ULB login, under Committee under SUH tab.
- iii. Shelter Management Committee: under State/UT login, under add/edit shelters profile under SUH.
- It is requested to ensure regular uploading of the information on the same on the above mentioned links as and when there is any material change in the status in each of above aspects.
- 3. Further, it is also requested that the particulars of all the inmates/beneficiaries of the Shelters functional under SUH component of DAY-NULM may also be computerised at the Shelter level.

Yours faithfully,

(Surender Kumar)

Under Secretary to the Government of India

Tele: 23061185

গ্রায়ন সংস্থা LOPMENT AGENCY



াননগর, কলকাতা-৭০০ ১০৬, পশ্চিমবঙ্গ

idhannagar, Kolkata - 700 106, West Bengal

তারিখ 18/12/17

of Tiffin Packets

No-M-13/23/2017-UPA-1/EFT-9026965

d Tea & Snacks as per prescribed rate at The detail is mentioned below;

a	Number of Tiffin Packets	Rate of Tea & Snacks	
		Rs.10+Rs.10	
	45	(Each 500ml	
		mineral Water	
		Bottle)	

e Patties, Cake, Chips, 1 Sweet). ontaining drinking water with dispenser day.

d for processing payment form SUDA as

somether government

Yours fait

Mission Director, WBSULM

Tel: 2358 6403/5767, Fax: 2358 5800, E-mail: wbsudadir@gmail.com

WEST BENGAL STATE URBAN LIVELIHOOD MISSION

(Under Municipal Affairs Department, Government of West Bengal)

"ইলগাস ভবন", এইচ-সি ব্লক, সেকটর-৩, বিধাননগর, কলকাতা ৭০০ ১০৬, পশ্চিমবঙ্গ।
"ILGUS BHAVAN", H-C Block, Sector-III, Bidhannagar, Kolkata 700 106, West Bengal.

SUDA-23/2014(MPR)/ 1017

Date: 28 /11/2017

Memorandum

Release of funds for Shelter for Urban Homeless under DAY-NULM

Funds are shown herein are being released electronically in favour of Durgapur MC of Shelter for Urban Homeless under DAY-NULM as final installment.

SL		Amount (Rs. In Lakh)		
NO.	Name of ULBs	Central Share	State Share	Total
1	2	3	4	5
1.	Durgapur MC	13.98	9.32	23.30

Finance Officer, SUDA

দুরভাষ: ২৩৫৮ ৬৪০৩/৬৪২১/৫৭৬৭, ফ্যান্স : ২৩৫৮৫৮০০

Tel: 2358-6403/6421/5767, Fax: 2358-5800, E-Mail: wbsulm@gmail.com

The release of funds subject to the following conditions-

- 1. The fund should be utilized only for the approved components of the Project and within ceiling limits of approved cost.
- 2. The execution of the Schemes should be strictly as per the Procedure laid down in Govt. Order No. 329/MA/C-10/3S-22/2013 Dated 04.05.2015 (Copy enclosed) for implementation of Shelters under NULM with MED as the Technical Support Agency.
- 3. Monthly report of Physical and Financial Progress should be sent to SUDA and MED by the $7^{\rm th}$ of the following month.
- 4. The amount released herein should be kept in the dedicated Bank Account for NULM since opened by the ULB.
- 5. A Subsidiary Cash Book should be maintained for keeping accounts (deposits and withdrawals) of funds.
- 6. Money receipt in Form 42 may be sent immediately after receiving the fund.
- 7. No fund should be utilized for any purpose other than for which the amount is released.
- 8. Utilisation certificate on achieving 70% plus expenditure of the amount released herein and earlier vide no. SUDA-23/2014/250 dt. 31.03.15 should be submitted in prescribed proforma duly authenticated by MED for release of subsequent installment.

Finance Officer, SUDA

SUDA- 23/2014 (MPN) / 1017-(115)
Copy for information to:

- 1. The Mayor Durgapur MC. He/she is requested to verify the respective Bank Account of the ULB in respect of NULM that the amount released in this Memorandum is duly credited. It may kindly be ensured that all money receipts against previous releases by SUDA have been submitted.
- 2. Secretary, UD&MA. Deptt, Govt. Of West Bengal.
- 3. Joint Secretary, UD&MA. Deptt, Govt. Of West Bengal.
- 4. Chief Engineer, M.E. Directorate.
- 5. Joint Director, SUDA.

Finance Officer, SUDA

Medhuman.

Government of West Bengal 03242-257-658 Office of the District Magistrate, Bankura bankuramunicipalaffairs@gmail.com Municipal Affairs Cell Memo no. 101 /M.A /Dated 25, 08, 2017 The Joint Secretary to the Government of West Bengal Deptt. of Urban Development & Municipal A frais Government of West Bengal,

'Nagarayan'. DF-8, Sector-I. Salt Lake. Kolkata - 700064.

Sub: Report regarding progress of Shelters under the scheme Shelter for Urban Homeless (SUH) under the Programme NULM in the ULBs.

Ref: Your Memo. No. Secy/UD&MA/2017/21 dated 06.07.2017

Sir.

To

With reference to above, this is for favour of your kind information that an amount of Rs.45.30 lakh has been sanctioned for construction of Shelter with in Bankura Municipality and a plot bearing no. 817(RS), Mouza Bankura, JL no. 211 has been identified for the construction of said Shelter with 50 Beded capacity. The Executive Engineer, M.E. Dte. Bankura Division has been authorized as a Executing Agency by the Bankura Municipality for implementation of the said project. The work yet to be started and expected to be completed by November. 2018 as stated by the Executive Agency.

A format report in this regard of the Chairman, Bankura Municipality is enclosed herewith and the work is being pursued in time to time.

Thanking you.

Enclo: As stated.

Yours faithfully

Additional District Magistrate (Dev)

Bankura. Dated 25/08/2017

Memo.No. 101 Copy forwarded to:

> 1. The Chairman, Bankura Municipality with the request to take effective action for immediate completion of this scheme. This has a reference to his memo. no. 1335/VIII-14 dated 26.07.2017.

2. C.A. to District Magistrate, Bankura with the request to place it before the District Magistrate, Bankura.

> Additional District Magistrate (Dev) Bankura.

FORMAT FOR MONTHLY STATUS OF SUH, A COMPONENT UNDER DAY-NULM

			_		
	1			1	
		V 41.			
		1.11	4		
		12.4	100		
	ĺ	~			
			1		
		110			
	ľ	0.0			
		CUE N			
			-		
-			-		

25th day of July 2017
Malus as on:-

1 4	
Physical progress achieved in details (Photograph anneved if applicable)	, (5) a
neat period	9
Fred Total	35 30
A special at a second completion (Total)	styli day of Novembe 2018
Other Cost of Oa vs. Cost of Control Date of Control of	Yet to State
Preject (ext	27.00
Cost per	(7)
(Cost of Cost of Cost) (Terestee A Cost per Cost	7.
Civit & The trification with Science plumbing cost (With 3%,	N 7 (46)
Particular National N	27% day of Day, navy Votts vide Wener No. 696 MAP P. 10° IG-3
Shaller (Beds)	An Rest
of the Shaffer	Lay Onti Pierry, Motiva Mankura, I No. 911 Bankura

CHARMAN

CHARMAN

BANKURA MUNICIPALITY

Charman

Charman

GOVERNMENT OF WEST BENGAL OFFICE OF THE CHIEF ENGINEER

Municipal Engineering Directorate

Bikash Bhawan, South Block (1st Floor) Salt Lake, Kolkata - 700091. Phone No: (033)2337-1331/(033)2358-3347 \ Fax: (033) 2337-5474

E-mail: ce medte @ yahoo.com

No. ME/

The Chief Engineer, From :

Municipal Engineering Directorate,

Bikash Bhavan, Salt Lake,

Kolkata - 700091.

To

The Superintending Engineer,

East Circle, M.E.Dte.

Dated:



Sub: Shelter for Homeless under NULM within Bhatpara Municipality

WOWN 05 19 Ref: Memo No. ME/SE(E)/513/1S-572/2015 dt. 29.11.2017 You are not at all vividly following the directions, as conveyed in earlier times towards monitoring all tenders related to MED under your jurisdiction as well forwarding tender documents for placement to Technical Committee etc.

Now in this case the following documents have not been attached with the documents sent to this office from your end, which otherwise lapse a lot of time.

- Revised format of Annexure-I as per FD Memo No. 4378F(Y) dt. 13.7.17.
- 2. News paper cuttings for 1st and 2nd call.

An immediate action is desired.

SIX

Chief Engineer, MED

Copy forwarded for information and necessary action to:

1. The Mission Director, WBSULM & Director, SUDA

2. The Chairman, Bhatpara Municipality

3. The Executive Engineer, North 24 Parganas Division, M.E.Dte.

Chief Engineer, MED

ng, NULM, Bhatpara, SE(E)...30.11.17.docx_J



Office of the Municipal Councillors of Bankura

Office: 250367.250344.254804 Fax: 03242-259269 / 250367

Resi: 03242-253338, Mobile: 09434115191

E-mail: bankuramunicipality@rediffmail.com

:senguptamahaprasadcm@yahoo.in

Website: WWW.bankuramunicipality.org.

Dated, Bankura:

From: Sri Mahaprasad Sengupta

Chairman, Bankura Municipality

Memo. No.

Kenduadihi. Bankura.

The Executive Engineer, M.E.Dte., Bankura Division.

To

/VIII-14 (NULM)

/2017.

Ref:- Your office Memo No. MED/BKU/517/NULM-1/2015, dated 10/11/2017, MED/BKU/440/NULM-1/2015, dated 22/09/2017, & the last meeting on dated 09/11/2017 at the Chairman's Chamber, Bankura Municipality

Sub:- Construction of 50 Bedded five storied Building under NULM within jurisdiction of Bankura Municipality.

Sir,

With the above reference this is also to inform you that after several correspondences with the Agency (Kartick Sen) he does not agree to start the work of NULM Project at present situation and prayer for showing the revised project value with a G.S.T. rate, on dated 09/11/2017. The copy of the prayer has been enclosed herewith. It also to inform you that the different local situation and climatic condition the project site was not possible to handed over in due time before implementation of G.S.T. form 1st July 2017 although the work order had been issued him on dated 25/05/2017.

In this circumstance this is forwarded for your necessary technical opinion. Your early action may solicit.

Enclo. As stated.

Thanking you.

Chairman Bankura Municipality

Memo no:- 2575 (3) /VIII-14(NULM), Dated:- 13/11/17.

Copy forwarded for information and take necessary action from your end.

The Director, SUDA, ILGUS BHAVAN, HC Block, Sector - III, Bidhannagar, Kolkata 700106. West Bengal.

2. The Joint Secretary, Department of UD & MA, Government of West Bengal, Poura Prasasan Bhavan, Block DD-1, Sector-1, Salt Lake City, Bidhan Nagar, Kolkata - 700064

3. The Superintending Engineer (South), Municipal Engineering Directorate (South Circle), Kousallya, P.O. Khargpur, Dist:- Paschim Midnapur.

Bankura Municipality

Chairman Bankura Municipality

9363/M. D1.04.11.17

KARTICK SEN

Govt. Contractor & General Order Supplier

Mobile: 9232694223 Emai: kartick37@yahoo.com

mai:: karticks/@yanoo.com karticksen75@gmail.com

RAJGRAM

BANKURA (W.B.)

Dure 09-11-2017

40

The Chairman Sankura Municipality Bankura

Ref. No.

<u>Sub:-</u> Acceptance cum work order for construction of 50 bedded five storied building and ancillary work for shelter for urban homeless within jurisdiction of Bankura municipality under NULM. Layout plos no.817(R.S), mouza-Bankura, Ji no.211 Bankura.

Ref:- NIT NO.WBMAD/CM/BM/24/NULM/2016-17 of office memo no. 3106/VIII-14 Dated-21/01/2017 Ref:-Your latter of acceptance cum work order no.618/VIII-14 Dated-22/05/2017

Sir

I would like to inform you that the work order for the above mentioned work. Thought issued 22/05/2017 but could not taken up for want of clear site free form encroachment not made available to me.

I must mention that the estimated amount put to tender being Rs. 1,84,07,355.00 was made basing on 3% value but the Govt. of India introduced G.S.T. form 1st July 2017. So as per pre G.S.T. contract agreement which was exclusive of VAT need to be revised of contractual value in the contact due to impact of change in tax rate.

So I would request you to kindly revise the project value with a G.S.T. rate of 6% CGST and 6% SGST excluding vat 3%. As otherwise it would adversely affected to the agency. Kindly decide and communicate your value decision earliest to help me to commence the work.

Thanking You

Yours Faithfully

Karter X 8m

Copy Forwarded to information

- 1. The Superintendent Engineer M.E.Dte. Khargapur
- 2. Executive Engineer, M.E.Dte. Bankura



Office of the Municipal Councillors of Bankura

Office: 250367,250344,254804 Fax: 03242-259269 / 250367

Resi: 03242-253338, Mobile: 09434115191

E-mail: bankuramunicipality@rediffmail.com :senguptamahaprasadcm@yahoo.in

Website: WWW.bankuramunicipality.org.

From: Sri Mahaprasad Sengupta

Chairman, Bankura Municipality

Memo, No.

/VIII-14 (NUCM)

Dated, Bankura:

2017.

The Executive Engineer, M.E.Dte., Bankura Division,

Kenduadihi. Bankura.

Ref:- Your office Memo No. MED/BKU/517/NULM-1/2015, dated 10/11/2017, MED/BKU/440/NULM-1/2015, dated 22/09/2017, & the last meeting on dated 09/11/2017 at the Chairman's Chamber, Bankura Municipality

Sub:- Construction of 50 Bedded five storied Building under NULM within jurisdiction of Bankura Municipality.

Sir.

With the above reference this is also to inform you that after several correspondences with the Agency (Kartick Sen) he does not agree to start the work of NULM Project at present situation and prayer for showing the revised project value with a G.S.T. rate, on dated 09/11/2017. The copy of the prayer has been enclosed herewith. It also to inform you that the different local situation and climatic condition the project site was not possible to handed over in due time before implementation of G.S.T. form 1st July 2017 although the work order had been issued him on dated 25/05/2017.

In this circumstance this is forwarded for your necessary technical opinion. Your early action may solicit.

Enclo. As stated.

Thanking you.

Chairman Bankura Municipality

Memo no:- 2575 (3) /VIII-14(NULM), Dated:- 12 / 11 /17. Copy forwarded for information and take necessary action from your end.

1. The Director, SUDA, ILGUS BHAVAN, HC Block, Sector – III, Bidhannagar, Kolkata 700106, West Bengal. The Joint Secretary, Department of UD & MA, Government of West Bengal, Poura Prasasan Bhavan, Block DD-1, Sector-1, Salt Lake City, Bidhan Nagar, Kolkata - 700064

3. The Superintending Engineer (South), Municipal Engineering Directorate (South Circle), Kousallya, P.O.

Khargpur, Dist:- Paschim Midnapur.

Chairman Bankura Municipality

Bankura Municipality

Sylph Southor SUDA

9363/M. DI. C4.11.14

KARTICK SEN

Govt Contractor & General Order Supplier

RAJGRAM BANKURA (W.B.) Mobile: 9232694223

Email: kartick37@yahoo.com karticksen75@gmail.com

Dure 09-11-2017

10

The Chairman
Sankura Municipality
Bankura

Ref. No.

<u>Sub:-</u> Acceptance cum work order for construction of 50 bedded five storied building and ancillary work for sheiter for urban homeless within jurisdiction of Bankura municipality under NULM. Layout plot no.817(R.S), mouza-Bankura, Jl no.211 Bankura.

Ref:- NIT NO.WBMAD/CM/BM/24/NULM/2016-17 of office memo no. 3106/VIII-14 Dated-21/01/2017 Ref:-Your latter of acceptance cum work order no.618/VIII-14 Dated-22/05/2017

Sir

I would like to inform you that the work order for the above mentioned work. Thought issued 22/05/2017 but could not taken up for want of clear site free form encroachment not made available to me. I must mention that the estimated amount put to tender being Rs. 1,84,07,355.00 was made basing on 3% vat. But the Govt. of India introduced G.S.T. form 1st July 2017. So as per pre G.S.T. contract agreement which was exclusive of VAT need to be revised of contractual value in the contact due to impact of change in tax rate.

So I would request you to kindly revise the project value with a G.S.T. rate of 6% CGST and 6% SGST excluding vat 3%. As otherwise it would adversely affected to the agency. Kindly decide and communicate your value decision earliest to help me to commence the work.

Thanking You

Yours Faithfully

Karta-X8-7

Copy Forwarded to information

- 1. The Superintendent Engineer M.E.Dte. Khargapur
- 2. Executive Engineer, M.E.Dte. Bankura

Topard Bry (1)



OFFICE OF THE MUNICIPAL COUNCILLORS

ENGLISHBAZAR MUNICIPALITY, MALDA

- Netaji Subhas Road, Malda, Pin -732101 -

E-mail: englishbazarmunicipality@gmail.com

website: www.englishbazarmunicipality.com

Office:(EPABX): 03512-252029

Fax: 03512-253329

Мето No. --

1499 XIVS1(4) 17

Date

25.08.17

The Director SUDA &

Mission Director, WBSULM ILGUS, Bhavan, H.C block, Sector-3 Salt Lake, Bidhannagar, Kolkata-106

meless under DAY-NUIM

Sub: Monthly Status Report of Construction of Shelter for Urban Homeless under DAY-NULM project of Englishbazar Municipality, Malda

Ref:- SUDA-23/2014(MPR)/603 (2)

Date-17.08.2017

With reference to the memo no stated above in connection with the Status Report of Construction of Shelter for Urban Homeless under DAY-NULM project of this municipality, this is to inform you that the Work Order has been issued on 09.08.2017 (copy enclosed) and the work is yet to be started. The details of the progress report is enclosed (Specific Format) for your ready reference.

This is for your information & taking necessary action.

Enclo: As Stated

Chairman

will--- G.

Englishbazar Municipality, Malda


Memo no..

Copy forwarded for information & necessary action:

- 1. Additional District Magistrate (Gen), Malda
- 2. Chairman-In-Council, NULM, Englisbazar Municipality, Malda
- 3. Executive Officer & CPO (NULM) Englishbazar Municipality, Malda
- 4. Manager-S.D.I, Englishbazar Municipality, malda
- 5. SAE-1, Englishbazar Municipality, malda
- 6. APO (NULM), Englihbazar Municipality, Malda
- 7. Office copy, Englishbazar Municipality, Malda

Chairman

Englishbazar Municipality, Malda



Englishbazar Municipality

Name of ULB	f ULB	Englishbaza	Englishbazar Municipality						Status	Status as on	25-08-2017
											Amount Rs. In Lakhs
Location of the Shelter	Capacity of each shelter (beds)	Date of approval by PSC	Civil & Electrification with Sanitary Plumbing Cost (With 3% contigency)(a)	Other Costs(Cost of O&M Cost Total Project Commence Utensils & per Year Cost (a+b) ment of Furniture) (b) Date of Commence Work	O&M Cost per Year	Total Project Cost (a+b)	Date of Commence ment of work	Expected date of completion	Fund Received (Total)	Total Expenditure Incurred	Total Physical progress achieved in Expenditure details (Photograph annexed if Incurred needed)
R.K Mission Ghat Road, EBM	50	04.10.2016	102.09	8.71	30.1	118.39	09.08.2017 30.12.2018	30.12.2018	46.02	NIL	Work order issued. Civil Construction ● yet to be started

Chairman

0

Englishbazar Municipality



OFFICE OF THE MUNICIPAL COUNCILLORS

MULH

ENGLISHBAZAR MUNICIPALITY, MALDA.

Netaii Subhas Ro	ad, Malda. Pin-732101
------------------	-----------------------

E-mail :englishbazarmunicipality@gmail.com[]Website : www.englishbazarmunicipality.com[]Office :(EPABX):03512-252029 Fax :03512-25339

Memo No.....

Date

From: The Chairman,

Englishbazar Municipality, Malda.

To:

BONI ENGINEERING

Thakurbari Lane, Mokdumpur,

Maida.

Sub: Work Order for the work of "Proposed (G+3) Storied Building of Shelter For Urban Homeless Under N.U.L.M Project Within English Buzar Municipality, Dist- Malda. (2nd Call)"

Ref: (i) Letter Of Acceptance vide Memo No. 1127/IV-2/17-18 dated 01.08.2017

(ii) Minutes of the 76th Meeting of Technical Committee under SUDA held on 18.07.2017

(iii) NIeT No. MAD/ULB/EBM/NULM/01/16-17(2nd Call) vide memo no. 205/IV-2/17-18 dated 28.04.17

Amount put to Tender: Rs 1,07,56,440.00 -

Bid Amount

: Rs 97,88,361.05 -(9.00% less on amount put to tender)

Accepted Amount

: Rs 97.88.361.05 - (Rupees Ninety Seven Lakh Eighty Eight Thousand Three Hundred Sixty One

Rupees & Five Paise only)

I on behalf of Board of Councillors, Englishbazar Municipality do hereby inform you that you are requested to start the work under reference as per your execution of formal agreement with the undersigned. Now you are requested to meet the Executive Engineer, Malda Division, M.E.Dte., Malda to submit a programme of works and also start the work immediately in order to successful completion of work within the stipulated time failing which action will be taken as per Tender Agreement.

You are also requested to complete the said work within 365 days from the date of issue of this letter and also note that all payment will be made after entire satisfaction of the Municipal Authority and the bill has to be recommended and certified by the Executive Engineer, M.E.Dte., Malda Division, Malda.

Sd/-

Chairman

Englishbazar Municipality, Malda

Memo No

1178 m. 2/17/18/(9)

Date: 09:08-2017

Copy forwarded for information to:

- 1. The Secretary, U.D & M.A Department, Govt. Of West Bengal.
- 2. The District Magistrate, Malda.
- 3. The Chief Engineer, M.E.Dte, Bikash Bhawan, Salt Lake City, Kolkata-91
- 4. The Vice-Chairman, Englishbazar Municipality, Malda.
- 5. The C.I.C. Project, Englishbazar Municipality, Malda.
- 6. The Superintending Engineer, Central Circle, M.E.Dte, N.S Road, Malda.
- 7. The Executive Engineer, Malda Division, M.E.Dte, Atul Market, Malda.
- The Junior Engineer-I, Englishbazar Municipality, Malda.
- 9. The Accountant, Englishbazar Municipality, Malda.

Chairman

Englishbazar Municipality, Malda Nihar Ranjan Ghosh CHAIRMAN

English Buzar Municipality, Makta





রাজ্য নগর উন্নয়ন সংস্থা



STATE URBAN DEVELOPMENT AGENCY

"**ইলগাস ভবন**", এইচ-সি ব্রক, সেক্টর-৩, বিধাননগর, কলকাতা-৭০০ ১০৬, পশ্চিমবঙ্গ "ILGUS BHAVAN", H-C Block, Sector - III, Bidhannagar, Kolkata - 700 106, West Bengal

SUDA-23/2014(MPR)/98	SUD.	A-23	/201	4(M)	PR)/	9	8	3
----------------------	------	------	------	------	------	---	---	---

23.11.2017

তারিখ

From: Director, SUDA

To : The Manager,

State Bank of India.

Salt Lake City, Kolkata - 700 091.

Sub: Electronic Transfer of Fund debiting this office Current Account No. 34061121921.

Construction of Shelter for Urban Homeless under NULM

Sir.

You are requested to kindly arrange for electronic transfer of funds as per details given below debiting the amounts from this office Current Account No. 34061121921 lying with your branch in respect of Construction of Shelter for Urban Homeless as final instalment under DAY-NULM.

Sl. No.	Name of Payee	Amount (In Rs.)	Payees' Bank Details
01	Durgapur Municipal Corporation	23,30,000.00	Allahabad Bank, City Centre Branch, A/C No. 50310508645, IFS Code. ALLA0211764
	TOTAL	23,30,000.00	

(Rupees Twenty three lakh thirty thousand only)

(Md Asif Sardar) Finance Officer SUDA

(Amalendu Sekhar Naskar) Addl. Director & FA

SUDA Jedhuston 20 17.

দূরভাষ ঃ ২৩৫৮ ৬৪০৩ / ৫৭৬৭, ফ্যাক্স ঃ ২৩৫৮ ৫৮০০

Tel: 2358 6403/5767, Fax: 2358 5800. E-mail: wbsudadir@gmail.com

Account Section: 2358 6408



রাজ্য নগর উন্নয়ন সংস্থা



STATE URBAN DEVELOPMENT AGENCY

"ইলগাস ভবন", এইচ-সি ব্লক, সেক্টর-৩, বিধাননগর, কলকাতা-৭০০ ১০৬, পশ্চিমবঙ্গ "ILGUS BHAVAN", H-C Block, Sector - III, Bidhannagar, Kolkata - 700 106, West Bengal

SUDA-23	/2014	(MPR)/	9	8	3

23.11.2017

তারিখ

From: Director, SUDA

To: The Manager,

State Bank of India,

Salt Lake City, Kolkata - 700 091.

Sub: Electronic Transfer of Fund debiting this office Current Account No. 34061121921.

Construction of Shelter for Urban Homeless under NULM

Sir.

You are requested to kindly arrange for electronic transfer of funds as per details given below debiting the amounts from this office Current Account No. 34061121921 lying with your branch in respect of Construction of Shelter for Urban Homeless as final instalment under DAY-NULM.

SI. No.	Name of Payee	Amount (In Rs.)	Payees' Bank Details
01	Durgapur Municipal Corporation	23,30,000.00	Allahabad Bank, City Centre Branch, A/C No. 50310508645, IFS Code. ALLA0211764
	TOTAL	23,30,000.00	

(Rupees Twenty three lakh thirty thousand only)

(Md Asif Sardar) Finance Officer SUDA

(Amalendu Sekhar Naskar) Addl. Director & FA

Broke

SUDA Sedhuman.

দ্রভাষ ঃ ২৩৫৮ ৬৪০৩ / ৫৭৬৭, ফ্যাক্স ঃ ২৩৫৮ ৫৮০০

Tel: 2358 6403/5767, Fax: 2358 5800, E-mail: wbsudadir@gmail.com

Account Section: 2358 6408



DURGAPUR MUNICIPAL CORPORATION

CITY CENTRE, DURGAPUR - 713216, DIST.- BURDWAN

EPABX \iff (0343) 2545842, 2546994, 2546107 * Mayor : 2545828 * Fax No. : 254-6472 Website : durgapurmunicipalcorporation.org * E-mail : durgapurcorporation@gmail.com

Ref. No. DMC / NULM /2008

Date 18.9.17

From

:The Commissioner

Durgapur Municipal Corporation

To

: The Director

State Urban Development Agency,
'ILGUS BHAVAN', H-C Block, Sector-III

Bidhannagar, Kolkata-106

Sub:- Utilization Certificate of FORM GRF 19-A for Shelter for Urban Homeless

Sir.

With reference to the above, I am hereby submitting the utilization certificate for Shelter for Urban Homeless in FORM GRF 19-A form of utilization certificate.

Thanking you.

Yours faithfully.

Commissioner

Durgapur Municipal Corporation

18/19/17

Encl: As stated above

FORM GFR 19-A (See Rule 212(1))

FORM OF UTILISATION CERTIFICATE

SI. No.	Letter No. and Date	Amount (Rs.)
1.	SUDA-23/2014/1258 DT. 21.09.2015	4799000.00
2.	SUDA-23/2014/405 dt. 25/05/2017	4527000.00
	Total	9326000.00

certified that out of Rs 9326000.00 Of Grant-in-aid sanctioned during the year 2015-2016 & 2017-2018 in favour of Durgapur Municipal Corporation under this Ministry/Department letter no. given in the margin and Rs NIL on account of unspent balance of the previous, a sum of Rs. 7932627.00 has been utilized for the purpose of expenditure of Shelter for Urban Homeless People for which it was sanctioned and that the balance of Rs1393373.00 remaining unutilized.

Certified that I have satisfied myself that the conditions on which the grant-inaid was sanctioned have been duly/are being fulfilled and that I have exercised the following check to see that money was actually utilized for the purpose for which it was sanctioned.

Kinds of checks exercised

01.V.N 001329 dt.31/08/16 Rs.140000.00

02. V.N 001521 dt. 08/09/16 Rs. 1563440.00

03. V.N 002149 dt. 28/11/16 Rs. 2758841.00

04. V.N 001236 dt. 27/06/17 Rs.2599846.00

05. V.N. 001782 dt.28/08/17 Rs .458000.00

06. V.N. 001783 dt. 28/08/17 Rs. 412500.00

Total

Rs.7932627.00

Finance Officer

Durgapur Municipal Corporation

Signature

Designation :

Date

Commissioner

Ourgapur Municipal Corporation

Accountant, NULM Durgopur Municipal Corporation

Prepared by Aft Ain

ASSISTANT ENGINEER
ASANSOL DIVISION, M. E. DTE

GOVT, OF W. B

Asansol Division

Municipal Engineering Directors

Govl. Of West Bengal

Minutes of the Fourth Meeting of Project Sanction Committee (PSC) under the scheme of Shelter for Urban Homeless (SUH) under NULM held on 31.07.2015 at Writers' Buildings, Kolkata – 700 001

Member Present:

1.	Sri B. P. Gopalika, IAS	Chairman
	Principal Secretary, M. A. Department,	
	Government of West Bengal	
2.	Sri M. Chatterjee	Member
	Joint Secretary, M. A. Department,	
	Government of West Bengal	28
3.	Sri A. Das	Member
	Chief Engineer, M. E. Dte.,	
	Government of West Bengal	
4.	Sri S. Saha	Member
	Regional Chief, HUDCO, Kolkata	
5.	Sri M. N. Pradhan, IAS	Member, Conveno
	Director, SUDA	

Others present:

Sri D. Chakraborty
 Dy. G. M. (Projects),
 HUDCO, Kolkata

Sri S. K. Mukherjee Technical Adviser, SUDA

3. Sri B. Das TUO, SUDA

Sri S. BanerjeeAE, MED

Sri B. P. Gopalika was in the chair.

Agenda 1. Confirmation of the minutes of the Third Meeting of the Project Sanction Committee held on 19.06.2015

The minutes of the Third Meeting of the Project Sanction Committee held on 19.06.2015 copies of which were sent to all concerned were confirmed.

Agenda2. Approval of DPRs of one shelter unit each in Jalpaiguri Municipality and Coochbehar Municipality

Jalpaiguri Municipality

The DPR for setting up of a shelter at Racecourse para, Ward No.10 with a capacity of 50 beds was approved at an estimated cost of Rs.122.02lakh (including 3% DPR preparation cost of Rs.3.45lakh) subject to furnishing a declaration from the Municipality that the land is free of encroachment and under sole ownership of the Municipality, to SUDA and thereafter SUDA will process release of funds as per guidelines.

The annual O & M cost is Rs. 6.02 lakh

Coochbehar Municipality

The DPR for setting up of a shelter at Santiban, Ward No.10 with a capacity of 50 beds was approved at an estimated cost of Rs.123.02lakh (including 3% DPR preparation cost of Rs.3.48lakh). SUDA is directed by the Committee to process release of funds as per guidelines.

The annual O & M cost is Rs. 6.02 lakh

Agenda Miscellaneous 1. Approval of DPR of one shelter unit in Berhampore Municipality

Berhampore Municipality

The DPR for setting up of a shelter at Saidabad Mouza with a capacity of 50 beds was approved at an estimated cost of Rs.122.89lakh (including 3% DPR preparation cost of Rs.3.48lakh) subject to furnishing a declaration from the Municipality that the land is free of encroachment and under sole ownership of the Municipality, to SUDA and thereafter SUDA will process release of funds as per guidelines.

The annual O & M cost is Rs. 6.02 lakh

Agenda Miscellaneous 2. Approval of DPR of one shelter unit in Durgapur Municipal Corporation

The matter was considered in the 3rd meeting of Project Sanction Committee and in the absence of actual transfer of the plot of land in favour of Durgapur Municipal Corporation, decision was deferred.

The Committee in the present meeting considered the No Objection Certificate of Asansol Durgapur Development Authority for setting up of a shelter vide their memo no.ADDA/DGP/PC-410/2014-15/784 dt.19.07.2015 and decided that in consideration of the No Objection Certificate the DPR may be approved

Accordingly, the DPR for setting up of a shelter at Muchipara, Bidhannagar with a capacity of 50 beds was approved at an estimated cost of Rs.119.95lakh (including 3% DPR preparation cost of Rs.3.39lakh) subject to furnishing a declaration from the Municipality that the land is free of encroachment, to SUDA and thereafter SUDA will process release of funds as per guidelines.

The annual O & M cost is Rs. 6.02 lakh

Meeting ended with a vote of thanks to and from the chair.

(B. P. Gopalika)
Principal Secretary
Municipal Affairs Department
Government of West Bengal

& Chairman, Project Sanction Committee

EXECUTIVE SUMMERY

Project Details

1 State

2 City

3 Project Name

Durgapur

Project Cost Central Share

(Rs. In Lacs) (Rs. In Lacs) (Rs. In Lacs)

Shelter for Urban Homeless of Durgapur under NULM 150.05 112.46

West Bengal

State Share

37.59

7 SOR Adopted

PWD (WB) SoR w.e.f. 1.7.14

Project Contributions (Physical + Financial) (Rs. In lacs)

130		BALL SERVICE		1462 5 7 7 7	Bull State State St	HOAS STORES	RETURNS VI	Towns and
Si No.	Scheme Component	Quantity	Unit	Rate (in Rs./unit)	Proposed project cost (in lakh)	Appraised Project Cost (in lakh)	Central Share	State Gov Share
1	Construction of 50 beded four storied Shelter including Sanitary Plumbing and internal Elecrification.	1	No.	10355564.00	103.56	103.56	77.67	25.89
2	Cost for furniture and Utensils	1	No.	870500.00	8.71	8.71	6.53	2.18
3	Service Concections (WBSEDCL)	1	LS	50000.00	0.50	0.50	0.38	0.13
4	Fire fighting arrangement	1	LS	40000.00	0.40	0.40	0.30	0.10
	Total	Cost	7900	A COMPANY	113.16	113.16	84.87	28.29
	ation and maintenance cost							
	O & M Cost for maintenance of two shelter for five year	5	Yns	602000.00	30.10	30.10	22.50	7,60
ther	Cost							
1	DPR Preparation, project management, supervision & Quality contro!	% total cost		3%	3.39	3.39	2.55	0.85
2	Contingency	% total cost		3%	3.39	3.39	2.55	0.85
2000				rand Total =	150.05	150.05	112.46	37.59

Assistant Engineer Durgapur Municipal Corporation

Durgapur Municipal Corporation

Status Report of SUH, a component under DAY-NULM

2 5 OCT 2017

		was at		New (Constru	etion			- 40	100	
SI No.	Name of ULB	Location of the Shelter	Capacity of each	Date of approval	Total Project	Date of Commen completi	Tentative time of	Fund Received	Total expendit	Physical progress	Remarks
1	Howrab	38 COWIES GHAT ROAD, BOROUGH- IV, WARD NO. 36, Dist- Howrah	50	18.03.2015	120.3		FY 2018-19	46.72		0	Population site change(relevan documents are n submitted by UL
					amantra)	reign begreit bis					
3	Berhampore	WARD NO. 05, J.L. NO. 100, PLOT NO. 1560/3415, 1561, 1561/3456, 1561/3987, Dist- Berhampore	50	31.07.2015	119.42		FY 2018-19	49.16	0	0	Technical Bid approved. Financial bid yet be approved.
4	Barrackpore	Dag. No- 2196, MOUZA: CHANAK, J.L. NO. 4, HOLDING NO.151(26), M.P. ROAD, WARD NO	50	16.12.2015	120.54		FY 2017-18	48.21	0	10%	Due waterlogging construction we is stoped. Inform by AE concern ULB
5	Halisabar	Chowdhury Para Road, Mouza: Halisahar, Ward No. 06, PS. Bizpur, Dis: North 24 Paraganas	50	16.12.2015	120.75		FY 2018-19	48,3	0	8%	Technical and financial Bid opened (4 th cal
SHE!	64 AE 100		MI STE		Preservo	YEAR 2016-17	No. of Contract of	A TOP	No. of the		12 (SW1997)
6	ASANSOL (4 Shelter unit)	(KULTI, 4 JAMURIA, ASANSOL, RANIGANJ)	200	26.05.2016	486.92		FY 2018-19	194.8	0	10% for Jamuria Layout given for Raniganj	Work Order issue for Jamuria (Raniganj Poposed for si change(relevant documents are ne submitted by UL for Asansol (Kulti)
7	Bhatpara	NARAYANPUR, KUTUBPUR,WARD NO31, MOUZA- PANPUR, J.L. NO 05,DAG NO- 380(R.S.),843(L.R.), L.R. KH NO-2685, BHATPARA	50	26.05.2016	134.31		FY 2018-19	53.72	0	0	Technical b opened (3 rd call Financial bid yet be opnened
8	Bankura	MOUZA-Bankura, J.L. NO- 211,PLOT NO. 817, WARD NO 1, Dist- Bankura	50	26.05.2016	113.27		FY 2018-19	45.3	0	0	Work order issue for construction 22.05.201 Work is not starte by ULB, Sever times intimated start work
9	Uttarpara-Kotrang	K.G.T ROAD, WARD NO. 05 UNDER UTTARPARA MUNICIPALITY	50	04.10.2016	167.51		FY 2018-19	67	0	0	Work Order issue by ULB on 12.07.2017. Wor is not started by ULB, Several times intimated t start work
10	Titagarh	A.P. DEVI ROAD, WARD NO. 06, UNDER TITAGARH MUNICIPALITY, Dist- N24PS	50	04.10.2016	120.54		FY 2018-19	48.21	0	0	Poposed for site change(relevant documents are no submitted by ULI
11	Rajpur-Sonarpur	WARD NO. 22, MOUZA: MAHINAGAR, J.L. NO. 79 under RAPUR- SONARPUR MUNICIPALITY	50	09.02.2017	118.33		FY 2018-19	47.33	0	0	Work order issue on 18.10.2017

Si No.	Name of ULB	Location of the Shelter	Capacity of each	Date of approval	Total Project	Date of Commen	Date of completi	Tentative time of	Fund Received	Total expendit	Physical progress	Remarks
12	Mahestain	WARD NO. 35, MOUZA: SARAGBAD, J.L. NO. 47, P.S. MAHESTALA under MAHESTALA MUNICIPALITY	50	09.02.2017	118.35			FY 2018-19	47.34	0	0	Work order issue on 16.10.2017
13	Tamralipta	WARD NO. 13, J.L. NO. 143, MOUZA: PARBATIPUR, P.S. TAMLUK under TAMRALIPTA MUNICIPALITY	50	09.02.2017	122.04			FY 2018-19	48.82	0	0	1 st Call and 2 n was cancelled du to insufficier number (c bidders,3rd call floated. Techini bid yet to b approved.
14	Arambag	WARD NO. 03, J.L. NO. 37, MOUZA; PASCHIM KRISHNAPUR, under ARAMBAG MUNICIPALITY	50	09.02.2017	114.87			FY 2018-19	45.95	0	0	Work order issued on 17.10.2017
				250	FINANCIAL	YEAR 201	7-18	TALL SER	20.00			25 000000
15	North Dum Dum	Ward No. 09, Mouza- Bandra, J.L. No. 09, Khatian No. 57, North Dum Dum, Dist- North 24 Paraganas	50	05.06.2017	123.05			FY 2018-19	49.4	0	0	Detailed Design & Drawing yet to be received from MED
16	Barasat	Ward No. 16, Mouza- Banamalipur, J.L. No. 80, Khatian No. 01, Barasat, Dist North 24 Paraganas	50	05.06.2017	116.51			FY 2018-19	46.6	0	0	Aptroval for issuing work order is pending.
17	Santipur	Ward No. 18, J.L. No. 22, Mouza Santipur, P.S. Santipur, Dist-Nadia	50	05.06.2017	113.87			FY 2018-19	45.54	0	0	i st call was cancelled by EE, MED
18	Jiaganj Azimganj	Ward No. 01, J.L. No. 36, Mouza- Panisali, Jiaganj Azimganj, Dist Mursidabad		05.06.2017	120,69			FY 2018-19	48.27	0	o	Tender is not floated.
19	Balurghat	Ward No. 25, J.L. No. 110, Mouza: Khadimpur, Balurghat, Dist- South Dinajpur	50	05.06.2017	122.81			FY 2018-19	49.12	0	0	Tender process is not initiated
20	Tarakeswar	Ward No. 10, J.L. No. 29, Mouza: Tarakeswar, Tarakeswar, Dist- Hooghly	50	05.06.2017	121.74			FY 2018-19	48.7	0	0	Technical bid opened. Financial Bid yet to be opened
21	Madhyamgram	Ward No. 08, Mouza: Doharia, J.L. No. 45,Badu Road,P.S. Madhyamgram, Dist- North 24 Paraganas	50	03.08.2017	118,56			FY 2018-19	47.42	0	0	Soil Test has been done & process for preparation of Detailed Design & Drawing





OFFICE OF THE COUNCILLORS OF ARAMBAGH MUNICIPALITY

Arambagh, Hooghly.

Phone: (03211)255030/257467, Fax: 255030

Ref. No. - 1075 / Aram NULM

Date 17. 10 . 17

From: The Chairman

Arambagh Municipality.

ABC Engineers Co-operative Society Limited.

Near Arambagh Boys High School, Ward No.-3, Arambagh, Hooghly.

Ref.:-NIT No.-47/ARAM/2016-17(3rd Call) Dated 28/06/2017



Sub: - Work Order for Construction of a Four Storied Building for 50 beded Shelter for Urban Homeless within Arambagh Municipality under NULM Project.

Amount put to Tender -- Rs.98,55,805/-Contractual Rate - @0.36% below Tendered Amount - Rs. 98, 20, 324.10 Deposited Earnest Money -- Rs.1,97,116/-Time Allowed: 365 days

Dear Sir.

With reference to the above I, on behalf of the Board of Councillors of Arambagh Municipality, have the pleasure to inform you that your rate @ 0.36%(zero point three six percent) below for the said work as offered by you on dated 1/09/2017 stands lowest and as such your tender is hereby approved & accepted by this office. Thus the total value of your work comes to Rs.98,20,324.10 (Rupees Ninety Eight lakh Twenty thousand Three hundred Twenty Four point one zero) only, inclusive of all taxes and charges.

You are requested to take up the work immediately in consultation with the Executive Engineer M.E.Dte. Hooghly as per specifications of the Schedule of Rates (enclose herewith) and as per direction of the Engineer-in-Charge of said work. Any materials supplied by the contractor for the work should be approved by the Engineer-in-Charge prior to use in the construction building work, You are requested to note that total time allotted for the work is only 365 days and necessary progress for the work should be made in proportion to the time allotted for the entire work. Other wise penal action will be taken by the Municipality.

However you will furnish an agreement within seven days in Duplicate Tender Form which will be available from the office after depositing requisite fees.

Thanking you,

Yours faithfully.

Chairman

Chairman Arambagh Municipality agh Municipality

Memo no .-

Date -

Copy forwarded for information and necessary action to :-

1. The Sabhadhipati, Hooghly District

2. The Chief Engineer, M.E. Dte, Bikash Bhaban, Salt Lake, Kol - 700091

3. The District Magistrate, Hooghly, P.O. Chinsurah, Dist-hoghly

4. The Superintending Engineer, West circle, M.E.Dte.

5. The Executive Engineer, Hooghly Division, M.E.Dte.-He is requested to take up the work immediately.

The Superintending of Police, Hooghly District

7. The Income Tax Officer, Chinsurah, Hooghly

8. The Director of Local BodiesGovt. Of W.B.Purta Bhavan(1st Floor), Salt Lake, Kolkata-91

The Accountant, Arambagh Municipality

10. The Head Clerk, Arambagh Municipality

11. The Councillor, Ward No. - 03, Arambagh Municipality

His Municipality Municipality

MAHESHTALA MUNICIPALIT MAHESHTALA SOUTH 24 PARGANAS

Phone: 2490-1651, 2490-3389

Fax :- 2490-9296, Email : maheshtalamunicipality@gmail.com

Memo No: 2161/MM/WBSULM/SUH/131(6)

Date: 16.10.2017

To, M/S KEYSTONE ENGINEERS. PROPRIETOR: SYED SAKER ALI, JT VILLA, 24 NATUN NAGAR ROAD KOLKATA-700088.

Sub: Letter of acceptance for the work construction of 50 bedded four storeyed shelter under NULM for Urban Homeless at Maheshtala Municipality.

e-NIT NO e-TENDER ID

: MAD/MM/NIT-69/17-18 : 2017_MAD_123267 1

Estimated AmountAmount put to tender

Rs. 13789212.00/-Rs. 13387585.00/-

Quoted percentage

0.1% Less

Tendered Amount:

Rs. 13374197.00/-

Time for completion

12 months

Dear Sirs.

Your quoted amount for the above said work has been accepted on behalf of the Board of Councillors of Maheshtala Municipality.

You are to execute formal agreement in three (3) copies in municipal printed tender form out of which one on Ten rupees non judicial stamp paper, which may be supplied by you, all other documents will be made available from this office on usual charges within seven (7) days from the date of issue of this letter. In case of failure to do so within the prescribed period, your offer will be liable for termination and the earnest money deposited by you, will be forfeited without any reference to you.

You are also requested to apply in form no (V) as per rule 21(2) of West Bengal contract labour (Regulation & Application) Rule 1972 for obtaining a certificate of Principal Employees in order to apply to the respective regulation officer of Labour Department in this connection.

The work should be executed as per specification, drawing and the terms and condition as laid down in the tender agreement. The Executive Engineer, South 24 Parganas Division, M.E. Dte, who will act as Engineer-in-charge will supervise the execution of the work.

Arrangement like go-down, labour shed, site office etc. should be immediately be made in order to take up this work. Please take up the work immediately in consultation with the A.E., Maheshtala Municipality under direction of from the EIG.

Page No. 1 of 2



OFFICE OF THE EXECUTIVE ENGINEER BANKURA DIVISION MUNICIPAL ENGINEERING DIRECTORATE U.D.& M. A. DEPARTMENT

Taragati Samanta Road, P.O.Kenduadihi, Dist.- Bankura, PIN- 722102. Phone& Fax: (03242-250922), e-mail:med_bku_divn@yahoo.com

No.

MED/BKU/

From: The Executive Engineer,

Bankura Division

Municipal Engineering Directorate

To.

Kartick Sen

Rajagram, Bankura

[

Date -

GMM- 5051

Subject: Construction of 50 Bedded five storied Building and anciliary work for shelter for Urbam Homeless within jurisdiction of Bankura Municipality under NULM. Lay out Plot no.- 817(R.S), Mouza- Bankura, J.L. No.-211 Bankura.

Reference: A) Work Order No.- i) 618/VIII-14, dated- 22.05.17 & ii) MED/BKU/95/NULM-1/2015, dt.-25.05.17.

B) NIT No. -WBMAD/CM/BM/24/NULM/2016-17

Dear Sir.

Whereas it appears to the undersigned that, the work entrusted to you on 22.05.17 with a time of completion 550 days from the date of issue of the Work order. But till this day you did not start the work. In the mean time, about 4 months has already been passed away. It is obvious that, the site was not free from encroachment, but at present, the Municipality has shifted the encroachments and the Trees cutting has also been done of about last one month ago. In spite of that, you did not insert any effort to start the work and the reason behind it, is not clear to the undersigned.

In this situation, you are instructed to state the reason for not starting up the works, within 3 days from the date of receipt of the letter failing which necessary action will be taken up against you as per tender clause.

Further, you are requested to submit the work programme matching with the completion date of the work order keeping in mind that, 'Time is the Essence of the Contract'.

Yours faithfully

Executive Engineer

Bankura Division, M. E. Directorate

No. MED/BKU/ 440 (2) / NULM - 1 / Copy forwarded for information and necessary action to :

Date - 22 . 9 . 17

- 1) The Chief Engineer, Municipal Engineering Directorate, Bikas Bhavan, Salt-Lake City, Kol.-91.
- The Director SUDA, ILGUS Bhavan, HC Block, Sector-III, Bidhannagar, Kolkata-106.
 - 3) The Chairman, Bankura Municipality, Bankura.
- 4) The Superintending Engineer, South Circle, M. E. Directorate, Khargapur, Paschim Medinipore.
- 5) Sri Malay Bhattacharjee,, Assistant Engineer, Bankura Division, M.E. Dte
- 6) The Divisional Accounts Officer, Bankura Division, M.E. Dte.

Executive Englager

Bankurg Division Divis. (Media) ate

M.E. Directorate

Govt. of Weet Bengal



রাজ্য নগর উন্নয়ন সংস্থা



STATE URBAN DEVELOPMENT AGENCY

''ইলগাস ভবন'', এইচ-সি ব্লক, সেক্টর-৩, বিধাননগর, কলকাতা-৭০০ ১০৬, পশ্চিমবঙ্গ "ILGUS BHAVAN", H-C Block, Sector - III, Bidhannagar, Kolkata - 700 106, West Bengal

क नाः	.60a S
4 45	To 9

SUDA- 23 /2014(MPR) / 799

13,10,2017 তারিখ

From: Director, SUDA

& Mission Director, WBSULM

To: The Chairman,

Uttarpara-Kotrang Municipality

Sub: Progress of the work of construction of Shelter for Urban Homeless under DAY-NULM

Sir.

You may be aware that one 50 bedded shelter unit under the scheme Shelter for Urban Homeless (SUH) under DAY-NULM was sanctioned in favour of your municipality by the Project Sanction Committee on 04.10.2016. From the record available at this office, this is noticed that Work Order for construction of the shelter was given by the ULB on 12.07.2017 and the work is not grounded till now.

Under these circumstances considering the gravity of the situation, you are requested to ground the work on immediate basis so that it will be reflected in the monthly progress

report which will be communicated to appropriate authority as per norms.

Yours faithfully,

Director, SUDA & Mission Director, WBSULM

Memo No23 /2014(MPR)/ 799 (10)

Date: 13.10.2017

Copy forwarded to the Chief Engineer, MED for information and further course of action

Director, SUDA & Mission Director, WBSULM



রাজ্য নগর উন্নয়ন সংস্থা



STATE URBAN DEVELOPMENT AGENCY

''ইলগাস ভবন'', এইচ-সি ব্লক, সেক্টর-৩, বিধাননগর, কলকাতা-৭০০ ১০৬, পশ্চিমবঙ্গ "ILGUS BHAVAN", H-C Block, Sector - III, Bidhannagar, Kolkata - 700 106, West Bengal

SUDA- 23 /2014(MPR) / 798

ভারিখ 13.10.2017

ক্রমিক লং From: Director, SUDA

& Mission Director, WBSULM

To: The Chairman, Bankura Municipality

Sub: Progress of the work of construction of Shelter for Urban Homeless under DAY-NULM

Sir,

You may be aware that one 50 bedded shelter unit under the scheme Shelter for Urban Homeless (SUH) under DAY-NULM was sanctioned in favour of your municipality by the Project Sanction Committee on 26.05.2016. From the record available at this office, this is noticed that Work Order for construction of the shelter was given by the ULB on 22.05.2017 and the work is not grounded till now.

Under these circumstances considering the gravity of the situation, you are requested to ground the work on immediate basis so that it will be reflected in the monthly progress report which will be communicated to appropriate authority as per norms.

Yours faithfully,

& Mission Director, WBSULM

Memo No23 /2014(MPR)/ 798 /(1)

Date: 13.10.2017

Copy forwarded to the Chief Engineer, MED for information and further course of action

Director, SUDA & Mission Director, WBSULM

Account Section: 2358 6408

Yevelor.

SEP 2017

The Birector S. U.D.A

OFFICE OF THE MUNICIPAL COUNCILLORS, BHATPARA

1/1 West Ghoshpara Road, P.O - Kankinara North 24 Parganas, 743126

CONDITIONS AND REQUIREMENTS FOR TENDERING

e-NIT No:- MAD/ULB/BHATPARA/DR-2/3555

Form - L 3rd Call Dated:05/09/2017

Municipality for the following Works). MAD/ULB/BHATPARA/DR-2/2724,Dated:02/08/2017 due to technical reason 3rd call is invited by the Chairman, Bhatpara Sealed Tender in Two parts i.e. Technical bid and Financial bid in cancellation of earlier Tender 2nd Call vide e-NIT No.

[resent]	No.
Construction of 50 beded four storied shelter for urban homeless at Bhatpara, under NULM.	Description of Work
1,03,99,038.00	Estimated Amount
207981/-	Earnest Money (2%)
20/-	Price per copy of Tender Form
5000.00/-	Price per copy of 1 set of other Tender Documents
180 Days	Time of Completion

9 Concerned. Name and Address of the Department

0 whom eligibility certificate is to be Name and Address of the Authority from

obtained

Bhatpara Municipality, P.W.D. Department, 1/1 West Ghoshpara Road kankinara, 24 PGS (North)

Engineer, P.W.D. Department, Bhatpara Municipality, 1/1 West Ghoshpara

Road kankinara, 24 PGS (North)

- Name and Address of the Authority
 Accepting the Tender
- c) Contractors eligible to submit Tenders
- Chairman, Bhatpara Municipality, 1/1 West Ghoshpara Road kankinara, 24 PGS (North)
- 30% value of similar nature of work in a single contract against each Item of Work within last 3 years in any Govt. /Semi Govt./ULB Intending tenderer must have completed Work of Value not less than
- II. Valid PAN No., G.S.T.No.,copy of acknowledgement of latest Income-Tax Return & Professional Tax Return
- III. The intending tenderer asked to deposit the earnest money through the e-procurement portal of the Government of West Bengal http://wbtenders.gov.in using his login id & password by
- Select the tender to bid and initiate payment of pre-defined EMD/Tender Fees for that tender by selecting from either of the following payment modes:
- Net Banking (any of the banks listed in the ICICI Bank payment gateway) in case of payment through ICICI Bank Bank payment gateway;
- RTGS/NEFT in case of offline payment through bank account in any bank.

Cost of tender form & Tender documents should be deposited either by RTGS/NEFT to **"EMD AND SECURITY DEPOSIT A/C BHATPARA MUNICIPALITY"** at Axis Bank, Bhatpara Branch (A/C No. 915020038518268, IFSC Code UTIB0002674) in favour of **"THE CHAIRMAN, BHATPARA MUNICIPALITY"**, Payable at Kolkata. Scanned copy of which shall be submitted with the e-tender document and hard copy of which must be submitted separately to the OFFICE OF THE MUNICIPAL COUNCILLORS, BHATPARA (1/1, West Ghoshpara Road, P.O. – Kankinara, District: North 24 PGS, PIN: 743126.) Mentioning e-NIT No. & date in the envelop.

F. DATE & INFORMATION

Date of Published Tenders (Online)

Documents download /sell start date (Online)

Bid submission start date (On line)

Bid Submission Closing (On line)

Bid opening date for technical proposals (On line)

12/10/2017 at 12.30 hrs

09/10/2017 at 17.30 hrs

To notified later on

06/09/2017 at 17.30 hrs

06/09/2017 at 17.00 hrs

07/09/2017 at 16.00 hrs

Date and Time of Opening of Tender Financial Bid

e-NIT No, Part No. Name & Address of the agency on the cover of the sealed envelope.) sealed to be deposited in the following office through Courier/Post/By Hand delivery on or before 12.00 hrs of 12/10/2017 superscribing (Hard copies of Part -A & Part-B of tender in separate sealed envelopes & both in another bidder envelop perfectly marked & duly Last Date and time for submission of Hard Copy of the Tender (Part-A & Part-B): 12/10/2017 at 12.00 hrs

00 MUNCIPAL COUNCILLORS, BHATPARA (1/1, West Ghoshpara Road, P.O-Kankinara, District: North 24 PGS . Pin -743126.) later than 12.00 hrs on 12/10/2017 mentioning the e-NIT No, Name, Address of agency on the sealed envelopes: Viz, OFFICE OF THE Sealed e-tenders in hard copy (Technical & Financial) will be received at the following offices through post/courier/by hand delivery not

Website: Details may be seen in our website: https://wbtenders.gov.in

Chairman, Bhatpara Municipality

Copy forwarded for information to :-

- 1) Chairman, Bhatpara Municipality
- 2) Vice-Chairperson, Bhatpara Municipality
- 3) Executive Officer, Bhatpara Municipality
- 5) The President & All Members, Tender Committee, Bhatpara Municpality
- 6) Enginner, Bhatpara Municipality
- Assistant Engineer, PWD(Building), Bhatpara Municipality
- 8) Sub-assistant Engineer, PWD (Building), Bhatpara Municipality
- Finance Officer, Bhatpara Municipality
- 10) Officiating IT Co-ordinator, Bhatpara Municipality, with a request to get the matter published in our office portal.
- 11) Head Clerk, Bhatpara Municipality
- 12) Cashier, Bhatpara Municipality
- 13) Receiving Clerk, Bhatpara Municipality
- 14) Notice Board, Main Office & Branch Office Shyamnagar
- 15) Executive Engineer, 24 Pgs(N) Division, ., Barasat, M.E.D., Gov. Of W.B.
- 16) Superintending Engineer, East Circle, M.E.D., Baguaiati, Gov. Of W.B.

13) Joint Secretary, M.A.D., Gov. Of W.B.

Chairman,


Bhatpara Municipality


Format of Monthly Status of SUH, of component under DAY-NULM

Name of ULB: Midnapore Municipality

Status as on. 07.09.17

the Shelter	Central Bus Stand, Midnapore, Paschim Medinipur
Capacity if each Shelter (Beds)	50
Date of Approval by PSC	9/2/17
Civil & Civil & Electrification with Sanctuary Plumbing cost (With 3% Contingency)	85.99Lakh
Others cost (cost of Utensils & Furniture etc.) (b)	8.96Lakh
O & M Cost per year	6.02
Total Project Cost (a+b)	94.95
Date of Commencement of Work	25/07/17
Expected date of completion	31/12/17
Fund Received (Total)	39.50
Total Expenditure Incurred	Z.
Physical Progress achieve in details (Photograph annexed if applicable)	Up to Roof Level





8 SEP 2017

5783/2

Chairman Midnapore Municipality

Government of West Bengal Adhibition Day Office of the District Magistrate & Collector Paschim Bardhaman Date-Memo No-DEPARTMENT AND MUNICIPAL AFFAIRS the Secretary GOVT. OF W.B. Asansol Municipal Corporation Asansol, Paschim Bardhaman. Sub:- Submission of status report regarding the progress of shelter under the scheme shelter for · Urban Homeless (SUH) under the programme NULUM in the Urban Local Bodies under Ref:- Letter from Secretary, UD & MA affairs, Govt. of West Bengal dt-06.7.2017. In reference to the above mentioned letter you are requested to submit a status report as

In reference to the above mentioned letter you are requested to submit a status report as required to the secretary, UD & MA Department, Govt. of West Bengal with a copy to this end.

Additional District Magistra (1)

Enco:- As stated.

Memo No- 03(2) MA Posch Brother

Date- 10 8 17

Copy forwarded for information to:-

Secretary, UD& MA, Govt. of West Bengal.

2. CA to District Magistrate, Paschim Bardhaman.

Additional District Merstrate(6)



Office of the District Magistrate & Collector

Pasi Sim Bardhaman

No. Secy/UD&MA/2017/16

Department of Urban Development & Municipal Affairs Government of West Bengal 'Nagarayan', DF-8, Sector-I, Salt Lake Kolkata - 700064

Phone: (033) 2334 9394/Fax: 2334 7880

Email: secy.ma-wb@gov.in

Dated, 6th July, 2017

The District Magistrate Paschim Burdwan District West Bengal

Sub: Monitoring the progress of shelters under the scheme shelter for Urban Homeless(SUH) under the Programme NULM in the Urban Local Bodies in West Bengal

Department of Urban Development and Municipal Affairs (UD&MA) has sanctioned 34 shelters under the scheme Shelter for Urban Homeless under National Urban Livelihoods Mission (NULM) in different Urban Local Bodies in West Bengal. Out of these 34 shelters four shelters (Asansol, Kulti, Jamuria Raniganj) were sanctioned in favour of Asansol Municipal Corporation on 26.05.2016 and fund has been released in favour of them. But no physical progress is found for any cases after expiry of more than one year.

You are requested to take suitable action to guide the ULB to complete the construction work as soon as for functionalization of shelters within the stipulated time period of one year.

(Onkar Singh Meena)

Secretary to Government of West Bengal

Boncollan, and

FORMAT OF THE MONTHLY STATUS OF SUH, A COMPONENT UNDER DAY-NULM

Waiting for NOC for alternate land (Vested) at Dishergarh	Z.				11727668/-	155.37 LAC	870500/-	10857168/-	20.04,2017	50	KULTI
Waiting for NOC for alternate (Vested) land at opposite Durga market	N _i L	19480000/-			11727668/-	155.37 LAC	870500/-	10857168/-	20.04.2017	50	ASANSOL
5% FOUNDATION LEVEL	2	200	24.05.18	25.05.17	11727668/-	155.37 LAC	870500/-	10857168/-	20.04.2017	50	JAMURIA
Jungle cutting & land survaying is or process	Z E		24.05.18	25.05.17	11727668/-	155.37 LAC	870500/-	10857168/-	20.04.2017	50	RANIGANI
PHYSICAL PROGRESS ACHIEVED IN DETAILS	TOTAL EXPENDITURE INCURRED	FUND RECEIVED (TOTAL)	EXPECTED DATE	DATE OF COMMENCEMENT OF WORK	TOTAL PROJECT COST (a+b)	O&M COST PER YEAR	OTHER COST (COST OF UTENSILES & FURNITURE ETC) (b)	CIVIL & ELECTRIFICATION WITH SANITERY PLUMBING COST(WITH 3% CONTIGENCY) (a)	DATE OF APPROVAL BY PSC	CAPACITY IF EACH SHELTER(BED)	THE SHELTER
			STATUS AS ON					ORPORATION	MUNICIPAL C	NAME OF THE ULB: ASANSOL MUNICIPAL CORPORATION	AME OF THE

Ushnish Roy
Urban Infrastructure specialist
ANIRUT
Asansol Municipal Corporation



Asansol Municipal Corporation

2017081115109

Government of West Bengal Office of the District Magistrate, Murshidabad Town & Country Planking Branch (Municipal Affairs Section)

e-mail: maffairs.msd@gmail.com

Diary No. 323 Department of Urban Development

Govt. of West Bengal

August,2017

Memo No.

From: The Addl.District Magistrate(MA)

Murshidabad

The Joint Secretary

Deptt. of Urban Development & Municipal Affairs

Government of West Bengal

Sub: Status report of progress under the scheme 'Shelter for Urban Homeless'

in Berhampore Municipality.

Ref: No.Secy/UD&MA/2017/19 dt.06-07-2017 of the Secretary, UD&MA Deptt, WB.

Sir,

In respect to above cited subject & no. under reference this is to inform you that, after receiving 1st installment of sanctioned cost, long time has been spent for alteration of the site of the scheme. Now, after completion of e-tender process bidder documents has been sent to Superintending Engineer of Municipal Engineering Directorate for technical evaluation.

However, work order will be issued shortly with time frame of completion of the construction is six months.

This is for your kind appraisal.

Yours faithfully,

Eclo: As stated.

Addl. District Magistrate(MA) Murshidahad

BERHAMPORE MUNICIPALITY BERHAMPORE : MURSHIDABAD

Phone: 250012(O)/ 256762 CM & FAX No. – 03482-251299

e-mail: chairman.berhampore@gmail.com

Memo No.:- NULM/1008/B.M./2017

Dated, Berhampore, the 26-07-2017.

From: Executive Officer,

Berhampore Municipality

To

The District Magistrate

Dist.- Murshidabad

[Municipal Affairs Section]

Sub.:- Status report of progress under the scheme of "Shelter for Urban Homeless" under reference.

Ref. :- Memo No.- 165/MA/En Dated 25-07-2017.

Sir.

As regards the Ref. No. Secy /UD & MA/2017/19 Dated 06-07-2017 of the Principal Secretary to the Government of West Bengal, Urban Development & Municipal Affairs Department, the undersigned is obliged to submit the following status report of the scheme of 'SUH' under the programme of NULM of Berhampore Municipality.

- 1. After receiving 1st installment of sanctioned cost on 31-07-2015, long-time has been spent for alteration of the site of the scheme.
- 2. Secondly, further time has been lost for acceptance of the suitable bidder through e-tendering process.
- 3. Today, i.e. on 26-07-2017, e-tender has been opened and in a position to be accepted.
- 4. Bidder documents will be submitted to the Superintending Engineer of Municipal Engineering Directorate, Malda Circle on 31-07-2017 for technical evaluation.
- Work-Order will be issued by the Chairman of Berhampore Municipality as soon as the necessary approval will be obtained from the State-Level-Authority in respect of the said technical bid of e-tender.
- 6. Duration of completion of the construction work of the 'SUH' is six months from issuance of the work-order.

This is submitted for favour of your kind appraisal as well as for onward submission, if necessary.

Yours faithfully,

0

Executive officer Berhampore Municipality

F:\EO-2017

Murshidabad Collegior Bespatch Section. Memo no: 173/MA/En dated: 09/8/17 To: The foint Scenchosom, WHS, "Nugar on an st-8, sectoral I, Bidhammagar Town and Gunting Warning Becarely, 0.1.6 8



FFICE OF THE MUNICIPAL COUNCILLORS ENGLISHBAZAR MUNICIPALITY, MALDA

Date 25.08.

The Director SUDA &

Mission Director, WBSULM ILGUS, Bhavan, H.C block, Sector-3 Salt Lake, Bidhannagar, Kolkata-106

Sub: Monthly Status Report of Construction of Shelter for Urban Homeless under DAY-NULM project of Englishbazar Municipality, Malda

Ref:-SUDA-23/2014(MPR)/603 (2)

Date-17,08,2017

With reference to the memo no stated above in connection with the Status Report of Construction of Shelter for Urban Homeless under DAY-NULM project of this municipality, this is to inform you that the Work Order has been issued on 09.08.2017 (copy enclosed) and the work is yet to be started. The details of the progress report is enclosed (Specific Format) for your

This is for your information & taking necessary action.

Enclo: As Stated

Englishbazar Municipality, Malda Date.....

Copy forwarded for information & necessary action:

- Additional District Magistrate (Gen), Malda
- 2. Chairman-In-Council, NULM, Englihbazar Municipality, Malda
- Executive Officer & CPO (NULM), Englishbazar Municipality, Malda
- 4. Manager-S.D.I, Englishbazar Municipality, malda
- 5. SAE-1, Englishbazar Municipality, malda,
- 6. APO (NULM), Englihbazar Municipality, Malda
- Office copy, Englihbazar Municipality, Malda

Chairman Englishbazar Municipality, Malda





OFFICE OF THE MUNICIPAL COUNCILLORS

ENGLISHBAZAR MUNICIPALITY, MALDA.

Netaji Subhas Road, Malda, Pin-732101

E-mail: englishbazarmunicipality@gmail.com()Website: www.englishbazarmunicipality.com()Office: (EPABX): 03512-252029 Fax: 03512-25339

Memo no.

To,

The Addln.District Magistrate(Gen.) Malda.

Sub:- Status Report in respect of the scheme "Shelter for Urban Homeless" under NULM, English Bazar Municipality Malda- Reg.

Madam.

APPROVED SITE ST. PSMM - 5252 Mr 24/09/02 With reference to your letter No -III/MA/MLD Dated-26/27th July ,2017 in connection with the status report in respect of the scheme "Shelter for Urban Homeless" under NULM, this is to state that the tender process for the construction of 50-beded shelter under the said scheme has been completed well past. However the work order has been kept with-held on account of want of sanction from "Technical committee' under SUDA. With the receip' of the said sanction from the Director, SUDA, Kolkata -700106, vide No-SUDA -272/2007 (pt-VV) /489 Dated-28/07/2017 (Photocopy enclosed), necessary work order will be issued within couple of days.

Encl: As above

Yours Faithfully

Chairman

witi (_______________.

English Bazar Municipality, Malda

No. 1133 10,2 17,18 (4) Date: 01.08.207

Copy forwarded for favour of kind information to :-

- The Secretary to the Govt., Deptt. Of Urban Devlopment & Municipal Affairs "Nagarayan", DF-8, Sector-I, Salt Lake, Kolkata-700064.
 - 2. The Vice Chairman, English Bazar Municipality, Malda.
 - The C.I.C, English Bazar Municipality, Malda.
 - 4. The S.A.E-I, English Bazar Municipality, Malda.
 - 5. Guard File, English Bazar Municipality, Malda.

Chairmar English Bazar Municipality, Malda



Government of West Bengal Office of the District Magistrate, Bankura Municipal Affairs Cell

©

03242-257-658
bankuramunicipalaffairs@gmail.com

Memo no.

101

/M.A

/Dated 25. 08. 2017

To

The Joint Secretary to the Government of West Bengal, Deptt. of Urban Development & Municipal Affairs, Government of West Bengal,

'Nagarayan', DF-8, Sector-I.

Salt Lake.

Kolkata - 700064.

Smm-5851 29/08/17

Sub: Report regarding progress of Shelters under the scheme Shelter for Urban Homeless (SUH) under the Programme NULM in the ULBs.

Ref: Your Memo. No. Secy/UD&MA/2017/21 dated 06.07.2017

Sir,

With reference to above, this is for favour of your kind information that an amount of Rs.45.30 lakh has been sanctioned for construction of Shelter with in Bankura Municipality and a plot bearing no. 817(RS), Mouza Bankura, JL no. 211 has been identified for the construction of said Shelter with 50 Beded capacity. The Executive Engineer, M.E. Dte. Bankura Division has been authorized as a Executing Agency by the Bankura Municipality for implementation of the said project. The work yet to be started and expected to be completed by November. 2018 as stated by the Executive Agency.

A format report in this regard of the Chairman, Bankura Municipality is enclosed herewith and the work is being pursued in time to time.

Thanking you.

Enclo: As stated.

Yours faithfully

Additional District Magistrate (Dev)

Bankura. Dated 25/08/2017

Memo.No. 101(2)MA Copy forwarded to:

> The Chairman, Bankura Municipality with the request to take effective action for immediate completion of this scheme. This has a reference to his memo. no. 1335/VIII-14 dated 26.07.2017.

2. C.A. to District Magistrate, Bankura with the request to place it before the District Magistrate, Bankura.

Additional District Magistrate (Dev)

Bankura.

FORMAT FOR MONTHLY STATUS OF SUB, A COMPONENT UNDER DAY-NULM

as on: 25th day of July 2017
Status
Name of the ULB: BANKURA

in the state of th	
Physical progress achived in defails (Photograph Buneved if	Carlotte and the state of the s
princing pri	7
fued (Total)	9 4
Sompletion (Total)	ith day of Novembe 2018
Date of work of work	Vertex Sint
100	236.41
reak ord per	6,0,3
(fortal OAN Project (action) Furniting year (action)	×. ×.
For Difficulties with Seniorge plumbing cost (With 3%) (autingency) (a	. T. es.
Date of Mysterian y	Provide on Dr. Brown Wills vide Work NAVP C. DOTGET 2016.
Nealer Meds:	Sty Rests
or fav.	Section Present Views of Tables of Members of Nov. 1911 Bunkura, 18 Nov. 1911 Bunkura

BANKURA MUNICIPALITY
Chauman
Bankura Municipality

Send Back to	Save Draft	hive	Report Spam	t with reply Delete	
					~
					^

Use the search box or search options to find messages quickly!

You are currently using 12551 MB (81%) of your 15360 MB

Last account activity: 19 minutes ago on this computer. Details

Terms - Privacy - Gmail Blog - Google Home

GOVT. OF WEST BENGAL OFFICE OF THE EXECUTIVE ENGINEER COOCH BEHAR DIVISION MUNICIPAL ENGINEERING DIRECTORATE DEPARTMENT OF MUNICIPAL AFFAIRS

P.O & Dist.- Cooch Behar. PIN - 736101.
Phone: (03582) 230743, E-Mail: coochbehardivnmed@gmail.com

Memo No. ME / COB/

/ NULM-2/15, Pt.I

Date: 20.07,2017

From:- Executive Engineer, Cooch Behar Division, M.E. Directorate.

To:- The Chief Engineer,

Municipal Engineering Directorate,
Bikash Bhavan, 1st Floor,
Salt Lake City, Kolkata – 700 091.

Smm-5257 Mr 2407/17

Sub:- Submission of Monthly Status Report for "Construction of 50 Bedded Shelter for Urban Homeless (SUH) Building at Cooch Behar under DAY-NULM as on 13th July'2017 under Cooch Behar Municipality.
 Ref No.- Chairman's letter Memo No. PWD / 538 /17, dtd. 14-07-2017

Sir,

Enclosed please find herewith the Monthly Status Report for "Construction of 50 Bedded Shelter for Urban Homeless (SUH) Building at Cooch Behar under DAY-NULM" as on 13th July'2017 under Cooch Behar Municipality.

This is for favour of your kind perusal and necessary action, please.

Enclo: -As stated above.

Yours faithfully,

Executive Engineer, Cooch Behar Division, M.E. Dte.

Date: 20.07.2017

Memo No. ME / COB/ 727() / NULM-2/15, Pt.I

Copy forwarded for kind information to :-

The Director, State Urban Development Agency (SUDA), "ILGUS" Bhavan, H-C Block, Sec-III, Kolkata-106- along a copy of the same.

2. The Superintending Engineer, North Circle, M.E. Dte., Siliguri. -along a copy of the same.

3. The Chairman, Cooch Behar Municipality - along a copy of the same.

Executive Engineer,
Cooch Behar Division, M.E.Dte.

Executive Engineer
Coochbehar Division M.E.Dte
Govt. of West Bengal

CONST. OF SUH BUILDING UNDER DAY-NULM AT COOCH BEHAR

COOCH BEHAR MUNICIPALITY Status as on: 13/07/2017

Subject Subjec	Shantiban, Ward No. 10	Location of the Shelter
Sub-Assistant Engineer thomas design Bellar Mu Cooch Bellar Mu	50	Capacity of each shelter (beds)
Sub-Assistant Engineer Sudapa addistrante ballon gineer Cooch Behar Cooch Behar	7/31/2015	Date of approval by PSC
	106.45	Civil & Electrification Cost (in Lakh) (With 3% Contingency)
Executive officer Cooch Behar Municipality Cooch Behar Municipality Cooch Behar Municipality	16.57	Others Cost { in Lakh} (Cost of utensiles & Furniture etc.) b
illy micipality	6.02	O&M Cost per year (in Lakh)
	123.02	Total Project cost (a+b) (in Lakh)
2883000	18/01/2016	Date of Commencement of Work
Salayuranan Bernawa Maua	30.06.2017	Excepted date of completion
Tripality .	64.76	Fund re Central
	30.86	Fund received (in Lakh) entral State Tota
	95.62	Lakh) Total
Decut MEDite., Coo Govit. of	Rs. 74.32	Total expenditure incurred (in Lakh)
MEDte., Cooch Behar Division Govt. of west Bengal	All structural works are almost completed. Inside and outside plastering completed. Colour washing in progress Elecrification work is going on.	Physical progress achieved in details (Photograph annexed of applicable)





OFFICE OF THE EXECUTIVE ENGINEER **BANKURA DIVISION** MUNICIPAL ENGINEERING DIRECTORATE U.D. & M. A. DEPARTMENT

Taragati Samanta Road, P.O.Kenduadihi, Dist.- Bankura, PIN-722102. Phone& Fax: (03242-250922), e-mail:med_bku_divn@yahoo.com

No. MED/BKU/

From: The Executive Engineer,

Bankura Division

Municipal Engineering Directorate

Chief Engineer To.

Municipal Engineering Directorate

Bikash Bhavan, Salt-Lake City, Kolkata-91

Date avelo

Subject: Submission of Monthly status report of SUH, a component of NULM.

Ref.: Chairman, Bankura Municipality's Office Memo No -1335/VIII-14, dt.-26.07.2017.

Sir,

As received from the Chairman, Bankura Municipality vide his office memo as cited above, I am to submit the monthly status report of SUH as per the revised approved cost with due recommendation from this end for your kind perusal and taking necessary action please.

Yours faithfully

ve Engineer **Bankura Division** M. E. Directorate

Enclo: As stated above.

Copy forwarded for information & necessary action to-

HO - MED/ BKU/ 277 (U/ HULM-1/2015

The Director , SUDA, ILGUS Building- With a copy of Monthly Status Report as on 25.07.17.

2) The Superintending Engineer (S), Municipal Engineering Dte. Kharagpur, Paschim Medinipore - With a copy of Monthly Status Report as on 25.07.17.

3) The Chairman, Bankura Municipality.

Bankura Division
M. Exerctiorate (Works)
Bankura Divn. M.E. Directorate Govt. of West Bengal

dt-31.07.17

FORMAT FOR MONTHLY STATUS OF SUH, A COMPONENT UNDER DAY-NULM

Name of the ULB:- BANKURA

Status as on:- 25th day of July' 2017

Amount Rs. In Lakh

Lay Out Plot No 817(R.S.). Mouza – Bankura, JL No211 Bankura	Location of the Shalter
50 Beds	Capacity if each Shatter (Beds)
20th day of December 2016 vide Memo No. 696/MA/P/C- 10/1G-1/ 2016	Date of Approval by PSC
217.66	Civil & Electrification with Sanitary plumbing cost (With 3% Contingency) (a)
23.25	Other Cost (Cost of Utensiles & Furniture etc.) (b)
6.02	O & M Cost per year
240.91	Total Project Cost (a+b)
Capacity if Date of each each Shalter PSC (With 3% (Cost of Beds) 20th day of December 2016 vide 696/MA/P/C-10/1G-1/2016 Total Ox Mercost (Cost of Project (Cost per Project (a+b)) 23.25 Other Cost of With Project commencement of Project (Cost work (a+b)) Other Cost of With Project commencement of Commencement of Commencement of Commencement of Commencement of Completion (Total) incurd incurd incurd (a+b) Expenditure Sear (a+b) Fund Total Commencement of Completion (Total) incurd incurd incurd (a+b) PSC (With 3% etc.) (b) 20th day of December 2016 vide (a+b) 20th day of 10/1G-1/ 2016	
30th day of Novembe 2018	Expected date of completion
45.30	Fund received (Total)
Z.	Total Expenditure incurd
0%	Physical progress achived in details (Photograph annexed if applicable)

Shaller o resurfued

Assistant Engineer
Assistant Engineer
M.E. Directorate
Govt. of West Bengal

Recommended

PAN

Executary on histories

Bankura Divn. (Works)

Bankura Divn. (Works)

Bankura Divn. (Works)

STT 177 Bankur

CHARMAN BANKURA MUNICIPALITY

Chairman Bankura Municipality

Format for Monthly status of SUH, A component under DAY-NULM Construction of 50 Beded Shelter at Kutir Math, Chandannagar

The second secon									Status as on :	7.			01-08-2017
Name of ULB		Changemagore	d										Amount Rs in ak-
				The second secon					Fu	Fund Received	٥		
Location of Shel ter	Capacity of each Shelter (beds)	Date of approval by PSC	Civil & Electrification Cost (With 3% contingency)	Other Cost (Cost of utensiles & Furniture etc)	Der year	Froject Cost (a + b)	Project Cost comencement of (a + b) work	date of completion	Central	State	Total	Total Expenditure incurred	Physical Pogress achieved in details (Photograph annexed if applicable)
CHANDERNAGDRE	8	5 12 2015	108.78	16.68	ē	124 96	15-11-2016	15-12-2017	36.23	12 08	48 30	16.51	1st Floor Construct or ongoing

E-120

Executive Engineer

Vunicipal Engineering Department

M.E. Directorate, Deptt. of M.A.

Changernagore Municipal Corporation

Chandernagore Municipal
Corporation

Olc



রাজ্য নগর উন্নয়ন সংস্থা STATE URBAN DEVELOPMENT AGENCY



"ইলগাস ভবন", এইচ-সি ব্লক, সেক্টর-৩, বিধাননগর, কলকাতা-৭০০ ১০৬, পশ্চিমবঙ্গ "ILGUS BHAVAN", H-C Block, Sector - III, Bidhannagar, Kolkata - 700 106, West Bengal

ক্রমিক নং ...SUDA-23/2014(MPR)/.. 603 (০৭)

তারিখ 17.08.2017

From: Additional Director, SUDA &

Additional Mission Director, WBSULM

To: The Commissioner/ Chairman,

Asansol MC/ English Bazar Municipality

Sub: Monthly Status Report of construction of Shelter for Urban Homeless under DAY-NULM

Sir,

This is to inform you that 50 bedded Shelter for Urban Homeless under DAY-NULM in your town has already been approved by Project Sanction Committee (PSC) and 1st installment of Central & State matching shares has also been released. For submission of periodic reports go Govt. of India, you are requested to kindly send the monthly status of construction of the shelter in your town to this office in the format enclosed herewith duly signed by the concerned Executive Engineer of MED within the first week of the following month positively as per clause No.15 of Operational guideline vide No.329/MA/C-10/3S-22/2013 dated 04.05.2015 (copy enclosed for ready reference). It may further be mentioned that the location of the proposed shelter & photographs of different states of construction may also attached with the monthly progress report.

Enclo: As stated

Yours faithfully,

Additional Director, SUDA

&

Additional Mission Director,

WBSULM

0/C

দ্রভাষ ঃ ২৩৫৮ ৬৪০৩ / ৫৭৬৭, ফ্যাক্স ঃ ২৩৫৮ ৫৮০০

Tel: 2358 6403/5767, Fax: 2358 5800, E-mail: wbsudadir@gmail.com

Account Section: 2358 6408

8 AUG 2017

Name of UEB: Midnapore Municipality

Format of Monthly Status of SUH, of component under DAY-NULM

Status as on. 02.08.17

Location of the Shelter Central Bus Midnapore, Medinipur Paschim Stand, Capacity if each Shelter (Beds) 50 Approval by PSC 9/2/17 Sanctuary Plumbing cost (With 3% Electrification Contingency) 85,99Lakh Civil & Furniture cost (cost 8.96Lakh Utensils & etc.) (b) Others O & M 6.02 per Project Cost (a+b) 94.95 Total Commencement of Work 25/07/17 Date of completion date of 31/12/17 Expected Received (Total) 39.50 Fund Expenditure Incurred Total Z Work Started annexed if applicable) (Photograph achieve in Progress Physical details

Sub-Asstt. Engineer **Midnapore Municipality**

Executive Engineer

West Midnapore Division

Govt. of West Bengal

M.E. Directorate

Midnapore Municipality Cheirman

GOVT. OF WEST BENGAL OFFICE OF THE EXECUTIVE ENGINEER COOCH BEHAR DIVISION MUNICIPAL ENGINEERING DIRECTORATE DEPARTMENT OF MUNICIPAL AFFAIRS

P.O & Dist.- Cooch Behar. PIN - 736101. Phone: (03582) 230743, E-Mail: coochbehardivnmed@gmail.com

Memo No. ME / COB/ 727

/ NULM-2/15, Pt.I

Date: 20.07.2017

From:- Executive Engineer, Cooch Behar Division, M.E. Directorate.

The Chief Engineer, To :-Municipal Engineering Directorate, Bikash Bhavan, 1st Floor, Salt Lake City, Kolkata - 700 091.

> Sub:- Submission of Monthly Status Report for " Construction of 50 Bedded Shelter for Urban Homeless (SUH) Building at Cooch Behar under DAY-NULM as on 13th July'2017 under Cooch Behar Municipality. Ref No.- Chairman's letter Memo No. PWD / 538 /17, dtd. 14-07-2017

Sir.

Enclosed please find herewith the Monthly Status Report for "Construction of 50 Bedded Shelter for Urban Homeless (SUH) Building at Cooch Behar under DAY-NULM" as on 13th July'2017 under Cooch Behar Municipality.

This is for favour of your kind perusal and necessary action, please.

Enclo: -As stated above.

Yours faithfully.

Executive Engineer,

Cooch Behar Districtive Makin Dte.

Date et o. Ovision 17 F Die Sovt. of West Bengal

Memo No. ME / COB/ 727(1-3) / NULM-2/15, Pt.I

Copy forwarded for kind information to :-

1. The Director, State Urban Development Agency (SUDA), "ILGUS" Bhavan, H-C Block, Sec-III, Kolkata-106- along a copy of the same.

2. The Superintending Engineer, North Circle, M.E. Dte., Siliguri. -along a copy of the same.

3. The Chairman, Cooch Behar Municipality - along a copy of the same.

Executive Engineer, Cooch Behar Division, M.E.Dte.

> **Executive Engineer** , cochbehar Division M.E.Dte Govt. of West Bengal

CONST. OF SUH BUILDING UNDER DAY-NULM AT COOCH BEHAR

Status as

13/07/2017

on:

COOCH BEHAR MUNICIPALITY

Ward No. 10 Shantiban, ation of the Shelter Capacity of shelter (beds) each 50 approval by PSC 7/31/2015 Date of Cost (in Lakh) Electrification Contingency) (With 3% CIVIL & 106.45 & Furniture etc.) year (in Lakh) Others Cost in Lakh) 16.57 O&M Cost per 6.02 cost (a+b) (in Lakh) Total Project 123.02 Commencement 18/01/2016 of Work Date of Excepted date of 30.06.2017 completion 64.76 Central Fund received (in Lakh) 30.86 95.62 State Total Rs. 74.32 expenditure (in Lakh) incurred Total Physical progress achieved All structural works are plastering completed. annexed of applicable) in details (Photograph Elecrification work is Colour washing in Inside and outside almost completed. going on. progress

Subcassistant Engager Subcassistant Engager

Cooch Behar Municipality
Cooch Behar Municipality
Cooch Behar Municipality

MEDIE: Cooch Behar Division
Govt. of west Bengal



রাজ্য নগর উন্নয়ন সংস্থা STATE URBAN DEVELOPMENT AGENCY

0/c



"ইলগাস ভবন", এইচ-সি ব্লক, সেক্টর-৩, বিধাননগর, কলকাতা-৭০০ ১০৬, পশ্চিমবঙ্গ "ILGUS BHAVAN", H-C Block, Sector - III, Bidhannagar, Kolkata - 700 106, West Bengal

ক্রমিক	न१	SUDA-23/2014/MPR\/	ane Com
		SUDA-23/2014(MPR)/	105(5)

তারিখ 13.07.2017

From: Additional Director, SUDA &

Additional Mission Director, WBSULM

To: Chairman Municipality

(BARRACKPORE / BANKURA / HABRA / UTTARPARA KOTRUNG/ MIDNAPORE)

Sub: Monthly Status Report of construction of Shelter for Urban Homeless under DAY-NULM Madam / Sir,

This is to inform you that 50 bedded Shelter for Urban Homeless under DAY-NULM in your town has already been approved by Project Sanction Committee (PSC) and 1st installment of Central & State matching shares has also been released. For submission of periodic reports go Govt. of India, you are requested to kindly send the monthly status of construction of the shelter in your town to this office in the format enclosed herewith duly signed by the concerned Executive Engineer of MED within the first week of the following month positively as per clause no. 15 of Operational Guideline vide no. 329/MA/C-10/3S-22/2013, dated. 04.05.2015 (copy enclosed for ready reference). It may further be mentioned that the location of the proposed shelter & photographs of different states of construction may also attached with the monthly progress report.

Yours faithfully,

o Blotfit

Enclo: As stated

Additional Director, SUDA & Additional Mission Director, WBSULM

Tel: 2358 6403/5767, Fax: 2358 5800, E-mail: wbsudadir@gmail.com

Account Section: 2358 6408



Format for Monthly status of SUH, a component under DAY-NULM

						Location of the Shelter		Name of the ULB :
						Capacity if each shelter (beds)		ne ULB:
						Date of approval by PSC		
						Civil & Electrification With Sanitatary Plumbling Cost (With 3% Contingency) (a)		
						Others Cost (Cost of Utensiles & Furniture etc.)		
						O&M Cost		
						Total Project cost (a+b)		
						Date of Commenc ement of Work		
						Date of Commenc Expected date ement of of completion Work		
						Fund received (Total)		Stat
						Total expenditure incurred		Status as on
						Physical progress achived in details (Photograph annexed if applicable)	Amount Rs. in Lakh.	

Monthly Status Report of SUH, a component under DAY-NULM JUNE 2017

۲٦.	4		ω	N	-		SI No.	
Durgapur	Haldia		Howrah	Howrah	Krishnagar		Name of ULB	
MOUZA: KHATPKUR, JL. NO. 59, P.S. KANKSA, R.S. PLOT NOS. 32(P), 33(P), 43(P), 46(P), 47(P), 49(P), 50(P), 53(P), 54(P)	Mouza: Chackrabortychak, J.L. No-160, Plot No. 16, Word No. 17		38 COWIES GHAT ROAD, BOROUGH-IV, WARD NO. 36	9, KOIPUKUR LANE, BOROUGH-IV, WARD NO.32	Jail Road, Ward No. 4, Mouza: Gobindasarak, KM		Location of the Shelter	
50	50		50	50	50		Capacity of each shelter (beds)	
19.06.2015	19.06.2015		18.03.2015	18.03.2015	18.03.2015		Date of approval	
116.56	119.53	FIS	120.3	120.3	118.3	FF -	Total Project cost (Rs. in Lakh)[excluding DPR preparation cost]	New Construction
24.04.2016	09.11.2015	FINANCIAL YEAR 2015-16		01.08.2016	11.07.2015	FINANCIAL YEAR 2014-15	Date of Commenceme nt of work	ction
31.05.2017	30.08.2016	015-16		31.10.2017	29.01.2016	014-15	Date of completion	
August, 2017			FY 2018-19	Oct 2017	June, 2017		Tentative time of Functionalizati on of shelter	
93.26	119.53		46.72	46.72	118.3		Fund Received by ULB(Rs. in Lakh)	
70.1	97.72		0	0	118,3		Total expenditu re incurred (Rs. in Lakh)	
Completed	Completed			70%	Completed		Physical progress achieved in details (Photograph annexed if applicable)	
Functional	Functional		Poposal for Land change(relevant documents yet o be received)	Roof casted upto 3 rd floor	Functional		Remarks	

11	10	9	ω	7	0	No.	
Chandannagar	Barrackpore	Berhampore	Jalpaiguri	Coochbehar	Nabadwip	Name of ULB	
PLOT NO. 175, J.L. NO. 01, WARD- 12,MOUZA: CHANDERNAGAR	Dag. No- 2196, MOUZA: CHANAK, J.L NO. 4, HOLDING NO.151(26), M.P. ROAD, WARD NO15	WARD NO. 05, J.L. NO. 100, PLOT NO. 1560/3415, 1561, 1561/3456, 1561/3987	MOUZA: KHARIA, J.L. NO.07, PLOT NO. R.S. 937(P), WARD NO. 10	Shantiban, Ward No. 10, Plot No. LR 4726 & 4728, Khatian No. LR 4050	Prafullanagar, Ward No-24, Nabadwip, Dist- Nadia	Location of the Shelter	***
50	50	50	50	50	50	Capacity of each shelter (beds)	
16.12.2015	16.12.2015	31.07.2015	31.07.2015	19.06.2015	19.06.2015	Date of approval	
121.43	120.54	119.42	118.58	119.54	118.49	Total Project cost (Rs. In Lakh)[excluding DPR preparation cost]	New Construction
15.11.2016			04.01.2016	18.01.2016	16.09.2015	Date of Commenceme nt of work	ction
15.12.2017			31.06.2017	31.05.2017	30.05.2017	Date of completion	
FY 2017-18	FY 2017-18	FY 2018-19	August, 2017	August, 2017	FY 2017-18	Tentative time of Functionalizati on of shelter	
48.3	48.21	49.16	96.84	95.62	118.49	Fund Received by ULB(Rs. in Lakh)	
0	0	0	48.81	49.62	94.08	Total expenditu re incurred (Rs. in Lakh)	
40%			85%	95%	Completed	Physical progress achieved in details (Photograph annexed if applicable)	
Work delayed started by the ULB	Work Order will be issued by 31.05.2017	1 st call was cancelled due to no bidders participated, 2 nd was cancelled due to the single bidder,3 rd call was floated	Finishing works are going on including Sanitery-Plumbing & Electrification	Electrification work is going on and plastering work in three side are completed	Will be Functional by July, 2017	Remarks	

16	15	14		13	12	No.	
Bankura	Bhatpara	ASANSOL (4 Shelter unit)		Bongaon	Halisahar	Name of ULB	
MOUZA-Bankura, J.L. NO- 211,PtOT NO. 817, WARD NO1	NARAYANPUR, KUTUBPUR, WARD NO31, MOUZA-PANPUR, J.L NO 05,DAG NO380(R.S.),843(L.R.), L.R. KH NO-2685, BHATPARA	(KULTI, JAMURIA, ASANSOL,		Champaberia, Ward no. 07,Boangaon	Chowdhury Para Road, Mouza: Halisahar, Ward No. 06, PS. Bizpur, Dis: North 24 Paraganas	Location of the Shelter	
50	50	200		50	50	Capacity of each shelter (beds)	
26.05.2016	26.05.2016	26.05.2016		16.12.2015	16.12.2015	Date of approval	
113.27	134.31	486.92	FIR	120.75	120.75	Total Project cost (Rs. In Lakh)[excluding DPR preparation cost]	New Construction
			FINANCIAL YEAR 2016-17	03.03.2016		Date of Commenceme nt of work	ction
			016-17	31.07.2017		Date of completion	
FY 2018-19	FY 2018-19	FY 2018-19		August, 2017	FY 2018-19	Tentative time of Functionalizati on of shelter	
45.3	53.72	194.8		94.62	48.3	Fund Received by ULB(Rs. in Lakh)	
0	0	0		38.4	0	Total expenditu re incurred (Rs. in Lakh)	
				95%		Physical progress achieved in details (Photograph annexed if applicable)	
Work order issued for construction on 22.05.2017	1 st and 2 nd call was cancelled 3 rd call will be floted soon	Work Order issued for Jamuria & Raniganj (Proposal for site change received for Asansol & Kulti)		will be functional by 01.08.2017	CS of Tender prposal yet to be approved by Technical Committee	Remarks	

23	22	21	20	19	18	17	No. SI	
Tamralipta	Mahestala	Rajpur-Sonarpur	Titagarh	Englishbazar	Uttarpara-Kotrang	Навга	Name of ULB	
WARD NO. 13, J.L. NO. 143, MOUZA: PARBATIPUR, P.S. TAMLUK under TAMRALIPTA MUNICIPALITY	WARD NO. 35, MOUZA: SARAGBAD, J.L. NO. 47, P.S. MAHESTALA under MAHESTALA MUNICIPALITY	WARD NO. 22, MOUZA: MAHINAGAR, J.L. NO. 79 under RAJPUR-SONARPUR MUNICIPALITY	A.P. DEVI ROAD, WARD NO. 06, UNDER TITAGARH MUNICIPAUTY	R.K. Mission Road, Ward No. 08, mouza- Mokdumpur, J.L.No. 68	K.G.T ROAD, WARD NO. 05 UNDER UTTARPARA MUNICIPALITY	BANIPUR, JL. NO.84,LO.P NO.439,MOUZA- ASRAFABAD,WARD NO. 22, HABRA	Location of the Shelter	
50	50	50	50	50	50	50	Capacity of each shelter (beds)	
09.02.2017	09.02.2017	09.02.2017	04.10.2016	04.10.2016	04.10.2016	26.05.2016	Date of approval	7
122.04	118.35	118.33	120.54	115.04	167.51	122,27	Total Project cost (Rs. In Lakh)[excluding DPR preparation cost]	New Construction
							Date of Commenceme nt of work	ction
							Date of completion	
FY 2018-19	FY 2018-19	FY 2018-19	FY 2018-19	FY 2018-19	FY 2018-19	FY 2018-19	Tentative time of Functionalizati on of shelter	
48.82	47.34	47.33	48.21	46.02	67	48.9	Fund Received by ULB(Rs. in Lakh)	
0	0	0	0	0	0	0	Total expenditu re incurred (Rs. in Lakh)	
							Physical progress achieved in details (Photograph annexed if applicable)	
Tender will be floated within July, 2017.	Tender is floated	Tender is floated	Proposal for Land change	CS recevied by SUDA and yet to approve by Technical Committee	Work Order issued by ULB on 12.07.2017	Work order issued by ULB on 14.06.2017	Remarks	

30	29	28	27	26		25	24	No.	
Balurghat	Jiaganj Azimganj	Santipur	Barasat	North Dum Dum		Midnapore	Arambag	Name of ULB	
Ward No. 25, J.L. No. 110, Mouza: Khadimpur, Balurghat, Dist- South Dinajpur	Ward No. 01, J.L. No. 36, Mouza- Panisali, Jiaganj Azimganj, Dist Mursidabad	Ward No. 18, J.L. No. 22, Mouza Santipur, P.S. Santipur, Dist-Nadia	Ward No. 16, Mouza- Banamalipur, J.L. No. 80, Khatian No. 01, Barasat, Dist North 24 Paraganas	Ward No. 09, Mouza-Bandra, J.L. No. 09, Khatian No. 57, North Dum Dum, Dist-North 24 Paraganas		Central Bus stand (existing portion), at WardNo. 03, J.L. NO. 168, Mouza: Cantoment Barpathar, P.S. Midnapur Under Midnapore Municipality	WARD NO. 03, J.L. NO. 37, MOUZA; PASCHIM KRISHNAPUR, under ARAMBAG MUNICIPALITY	Location of the Shelter	
50	50	50	50	50		50	50	Capacity of each sheiter (beds)	
05.06.2017	05.06.2017	05.06.2017	05.06.2017	05.06.2017		09.02.2017	09.02.2017	Date of approval	
122.81	120.69	113.87	116.51	123.05	FIN	98.73	114.87	Total Project cost (Rs. In Lakh)[excluding DPR preparation cost]	New Construction
					FINANCIAL YEAR 2017-18			Date of Commenceme nt of work	ction
					017-18			Date of completion	
FY 2018-19	FY 2018-19	FY 2018-19	FY 2018-19	FY 2018-19		FY 2017-18	FY 2018-19	Tentative time of Functionalizati on of shelter	
49.12	48.27	45.54	46.6	49.4		39.5	45,95	Fund Received by ULB(Rs. in Lakh)	
0	0	0	0	0		0	0	Total expenditu re incurred (Rs. in Lakh)	
								Physical progress achieved in details (Photograph annexed if applicable)	
Soil Test has been done & process for preparationof Detailed Design & Drawing	Soil Test has been done & process for preparationof Detailed Design & Drawing	Soil Test has been done & process for preparationof Detailed Design & Drawing	Soil Test has been done & process for preparationof Detailed Design & Drawing	Soil Test has been done & process for preparationof Detailed Design & Drawing		Work Order Issued by ULB on 12.07.2017	1 st call was cancelled due to insufficient credential of bidders, 2nd call NIT closing date 24.05.2017	Remarks	

	31	SI No.	
	Tarakeswar	Name of ULB	
	Ward No. 10, J.L. No. 29, Mouza: Tarakeswar, Tarakeswar, Dist- Hooghly	Location of the Shelter	
1700	50	Capacity of each shelter (beds)	
	05.06.2017	Date of approval	
4105.34	121.74	Total Project cost (Rs. In Lakh)[excluding DPR preparation cost]	New Construction
		Date of Commenceme nt of work	ction
		Date of completion	
	FY 2018-19	Tentative time Fund expenditu of Received by re Functionalizati ULB(Rs. in on of shelter Lakh) Total expenditu re Lakh)	
2044.59	48.7	Fund Received by ULB(Rs. in Lakh)	
517.03	0		
		Physical progress achieved in details (Photograph annexed if applicable)	
	Soil Test has been done & process for preparationof Detailed Design & Drawing	Remarks	



Format for Monthly status of SUH, a component under DAY- NULM

Name of the ULB: Jalpaiguri Municipality

Status as on July2017

Amount Rs. In Lakh

Location in ward of the Shelter no.10 course para Race Capacity of each shelter (beds) 50 31/07/2015 approval by Date of Rs.84,70,670 (Civil Works) Electrification Cost(with 3% Contingency) Civil & (a) Cost(Cos Utensils Furniture Other Z etc) 2 (b) W.80 Cost Z year per Rs.84,70,670 | 04/01/2016 | 28/07/2017 | 15.36.61 **Total project** (a+6) COST Commencement of work Date of of Completion Expected date 200.31 Central FUND Relieved 12.20 State Total 25.74 48.81 Total= 46.05 Rs. 48.81 Expenditure incurred Total Finishing work all applicable) annexed if tograph details(Pho progress completion. achieved Physical most near

1) Sanctioned amount: 122.04Lacs, 2) Estimated Cost: 8470670.00/-, 3) Tender Amount: 8468129.00/-, 4) Contractual Percentage: 0.03% Less, 5) Tender

No: WBMAD/JM/CH/e-NfT-05(3rd Call)/2015-16 Dated:14/09/2015

Sub-Assistant Engineer

Jalpaiguri Municipality

Jalpaiguri

Executive Engineer 1 17

Municipal Engineering Directorate

Jalpaiguri


Executive Engineer
Jalpaiguri Division M.E.Dte.
Govt. of West Bengal

Jalpaiguri Municipality

Chairman

Jalpaiguri





OFFICE OF THE COUNCILLORS OF

MIDNAPUR MUNICIPALITY

MIDNAPUR

1756 Memo. No.

From: Chairman,

Midnapur Municipality.

To:

Kuntal Mukherjee,

Manipur, Midnapore.

Sub:

Acceptance cum formal work order for Construction of 50Baded Shelter for

Urban Homeless (SUH) at Central Bus Stand under Midnapore Municipality.

Ref:

BID No. WBMAD/ULB/MID/CM/e-NIT-36/ 16-17, BID OPENING DATE

22/05/2017.

Estimated Amount put to tender :Rs.7848122.00

Contractual Percentage

: 25.10% less.

Work Estimated Amount

: Rs. 5878244.00

Sir,

Your tender for the above noted work at your quoted 25.10% less than the schedule of rates with the e-tender

procurement system of Govt. of West Bengal, is hereby accepted by the undersigned.

You are, therefore, requested to execute the formal deed of agreement in 4(four) sets in Municipal Tender Form 2911(ii) on payment of cost of Rs. 500/- per set in cash with all other relevant papers in complete sets within 7(seven) days

on receipt of this order failing which your tender likely to be terminated without further reference.

After execution of formal agreement with the undersigned. You are requested to start the such work and complete the same within 5(five) months from the date of layout in consultation with the Executive Engineer, Midnapore Division, M.E. Dte. You are also requested to submit the work programme matching with the completion date of the work within 7(seven) days from the date of receipt of this letter prior to execution of the work.

No. execution will be allowed until submission of the said work programme.

It should be clearly understood that timely completion of the work is the essence of contract made with you.

Yours faithfully,

Chairman,

Midnapur Municipality

Chaurnar mar Municipalited

Memo. No. 1756 P/11

Copy forwarded for information and necessary action to:-

1) The District Magistrate, Paschim Medinipur.

The Chief Engineer, M.E.D., Bikash Bhawan (1st floor), Salt Lake, Kolkata - 700091.

The S.E. (S), M.E.D., Koushallya, Kharagpur.

The Executive Engineer, Midapore Division, M.E.D., Bidhannagar, Midnapur. He is hereby requested to take up the work of supervision immediately with an intimation to that effect to the undersigned.

The Asstt, Labour Commissioner, Midnapore Sadar, RLO, Midnapur.

6) Asstt. Engineer, Midnapore Municipality.

7) Sub-Asstt. Engineer (H. Khan), Midnapore Municipality.

8) The Executive Officer, Midnapore Municipality.

9) The F.O., Midnapore Municipality

10) The Accit. Midnapore Municipality.

11) The Cashier, Midnapore Municipality.

Chairman, Midnapur Municipality.

Chairma

Recenod

Format for Monthly status of SUH, a component under DAY-NULM

Durgaper Municipal Corporation

Name of the ULB

Status as on, 30.06.2017

Amount Rs. in Lakh.

Hoperson of the state of the st	A PROPERTY.	(permanent electric & water connection ele still to be completed;	
Total expenditure incurred a			70.61
NAME OF TAXABLE PARTY.		10 11 10 10	93.26
State Total		22,23.	37.3
Central		35.99	55.96
tracepted Central date of completering		completed	
Date of Commence meet of Work	NA BANG	20 05.2015 Arready as NOC complet received from ADDA vide memo nc. ADDA/DGP /PC A10/1415/1 0085 dt. 20 5.2016	
Total Cosmes Project received		150 05 lacs (GOI= 112.46 and GOWB= 37.59	
O&M Cost per yest		6.02lakhs (Total O & M Cost for five year= 30 10 lakhs)	
Others Cost Kost of Uninview		16.40 lakhs	
Date of Chestas approval by a Cost With		06 09.2014 103.56 lakhs vice memb no SUDA-23/20:4/15 48 48 (1) dt. 06 09 2014	
cach spicore bac of steller spicore by		06 09.2014 vide memo no SUDA- 23/2014/15 48 (1) dt. 06 09 2014	
Capacity of each shelter	(beds)	50 beds	
Location of the pack Shoker theids		Urban Shetter within DMC site at Muchipara. Bidhannagar. Durgapur	

Asst. Engineer

pupared of the conferred conference Durgagut Muerran Mesporation

Asansoi Divn M.E FiTE Executive Engineer Govt. of W.B

> Durgapur Municipal Corporation Finance Officer Durgapur Municipal Corporation

Finance Officer,

Durgapur Municipal Corporation Commissione

#

Durgaour Pannina Corporation Commissioner



Details of Shelters (Under DAY-NULM)

			Sanctioned					Functional	al	
FY	New	Refurbishment	O&M	Total	Capacity	New	Refurbishn O&M		Total	Capacity
2014-15	3	0	0	3	150	0	0	0	0	0
2015-16	10	0	0	10	200	0	0	0	0	0
2016-17	15	0	0	15	750	1	0	0	0	50
2017-18	9	0	0	9	300	2	0	0	0	100

Total Shelters sanctioned under DAY-NULM Total Shelters functional under DAY-NULM

34

Total Shelters functional other than DAY-NULM :41

mail.google.com/mail/u/0//?ui=2&ik=caac2a76a4&view=pt&... Gmail - Urgent information on Shelters for Supreme Court Committee



Urgent information on Shelters for Supreme Court Committee

Wed, Jun 21, 2017 at 5:30 PM

Director SULM <wbsulm@gmail.com>

Yogendra Awana <dir-nulm@gov.in>

wbsulm@gmail.com, nulm.chd@gmail.com, mc.samajiksuvidhasangam@gmail.com pdlsgrajasthan@gmail.com, suda.haryana@yahoo.co.in, mdmepma.ts@gmail.com, karnataka.sulm@gmail.com, To: mdmepma@apmepma.gov.in, nulmmaharashtra@gmail.com, punjabsulm@gmail.com,

Cc: rakessh.nulm@gmail.com

Sir/Madam,

1. It has been brought to the notice that there are some problems in filling up data of shelter in online

Supreme Court a format has been devised which is attached herewith. 2. However, keeping in view the urgency for availability of data for preparation of report for Hon'ble

3. The information in the format may be provided urgently by 22nd June, 2017 (11.00 AM) positively.

regards,

Yogendra Singh Awana

Deputy Secretary to Govt. of India

Format for Details of SUH Status.xlax

Details of Shelters (Under DAY-NULM)

			Sanctioned	-				Emertional	-	The state of the s
	Nicon	D. E. L. T.	1					מונינוסו	2	
	MEM	New Returbishment O&M	OWM	Total	Capacity New	New	Refurbisher O.M. Total	O.S.A.	Total	:
717								OCIA	Oral	Lapacity
CT-4-TO		221								
4.0										
7015-16										
				_						
2016.17										
\T-0.										
1 10										
701/-18										

Total Shelters sanctioned under DAY-NULM Total Shelters functional under DAY-NULM

Total Shelters functional other than DAY-NULM

HOWRAH MUNICIPAL CORPORATION

Central Office: 4, Mahatma Gandhi Road, Howrah-711101



102/90 VIOZ/90



To, The Director, SUDA & Mission Director WBSULM

Sub: Submission of Monthly Status Report of SUH

Sir,

The Monthly Status Report of SUH for the month of May & April is enclosed herewith for

kind perusal.

Kindly find the report.

Commissioner 13/6/1

Howrah Municipal Corporation

HOWRAH MUNICIPAL CORPORATION
Monthly Status of SUH, a component under DAY-NULM
FOR THE MONTH OF APRIL, 2017

						ME				
Physical progress achieved in details (photograph annexed if applicable)	1" Floor Roof casted, 2" Floor Roof casted & 3" Floor Roof Casted		Account to a				And the second s			
Total expenditur e incurred	26,97,271								V	
Fund received (Lakhs) Central State Total	50 (As advance for shelters)	And the last of th	The second secon							
Fund										
Excepted date of completion	01.08.2017						the control of the co			
Date of Commentm ent of Work	01.08.2016	The state of the s	And the state of t							
Total Project Cost (a+b) (in Lakhs)	115.895									22
O & M cost per year	6.02									
Other cost (cost of utensiles and furniture's etc.) b (in Lakhs)	8.705		And the second s							1
Civil & Electrification cost (with 3% contingency) a (in Lakhs)	107.19		And And part of the second of place and required to the part of th						The state of the s	/
Date of Approval by Hon'ble Mayor, · H.M.C.	20.08.2016			,					perfection and remainment of the extension	
Capacity of each Shelter (beds)	20		4							
Name of the shelter	9, Kolpukur Iane									
15 · S o	-				AP-11-11-10					

COMMISSIONER HOWBAH MUNICIPAL CORPORATION

EXECUTIVE Engineer

NULLY VANDALISM M.E. Directorate, Deptt. of M.A.

SATERIT PROJECT CORPORATION

GOVI. of West Bengal

HOWRAH MUNICIPAL CORPORATION

husenfoly:7

Monthly Status of SUH, a component under DAY-NULM HOWRAH MUNICIPAL CORPORATION

FOR THE MONTH OF MAY, 2017

Physical progress achieved in details (photograph annexed if	applicable) 1" Floor Roof Casted, 2" Floor Roof casted, 3" Floor Roof Casted, 4" Floor Roof has been casted.	A PACK A THE REAL PROPERTY OF THE PACK A PAC			ION
Total expenditur e incurred	26,97,271				IONER AL CORPORAT
Fund received (Lakhs) Central State Total	93.40(As advance for 2 shelters]				COMMISSIONER HOWRAH MUNICIPAL CORPORATION
Excepted date of completion	01.08.2017				Jet 17 neer on A.
Date of Commentm ent of Work	01.08.2016				45 Luter 146413 Executive Engineer Magnetic Directorate, Deptt. of M.A.
Total Project Cost (a+b) (in Lakhs)	115.895				. 2
O & M cost per year	6.02				SHURY SHURY
Other cost {cost of utensiles and furriture's etc.} b (in Lakhs)	8,705				AIRANUMHOWDHURY
Civil & Electrification cost (with 3% contingency) a (in Lakhs)	107.19				Name of the second
Date of Approval by Hon'ble Mayor, H.M.C.	20,08,2016				SORATION
Capacity of each Shelter (beds)	20				E.E. VICIPAL CORP
Name of the shelter	9, Koipukur kane				E.E. HOWRAH MUNICIPAL CORPORATION
2 - 50					OF THE PARTY OF



GOVT. OF WEST BENGAL OFFICE OF THE EXECUTIVE ENGINEER COOCH BEHAR DIVISION MUNICIPAL ENGINEERING DIRECTORATE DEPARTMENT OF MUNICIPAL AFFAIRS

P.O & Dist.- Cooch Behar. PIN - 736101. Phone: (03582) 230743, E-Mail: coochbehardivnmed@gmail.com

Memo No. ME / COB/

/ NULM-2/15, Pt.I

Date: 08.06.2017

From:- Executive Engineer,

Cooch Behar Division.

M.E. Directorate.

To:- The Chief Engineer,

Municipal Engineering Directorate,

Bikash Bhavan, 1st Floor,

Salt Lake City, Kolkata - 700 091.

Sub:- Submission of Monthly Status Report for "Construction of 50 Bedded Shelter for Urban Homeless (SUH) Building at Cooch Behar under DAY-NULM as on 25th May'2017 under Cooch Behar Municipality.

Ref No.- Chairperson's letter Memo No. PWD / 379 /17, Dated 06-06-2017

Sir,

Enclosed please find herewith the Monthly Status Report for "Construction of 50 Bedded Shelter for Urban Homeless (SUH) Building at Cooch Behar under DAY-NULM" as on 25th May'2017 under Cooch Behar Municipality.

This is for favour of your kind perusal and necessary action, please.

Enclo: -As stated above.

Yours faithfully,

Executive Engineer.

Cooch Behar Division, M.E. Dte.

Date: 08.06.2017

Memo No. ME / COB/ 662(1) / NULM-2/15, Pt.I

Copy forwarded for kind information to :-

1. The Director, State Urban Development Agency (SUDA), "ILGUS" Bhavan, H-C Block, Sec-III, Kolkata-106- along a copy of the same.

2. The Superintending Engineer, North Circle, M.E. Dte., Siliguri. -along a copy of the same.

3. The Chairperson, Cooch Behar Municipality - along a copy of the same.

Cooch Beharin

CONST. OF SUH BUILDING UNDER DAY-NULM AT COOCH BEHAR

the	
of the	

COOCH BEHAR MUNICIPALITY

Status as 5/25/2017 on:

Shantiban, 50 Ward No. 10	Capacity of each Shelter (beds)
7/31/2015	Date of approval by PSC
106.45	Civil & Electrification Cost (in Lakh) (With 3% Contingency)
16.57	Others Cost { in Lakh} (Cost of utensiles & Furniture etc.) b
6.02	O&M Cost per year (in Lakh)
123.02	Total Project cost (a+b) (in Lakh)
18/01/2016	Date of Commencement of Work
30.06.2017	Excepted date of completion
64.76	Fund re Central
30.86	Fund received (in Lakh) entrai State Tota
95.62	Total
Rs. 74.32	Total expenditure incurred (in Lakh)
All structural works are almost completed. Three side plastering completed. Elecrification work is going on.	Physical progress achieved in details (Photograph annexed of applicable)

Sub-Assistant Engineer
Cooch Behar Municipality
Cooch Behar Municipality
Cooch Behar Municipality
Cooch Behar Municipality

Cooch Behar Municipality
Cooch Behar Municipality
Cooch Behar Municipality
Cooch Behar Municipality

Cooch Behar Municipality
Clast Behar Municipality
Cooch Behar Municipality
Cooch Behar Municipality

MEDICE, COOCE BETH CHIERTH CONTROL OF WEST BENGAL
GOAL OF WEST BENGAL

HOWRAH MUNICIPAL CORPORATION

Monthly Status of SUH, a component under DAY-NULM FOR THE MONTH OF MAY , 2017

March 25 (1971)	15.4		
Market Hard To .			
MANUAL DE		→	02.50
A STATE OF HOWRAH MUNIC		9, Koipukur lane	Name of the shelter
HOWRAH MUNICIPAL CORPORATION		50	Capacity of each Shelter (beds)
RPORATION		20,08.2016	Date of Approval by Hon'ble Mayor, H.M.C.
		107,19	Civil & Electrification cost (with 3% contingency) a (in Lakhs)
C.P.O. C.P.O.		8.705	Other cost (cost of utensiles and furniture's etc.) b (in Lakhs)
TO HURY ER (MILM). ERPORATIO		6.02	O & M cost per year
Exer Ha M.E. Dire Gov		115.895	Total Project Cost (a+b) (In Lakhs)
Executive Engineer Hanginy Division M.E. Directorate, Deptt. of M.A. Govt. of West Bengal		01.08.2016	Date of Commentm ent of Work
네쉬가 ineer sion ptt. of M.A. Bengal		01.08.2017	Excepted date of completion
COMMISSIONER HOWRAH MUNICIPAL CORPORATION		93.40(As advance for 2 shekters)	Fund received (Lakhs) Central State Total
COMMISSIONER MUNICIPAL CORPORA		26,97,271	Total expenditur e incurred
NOIF		1st Floor Roof casted, 2nd Floor Roof casted, 3nd Floor Roof Casted, 4nd Floor Roof has been casted.	Physical progress achieved in details {photograph annexed if applicable}

The Court of the C	
	Location of the Studior
8	Capaci Stacks) System S
16.12.2015	Date of by 95%
111.14	Covil & Electrifit assion Covil & [west of said for said
13.13	Others cost (Cost of Utensiles & Furniture esc.)b
6.02	OBM Cost
124.27	Costs Code Long Long Long Long Long Long Long Long
04.03.2016	Commence meant of work
180 days (As per Bar Chart Dated- 31,07,2017)	
36.43+21.53=57.96	Contral
12.14+26.50=38.64	Family reconsed
96.60	i i
38.4+11.74=50.14	Secondary London
Photograph enclosed	Physical progress actioned in the call special
Sac Charge Freezest (Sac Sac Charge Freezest (Sa Sac Sac Charge Freezest (Sa Sac Sac Sac Sac Sac Sac Sac Sac	Name of the last o

Format for Monthly status of SUH, a component under DAY-NULM Bongaon Municipality

Name of the ULS:

Amountly, whiteh

Status as 69 31.05 2017

The Contract of the Contract o

Format for Monthly status of SUH, A component under DAY-NULM Construction of 50 Beded Shelter at Kutir Math, Chandannagar

Name of OLB	Chandernagore							Status as on :	7:			
	The second secon											Amount Rs. In Lakh.
Conscievati		CIVII &	Other Cost					Fu	Fund Received	D		
Location of Sheiter Sheiter (beds)	approval by Cost (With 3% PSC contingency)	The same of the sa	(Cost of utensiles & Furniture etc.)	O & M Cost per year	Total Project Cost (a + b)	Total Date of Project Cost, comencement of (a + b) work	Expected date of completion	Central	State	Total	Total Expenditure incurred	Physical Pogress achieved in details (Photograph annexed if applicable)
KUTHIR MATH, CHANDERNAGORE 50 16	16-12-2015	108.28	16.68	6.02	124.96	15-11-2016 15-12-201	15-12-2017	36.23	12.08	48.30	48.30 7.53	Ground Floor Roof Casting

Executive Engineer

41 Harrosun

Municipal Engineering Department

Executive Engineer
Hooghly Division
M.E. Directorate, Deptt. of M.A.
Govt. of West Bengal

Chandernagore Municipal Corporation

Chandernagore (



রাজ্য নগর উন্নয়ন সংস্থা STATE URBAN DEVELOPMENT AGENCY



"ইলগাস ভবন", এইচ-সি ব্লক, সেক্টর-৩, বিধাননগর, কলকাতা-৭০০ ১০৬, পশ্চিমবঙ্গ "ILGUS BHAVAN", H-C Block, Sector - III, Bidhannagar, Kolkata - 700 106, West Bengal

ক্রমিক নং SUDA- 23/2014(Pt)/ 40/8

07.06.2017

From: Adl. Director, SUDA

& Adl. Mission Director, WBSULM

To: Chairman,

Bhatpara Municipality

Sub: Present progress of Shelter for Urban Homeless (SUH) under DAY NULM

Sir,

You may be aware that Committee as constituted by Supreme Court recently visited our state on 03.5.2017 to review the progress of Shelter for Urban Homeless (SUH) under DAY-NULM of the State. Committee suggested to complete the construction of sanctioned SUH as early as possible as per timeline mentioned in the DPR.

A 50 bedded **Shelter for Urban Homeless (SUH)** unit was sanctioned by Project Sanction Committee (PSC) in its 6 th meeting held on 26.05.2016 with an amount of Rs. 134.31 Lakh in favour of your ULB. Fund for the tune of Rs. 53.72 Lakh was released in favour of your ULB vides memo no. 23/2014(Pt)/ 1048 dated: 19.07.2016.

From the record it is noticed that any physical progress of construction work is not reported to this office till now.

You are therefore requested to comply with the suggestion of Hon'ble Committee.

Yours faithfully,

Adl. Director, SUDA

& Adl. Mission Director, WBSULM

Memo No. SUDA/23/2014(Pt)/ 498/1(1)
Copy forwarded for information to Chief Engineer, MED

Date: 07.06.2017

0/0

Adl. Director, SUDA & Adl. Mission Director, WBSULM

Tel: 2358 6403/5767, Fax: 2358 5800, E-mail: wbsudadir@gmail.com

Account Section: 2358 6408



Memo No / 15 /PW/Eng/2017

Date 25/ 05/2017

ACCEPTANCE CUM WORK ORDER

To.

GANAPATI BISWAS

Bogra.

Mobile No. 9434675204

Sub

: Work order for Construction of 50 Beded four Storied Shelter for

Urban Homeless at Jamuria, Under NULM.

E-Tender Notice No

263/PW/Eng./16

Date. 28/11/2016.

Estimated Amount

Rs. 99, 52,403/-

Tender Amount

Rs. 84, 04,804/-

Sir.

Your tender for the above mentioned work of the Estimated Amount Rs. 99,52,403 (Rupees Ninety-nine Lakh fifty-two Thousand four Hundred three) only & your quoted rate @ 15.55% (Fifteen point fifty-five Percent) BELOW resulting the Tender Amount to Rs. 84, 04,804/- (Rupees Eighty-four Lakh four Thousand eight Hundred four) only is hereby accepted by undersigned & you are asked to start the work in consultation with Executive Engineer, Asansol Division, M.E.Dte, Asansol immediately.

You are now requested to purchase the agreement documents in duplicate @ Rs. 2505/- per set from this office & submit the same alongwith all other relevant documents & also have to deposit the balance amount of earnest money, if required, within 7 (seven) days from the date of receipt of this letter, failing which action as deemed fit under the contract agreement may be initiated against you

The date of issue of work order should be treated as date of commencement of work. The completion time of work is 12 (Twelve months)

Memo No /10/PW/Eng./2017

Date / /201

Asansol Municipal Corporation

Secretary

Asansol Municipal Corporation

Copy forwarded for information to :-

1. Hon.ble Mayor, Asansol Municipal Corporation

2. Commissioner, Asansol Municipal Corporation

3. The Chief Engineer, M.E. Directorate, Bikash Bhavan, Salt Lake, Kolkata-91.

4. The Superintending Engineer, West Circle, M.E. Directorate, Patal Bazar, Burdwan.

5. The Additional District Magistrate, Asansol

6. The SDM, Asansol.

7. Sri Sukamal Mondal, Superintending Engineer. Asansol Municipal Corporation.

8. R.O., Asansol Municipal Corporation.

9. Executive Engineer M.E.Dtc., Asansol Division, Asansol.

10. S.A.E. , Asansol Municipal Corporation.

Secretary
Asansol Municipal Corporation

105 17 Post 7





Office of the Asansol Municipal Corporation Asansol :: Burdwan.

Memo No //6 /PW/Eng/2017

Date 25/05/2017

ACCEPTANCE CUM WORK ORDER

To,

M/S. NAG CONSTRUCTION

Mobile No.

Sub

: Work order for Construction of 50 Beded four Storied Shelter for

Urban Homeless at Raniganj, Under NULM.

E-Tender Notice No

263/PW/Eng./16

Date. 28/11/2016.

Estimated Amount

Rs. 99, 52,404/-

Tender Amount

Rs. 80, 73,390/-

Sir,

Your tender for the above mentioned work of the Estimated Amount Rs. 99, 52,404 (Rupees Ninety-nine Lakh fifty-two Thousand four Hundred three) only & your quoted rate @ 18.88% (Eighteen point eighty-eight Percent) BELOW resulting the Tender Amount to Rs. 80, 73,390/- (Rupees Eighty Lakh seventy-three Thousand three Hundred ninety) only is hereby accepted by undersigned & you are asked to start the work in consultation with Executive Engineer, Asansol Division, M.E.Dte, Asansol immediately.

You are now requested to purchase the agreement documents in duplicate @ Rs. 2505/- per set from this office & submit the same alongwith all other relevant documents & also have to deposit the balance amount of earnest money, if required, within 7 (seven) days from the date of receipt of this letter, failing which action as deemed fit under the contract agreement may be initiated against you.

The date of issue of work order should be treated as date of commencement of work. The completion time of work is 12 (Twelve months)

Memo No______/9/PW/Eng./2017
Copy forwarded for information to :-

Date ____/2017 week

Asansol Municipal Corporation

Hon.ble Mayor, Asansol Municipal Corporation
 Commissioner, Asansol Municipal Corporation

.

Secretary
Asansol Municipal Corporation

- 3. The Chief Engineer, M.E. Directorate, Bikash Bhavan, Salt Lake, Kolkata-91.
- 4. The Superintending Engineer, West Circle, M.E. Directorate, Patal Bazar, Burdwan.
- 5. The Additional District Magistrate, Asansol
- 6. The SDM, Asansol.
- 7. Sri Sukamal Mondal, Superintending Engineer, Asansol Municipal Corporation.
- 8. R.O., Asansol Municipal Corporation.
- 9. Executive Engineer M.E.Dte., Asansol Division, Asansol.
- 10. S.A.E. , Asansol Municipal Corporation.

TO SEAL CORRECTION

Secretary
Asansol Municipal Corporation

K.VA.M.C. Toroche Cott. Work codes 2016-17/2016-17/201790-43-0-Tamber91-T 201-da



OFFICE OF THE MUNICIPAL COUNCILLOR

BANKURA MUNICIPALITY BANKURA

Memo no: 618/VIII-14

To, Kartick Sen Raigram, Bankura 2598 29 MAY 2017 Arsgjosfre

Sub:- Acceptance cum work order for the work for Construction of 50 bedded five storied building and ancillary work for shelter for Urban homeless within jurisdiction of Bankura Municipality under NULM. Lay Out Plot No.- 817(R.S.), Mouza – Bankura, JL No.-211 Bankura.

Ref. No.: - NIT No. WBMAD/CM/BM/24/NULM/2016-2017 of office memo no-3106/VIII-14 dated:-21/01/2017.

Tender ID: - 2017 MAD 99513 1.

Estimated Amount put to Tender: - Rs. 184, 07, 355.00 (Rupees One Crore eighty four lakhs Seven thousand three hundred and fifty five and paisa zero zero) only.

Tender Amount: - 13.95% below the amount put to tender i.e. **15839528.79** (Rupees One Crore Fifty Eight Lakh Thirty Nine Thousand Five Hundred and Twenty Eight and paisa seventy nine) only.

Sir.

The undersigned is informed you that your above quoted rate for the above mentioned work is found lowest and accepted.

So, you are therefore requested to execute the Formal Agreement of the work in triplicate in W.B.F.2911(ii), within ten days from the date of issuance of this work order, failing which your work order is likely to be cancelled without any correspondence and the earnest money already deposited by you (converted into security deposit) will be forfeited by this municipality.

The date of commencement is reckoned from the date of issuance of this work order and you are therefore requested to start the aforesaid work immediately in consultation with the consultation with the Executive Engineer, Municipal Engineering Directorate, Bankura Division and complete the same in all respect within the stipulated time period as mentioned in NIT (i.e. 550 days) from the date of issuance of this work order positively.

Further, you are requested to kindly submit a work programme before starting the work keeping in mind that, "this is the essence of the contract"

Thanking you.

Chairman
Bankura Municipality.

Memo no:- 618 (10)/ VIII -14, Dated: 22-05-2017

Copy forwarded for information to:

1. The District Magistrate, Bankura, P.O. & Dist. Bankura.

7. The Director, SUDA, Illgus bhavan

- 3. Hon'ble Member Chairman-in-Councill (P.W.D). Bankura Municipality.
- 4. The Chief Engineer, M.E. Dte., Bikash Bhavan, Slatlake, Kol-91
- 5. The Superintending Engineer (S.C.) M.E. Dte. Kousallya, Kharagpur, Paschim Midnapur
- 6. The Executive Engineer, M.E. Dte. Kenduadihi, Bankura
- 7. Executive Officer, Bankura Municipality.
- 8. Head clerk, Bankura Municipality.
- 9. Accountant, Bankura Municipality
- 10. Respective file.

Charman

Bankura Municipality.

Chairman Bankura Municipality

Format for Monthly status of SUH, A component under DAY-NULM Construction of 50 Beded Shelter at Kutir Math, Chandannagar

Status as on :
oration of Shelter Capacity of Date of Civil & Other Cost O & M Cost Total Date of Expected Fund Received Total
Electrification (Cost of per year Project Cost comencement of date of Central State Total Ext
UTHIR MATH, 50 16-12-2015 108.28 16.68 6.02 124.96 15-11-2016 15-12-2017 36.23 12.08 48.30 7.53

Municipal Engineering Department
Executive Engineer
Hooghly Division
Hooghly Division
M.E. Directorate. Pentt. of M.A.
Govt. of West Congail

Executive Engineer

Reshma.

Chandernagore Municipal Corporation

Mayor Chandernagore Municipal Corporation

WEST BENGAL STATE URBAN LIVELIHOOD MISSION

(Under Municipal Affairs Department, Government of West Bengal)
"ইলগাস ভবন", এইচ-সি রুক, সেকটর-৩, বিধাননগর, কলকাতা ৭০০ ১০৬, পশ্চিমবন্ধ।
"ILGUS BHAVAN", H-C Block, Sector-III, Bidhannagar, Kolkata 700 106, West Bengal.

SUDA-23/2014/ 405

Date: 25/05/2017

Memorandum

Release of funds of Shelter for Urban Homeless under DAY-NULM

Funds are shown herein are being released electronically in favour of under mentioned Municipality of Shelter for Urban Homeless under DAY-NULM as 2nd installment.

SL		Amount (Rs	s. In Lakh)	
NO.	Name of ULBs	Central Share	State Share	Total
[1]	[2]	[3]	[4]	[5]
1.	Durgapur MC	19.97	25.30	45.27

Finance Officer, SUDA

দুরভাব্ধ ২৩৫৮ ৬৪০৩/৬৪২ ১/৫৭৬৭, ক্যান্ন : ২৩৫৮৫৮০০

Tel: 2358-6403/6421/5767, Fax: 2358-5800, E-Mail: wbsulm@gmail.com

The release of funds subject to the following conditions-

- The fund should be utilized only for the approved components of the Project and within ceiling limits of approved cost.
- 2. The execution of the Schemes should be strictly as per the Procedure laid down in Govt. Order No. 329/MA/C-10/3S-22/2013 Dated 04.05.2015 (Copy enclosed) for implementation of Shelters under NULM with MED as the Technical Support Agency.
- 3. Monthly report of Physical and Financial Progress should be sent to SUDA and MED by the 7^{th} of the following month.
- 4. The amount released herein should be kept in the dedicated Bank Account for NULM since opened by the ULB.
- 5. A Subsidiary Cash Book should be maintained for keeping accounts (deposits and withdrawals) of funds.
- 6. Money receipt in Form 42 may be sent immediately after receiving the fund.
- 7. No fund should be utilized for any purpose other than for which the amount is released.
- 8. Utilisation certificate on achieving 70% plus expenditure of the amount released herein and earlier vide no. SUDA-23/2014/250 dt. 31.03.15 should be submitted in prescribed proforma duly authenticated by MED for release of subsequent installment.

Finance Officer, SUDA

No. SUDA-23/2014/1(5)

25.5.2017

Copy for information to:

- 1. The Chairman Durgapur MC. He/she is requested to verify the respective Bank Account of the ULB in respect of NULM that the amount released in this Memorandum is duly credited. It may kindly be ensured that all money receipts against previous releases by SUDA have been submitted.
- 2. Secretary, UD&MA. Dept. Govt. Of West Bengal.
- 3. Chief Engineer, M.E. Directorate.
- 4. Director, SUDA.
- 5. Additional Director, SUDA.

Finance Officer, SUDA

10 fostupan. 2017

ofe

WEST BENGAL STATE URBAN LIVELIHOOD MISSION

(Under Municipal Affairs Department, Government of West Bengal)

"ইলগাস ভবন", এইচ-সি ব্লক, সেকটর-৩, বিধাননগর, কলকাতা ৭০০ ১০৬, পশ্চিমবঙ্গ।
"ILGUS BHAVAN", H-C Block, Sector-III, Bidhannagar, Kolkata 700 106, West Bengal.

SUDA-23/2014/ 405

Date: 25/05/2017

Memorandum

Release of funds of Shelter for Urban Homeless under DAY-NULM

Funds are shown herein are being released electronically in favour of under mentioned Municipality of Shelter for Urban Homeless under DAY-NULM as 2nd installment.

SL		Amount (Rs	s. In Lakh)	
NO.	Name of ULBs	Central Share	State Share	Total
[1]	[2]	[3]	[4]	[5]
I.	Durgapur MC	19.97	25.30	45.27

Finance Officer, SUDA

দুরভাষ: ২৩৫৮ ৬৪০৩/৬৪২ ১/৫৭৬৭, ফ্যাক্স: ২৩৫৮৫৮০০

Tel: 2358-6403/6421/5767, Fax: 2358-5800, E-Mail: wbsulm@gmail.com

The release of funds subject to the following conditions-

- 1. The fund should be utilized only for the approved components of the Project and within ceiling limits of approved cost.
- 2. The execution of the Schemes should be strictly as per the Procedure laid down in Govt. Order No. 329/MA/C-10/3S-22/2013 Dated 04.05.2015 (Copy enclosed) for implementation of Shelters under NULM with MED as the Technical Support Agency.
- 3. Monthly report of Physical and Financial Progress should be sent to SUDA and MED by the 7th of the following month.
- 4. The amount released herein should be kept in the dedicated Bank Account for NULM since opened by the ULB.
- 5. A Subsidiary Cash Book should be maintained for keeping accounts (deposits and withdrawals) of funds.
- 6. Money receipt in Form 42 may be sent immediately after receiving the fund.
- 7. No fund should be utilized for any purpose other than for which the amount is released.
- 8. Utilisation certificate on achieving 70% plus expenditure of the amount released herein and earlier vide no. SUDA-23/2014/250 dt. 31.03.15 should be submitted in prescribed proforma duly authenticated by MED for release of subsequent installment.

Finance Officer, SUDA

No. SUDA-28/2014/1(5)

25. 5.2017

Copy for information to:

- 1. The Chairman Durgapur MC. He/she is requested to verify the respective Bank Account of the ULB in respect of NULM that the amount released in this Memorandum is duly credited. It may kindly be ensured that all money receipts against previous releases by SUDA have been submitted.
- 2. Secretary, UD&MA. Dept. Govt. Of West Bengal.
- 3. Chief Engineer, M.E. Directorate.
- 4. Director, SUDA.
- 5. Additional Director, SUDA.

Finance Officer, SUDA



রাজ্য নগর উন্নয়ন সংস্থা



STATE URBAN DEVELOPMENT AGENCY

''ইলগাস ভবন'', এইচ-সি ব্লক, সেক্টর-৩, বিধাননগর, কলকাতা-৭০০ ১০৬, পশ্চিমবঙ্গ "ILGUS BHAVAN", H-C Block, Sector - III, Bidhannagar, Kolkata - 700 106, West Bengal

	SUDA-23/2014/	367
_		

22.05.2017 তারিখ

From: Director, SUDA

To

: The Manager,

State Bank of India.

Salt Lake City, Kolkata - 700 091.

Sub: Electronic Transfer of Fund debiting this office Current Account No. 34061121921.

Construction of Shelter for Urban Homeless under NULM

Sir.

You are requested to kindly arrange for electronic transfer of funds as per details given below debiting the amounts from this office Current Account No. 34061121921 lying with your branch in respect of Construction of Shelter for Urban Homeless under NULM

Sl. No.	Name of Payee	Amount (In Rs.)	Payees' Bank Details
01	Durgapur Municipal Corporation	45,27,000.00	Allahabad Bank, City Centre Branch, A/C No. 50310508645, IFS Code. ALLA0211764
	TOTAL	45,27,000.00	

(Md Asif Sardar) Finance Officer **SUDA**

(Amalendu Sekhar Naskar) Addl. Director & FA

3Mms

SUDA

ারভাষ ঃ ২৩৫৮ ৬৪০০ / ৫৭৬৭, ফ্যাক্স ঃ ২৩৫৮ ৫৮০০

Tel: 2358 @ 03/5767, Fax: 2358 800, E-mail: wbsud@lr@gmail.com

Account Section: 2358 6408



রাজ্য নগর উন্নয়ন সংস্থা



STATE URBAN DEVELOPMENT AGENCY

"ইলগাস ভবন", এইচ-সি ব্লক, সেক্টর-৩, বিধাননগর, কলকাতা-৭০০ ১০৬, পশ্চিমবঙ্গ "ILGUS BHAVAN", H-C Block, Sector - III, Bidhannagar, Kolkata - 700 106, West Bengal

SUI	DA-23/2014/	367
-		

22.05.2017

ক্রমিক নং

তারিখ

From: Director, SUDA

To

: The Manager,

State Bank of India,

Salt Lake City, Kolkata - 700 091.

Sub: Electronic Transfer of Fund debiting this office Current Account No. 34061121921.

Construction of Shelter for Urban Homeless under NULM

Sir.

You are requested to kindly arrange for electronic transfer of funds as per details given below debiting the amounts from this office Current Account No. 34061121921 lying with your branch in respect of Construction of Shelter for Urban Homeless under NULM

Sl.	Name of Payee	Amount	Payees' Bank Details
No.		(In Rs.)	
01	Durgapur Municipal Corporation	45,27,000.00	Allahabad Bank, City Centre Branch, A/C No. 50310508645, IFS Code. ALLA0211764
	TOTAL	45,27,000.00	

(Rupees Fourty five lakh twenty seven thousand only)

(Md Asif Sardar) Finance Officer SUDA (Amalendu Sekhar Naskar) Addl. Director & FA

SUDA Jakuman. 12.05. 2014.

দূরভাষ ঃ ২৩৫৮ ৬৪০৩ / ৫৭৬৭, ফ্যাক্স ঃ ২৩৫৮ ৫৮০০

Tel: 2358 6403/5767, Fax: 2358 5800, E-mail: wbsudadir@gmail.com

Account Section: 2358 6408

Shall Sharpy 18



DURGAPUR MUNICIPAL CORPORATION

CITY CENTRE, DURGAPUR - 713216, DIST. - BURDWAN

EPABX ⇒ (0343) 2545842, 2546994, 2546107 * Mayor : 2545828 * Fax No. : 254-6472 Website : durgapurmunicipalcorporation.org * E-mail : durgapurcorporation@gmail.com

Ref. No. DMC 1 565 15.8....

Date 13/4/17

To
The Director,
Suda & Mission Dicertor, WBSULM
ILGUS Bhavan,
H-C Bl,Sec-III, Bidhannagar
Kolkata-700106

Sub: Claim letter for 50- beded Shelter for Urban Homeless at Durgapur.

Sir,

We have got Rs. 47.99 lakh as 40% of total project cost amounting Rs. 119.95 lakh (including DPR preparation cost) for 50-beded Shelter for urban Homeless (SUH) unit in favour of Durgapur Municipal Corporation. Out of Rs. 47.99 lakh, we have already utilized Rs. 44.62 lakh and remain rest amount Rs. 3.37 lakh. The UC has been submitted to you on 02.01.2017.

So, you are requested to release the 2nd installment of next sanctioned amount for the SUH unit.

Thanking you.

Yours faithfully,

Commissioner,

Durgapur Municipal Corporation

DURGAPUR MUNICIPAL CORPORATION

CITY CENTRE, DURGAPUR - 713216, DIST. - BURDWAN

EPABX ⇒ (0343) 2545842, 2546994, 2546107 * Mayor : 2545828 * Fax No. : 254-6472 Website : durgapurmunicipalcorporation.org * E-mail : durgapurcorporation@gmail.com

Ref. No. DMC 15474750

Date 2/01/17

From

: The Commissioner

Durgapur Municipal Corporation

To

: The Director,

State Urban Development Agency,

'ILGUS BHAVAN', H-C Block, Sector-III

Bidhananagar, Kolkata-106

Sub

: Utilization Certificate for Shelter for Urban Homeless

Sir,

With reference to the above, I am to submit herewith the utilization certificate for Shelter for Urban Homeless in FORM GRF 19-A form of utilization certificate, for favour of your necessary action please.

Thanking you.

Yours faithfully,

Q 2000

Commissioner

Durgapur Municipal Corporation

Encl: As stated above.

FORM GRF 19-A (See Rule 212(1) FORM OF UTILISATION CERTIFICATE

SI NO.	Letter No. & Date	Amount in Lakh	Central Share	State Share
	1 SUDA -23/2014/1258 dt. 21.09.2015	47.99	35.99	12
	Total	47.99	35.99	12

Certified that out of Rs. 47.99 of grants-in-aid sanctioned during the years 2015-16 in favour of Durgapur Municipal Corporation under this Ministry/Department letter No. given in the margin and Rs.nil on account of unspent balance of the previous years, a sum of Rs.44.62 lakh has been utilized for the purpose of Const. of 50 beded shelter for urban homeless for which it was sanctioned and that the balance of Rs.3.37 lakh remaining un utilized at the end of the year has been surrendered to Governmentn(vide No....dt.) will be adjusted towards the grants-in-eid payable during the next year.

1. Certified that I have satisfied myself that the conditions on which the grants-in-aid was sanctioned have been duly/ are being fulfilled and that I have exercised the following check to see that the money was actually utilised for the purpose for which it was sanctioned.

Kinds of checks exercised

01. V-001329	Dt. 31.8.2016 Rs. 140000.00	
02 V-001521	dt. 08.09.2016 Rs.1563440.00	
03 V-002149	dt. 28.11.2016 Rs.2758841.00	,
	Total Rs 4462281 00	

Signature

Designation

Finance Officer **Durgapur Municipal Corporation**

@ 2 Every Commissioner **Durgapur Municipal Corporation**

EXECUTIVE ENGINEER ASANSOL DIVISION, M. E. DTE. GOVT. OF W. B

Format for Monthly status of SUH, a component under DAY-NULM

Name of the ULB: Durgapur Municipal Corporation

Status as on 31.03.2017

Amount Rs. in Lakh

Orban Shefter within DMC site at Muchipara, Bidhannagar, Durgapur		Location of the Shelter	CONTRACTOR DESCRIPTION
50-persons	のは、一般の	Capacity of cach shelter (heds)	CONTRACTOR DESCRIPTION OF
06.09.2014 vide memo no. SUDA- 29/2014/15 48 (1) dt. 06.09.2014		cach shelter approximal by (bads) = PSC	TOTAL STREET,
06.09.2014 103.56 lakhs vide memo no. SUDA-29/2014/15 48 (1) dt. 06.09.2014		打50000 0000000000	и.
16.40 lakhs		Cost (With Utensiles & Year	
6.02Jakhs (Total O & M Cost for five year= 30.10 Jakhs)		O&M Cost per Year	
150.05 lacs (GOI= 112.46 and GOWB= 37.59		Total Project cost (a+b)	Table of the state
20.05.2016 31.05.2017 as NOC received from ADDA vide memo no, ADDA/DGP /PC 410/1415/1 0085 dt 20.5.2016		OWN Total Date of Cost per Project Commence Year cost (a+b) ment of	EL STATION OF THE STATE
31.05.2017		Excepted date of completion	STATE STATE OF
35.99 lakhs		Central	
12 lakhs	からは	Fund received	
47.99 lakhs		Total	
44.62 lakhs		expenditure expenditure	
work in progress 90%	TATAL SECTION AND ADDRESS OF THE PARTY OF TH	Physical progress	一 の の の の の の の の の の の の の の の の の の の

Dagren Municul to pradice. **Durgapur Municipal Corporation** Asst. Engineer, 458TT 113 HERE

Finance Officer,

Durgapur Municipal Corporation

Finance Officer

Durgapur Municipal Corporation

Asansol Divn. M.E.DTE Govt. of W.B Executive Engineer

Durgapur Municipal Corporation Commissioner,

Commissioner Quigable Municipal Oppor

A WORNONO

Uttam Das Chairman

Dated:

Sub: - Information about the tender formalities for Construction of 50 Beded four storied shelter for urban homeless for Barrackpore Municipality under NULM.

Sir,

To,

The Chief Engineer,

Municipal Engineering Directorate, Bikash Bhavan, South Block (First Floor),

Salt Lake City, Kolkata - 700 091.

Memo No.: _

With reference to the letter no. SUDA - 272 / 2007 (Pt. IV) / 134 / 1 dated 21.04.2017 issued by Director SUDA and 357 / MA / P / C-10 / 3S-65 / 2006 dated 20.04.2017 issued by Joint Secretary to the Govt. of West Bengal, Municipal affairs Department, this is thereby informed that the tender formalities for the above mentioned work has been complied the observation laid down in the Finance Department Memo No. 9754-F(Y) dated 03.12.2012.

This is for your information please.

Thanking you.

Yours faithfully

Chairman

Sdl

Barrackpore Municipality

Memo No. 10/BKPM/CHAIRMAN/17-18/119(1)/1(2) Dated 29/04/2017

Copy to: -2. Director, SUDA, ILGUS BHAVAN, H-C Block, Sector - III, Bidhannagar, Kolkata - 700106. 2. Executive Engineer, North 24 Parganas Division, MED, Barasat, Kolkata - 700124. For information and necessary action please.

Barrackpore Municipality

Phone: 25010359

: 25017736

Fax : 25017736

Office Of The Board Of Councillors

Titagarh Municipality

From: Sri Prashanta Chowdhury

Chairman, Titagarh Municipality

No 225/T.M/17

Date: 25th April 2017

To
The Director - SUDA & Mission Director WBSULM,
H .C.Block, Sector- III,
Bidhannagar ,Kolkatta,- 7000106

Sub: Present progress of Shelter for Homeless (SUH) under DAY NULM

Sir,

This is to inform you that the soil test of the proposed site has been completed and the structural drawing and designing work are in progress.

It is expected that we will be able to float tender for the work very soon.

Yours faithfully

Pramet les smy

Chairman

Chairman TITAGARH MUNICIPALITY

BALURGHAT MUNICIPALITY

SOVA MAJUMDER SARANI



BALURGHAT: DAKSHIN DINAJPUR

PH. NO: 03522 - 255450 / 255680 / 256930 / 255649 / 256931 / 255655

<<< FAX - 03522 - 255649 >>>

e-mail - bmpality@gmail.com / bmpality@hotmail.com

website: www.balurghatpurasava.webs.com

Memo No. 204 | 6-95

Date 21.04.17

TO.

The Director, SUDA & Mission Director WBSULM,
ILGUS BHAVAN, H-C Block, Sector-III, Bidhannagar, Kolkata-106

Subject: - Submission of documents regarding construction of Shelter for Urban Homeless (SUH) under DAY-NULM within Balurghat Municipality.

Ref:- Our memo no-3392/PW-8 dated - 21.02.2017

Sir,

With reference to the above subject matter, this is to inform that we are sending herewith the required documents regarding construction of Shelter for **Urban Homeless(SUH)** under **DAY-NULM on** Municipality own land within **Balurghat Municipality** for your kind information and requested to take necessary action in this regard.

Thanking you,

Enclosed- As stated

RALLINGHAI ALONA PROPERTIES AND ALONA ALONA PROPERTIES AND ALONA ALONA PROPERTIES AND ALONA ALON

Yours faithfully

Vice- Chairman Balurghat Municipality

-gemens

OFFICE OF THE

SOVA MAJUMDER SARANI AT MUNICIPALI



BALURGHAT: DAKSHIN DINAJPUR

PH. NO: 03522 - 255450 / 255680 / 256930 / 256931 / 255655



<< EVX - 03222 - 222649 >>>

e-mail - har allty@qmall.com / bmpality@hotmail.com

: www.balurghatpurasava.webs.com

ILGUS BHAVAN, Her aller, See , Bidhannagar, Kolkata-106 The Director, 5UDA & Mission Disselet WBSULM,

under DAY-NULLS seeken Bahas has Municipality. Subject :- Submission of documents regarding construction of Shelter for Urban Homeless (SUH)

Ref:- Our memor set 1/21/2017

necessary action in

'AIS

"Nunicipality for your kind information and requested to take no NJUN-YAG 19bnu (HUS)sseless(SUH) under DAY-NULM on With reference to the above with it matter, this is to inform that we are sending herewith the

Than seidnedT

Municipality own las

required documents are a selected

Enclosed- As stated

Yours faithfully

cozus6298





OFFICE OF THE MUN PAL COUNCILLORS

ENGLISHBAZAR MUNICIPALITY, MALDA.

Ne	tali Subnas Koau, maida.	FIII-132101		
E-mail: englishbazarmunicipality@gmail.com	website: www.englishbazarmunicipality.com	n Office :(EPABX)	: 03512-252029	Fax: 03512-2533

Memo No. 3877/14

Date 31.03.2017

And 2:000000

To

The Director.

State Urban Development Agency & Mission Director, WBSULM ILGUS Bhavan, HC Block, Sector-III, Salt Lake City, Bidhannagore, Kolkata-700106.

Sub: Progress Report of Shelter for Urban Homeless at Englishbazar Municipality, Malda. dated on 20.03.2017 Ref:- SUDA-23/2014(Pt)/2967

Sir.

With reference to the above, this is to inform you that e-tender for the Shelter for Urban Homeless of Englishbazar Municipality has already been done. The physical work wills be started as soon as possible after completion of the necessary process as per NULM Guideline.

This is for your information & taking necessary action.

Chairman

Englishbazar Municipality, Malda ..date.....

Copy forwarded for information & taking necessary action

1. Chief Engineer, Municipal Engineering Directorate Bikash Bhavan, South Block (1st floor), Salt Lake. Bidhannagar, Kolkata-700091

- 2. Superintendent Engineer, MED, Central Circle, N.S Road, Malda
- 3. Executive Engineer, MED, Malda Division, Malda
- 4. Executive Officer, Englishbazar Municipality, Malda
- 5. Manager-S.D.& I., NULM Englishbazar Municipality, Malda
- 6. S.A.E-1, Englishbazar Municipality, Malda
- 7. Office Copy, Englishbazar Municipality, Malda

Chairman Englishbazar Municipality, Malda



Memo No. 3877 / 11. 2 1 13. 17 ON ENGLISHBAZAR MUNICIPAL SERVICE ONLY Date 31. 13.201 -

From : **ENGLISHBAZAR MUNICIPALITY**

P.O. & Dist. - MALDA (W.B.) PIN - 732101

...... Despatcher

The Director State urban H.c. Glock, Docker . W. Jan MYELLOY, WBSULM. I take city, Bulkannanove SAM A LOUNGH - HUMBORAL DOX. YOU



রাজ্য নগর উন্নয়ন সংস্থা



STATE URBAN DEVELOPMENT AGENCY

"ইলগাস ভবন", এইচ-সি ব্লক, সেক্টর-৩, বিধাননগর, কলকাতা-৭০০ ১০৬, পশ্চিমবঙ্গ "ILGUS BHAVAN", H-C Block, Sector - III, Bidhannagar, Kolkata - 700 106, West Bengal

	SUDA-23/2014 / 1288	5
্মিক নং	- 1	

21	.09.2015	
তারিখ		
ভা াব ৰ		

Sub: Release of funds for Shelter of Urban Homeless under NULM in Selected Urban Local Bodies.

Funds as shown herein are being released electronically in favour of the Urban Local Bodies for Shelter of Urban Homeless under NULM as first installment (40%).

Total
5
20.93
49.20
48.77
48.81
49.21
49.16
47.99

Finance Officer & Ex-Officio

Joint Director (Finance), SUDA

(*) Rs. 25.00 Lakh as Central Share was released Vide No. SUDA-23/2014/250 Dt. 31.03.15. The amount released herein represents balance of first instalment (40%).

Account Section: 2358 6408

EXECUTIVE SUMMERY

Project Details

1 State : West Beng 2 City : Durgapur

3 Project Name

Shelter for Urban Homeless of Durgapur under NULM

4 Project Cost (Rs. In Eacs) : 150.05
5 Central Share (Rs. In Lacs) : 112.46
6 State Share (Rs. In Lacs) : 37.59
7 SOR Adopted : PWD 0/81 Sc

PWD (WB) SoR w.e.f. 1.7.14

Project Contributions (Physical + Financial) (Rs. In lacs)

SI No.	Scheme Component	Quantity	Unit	Rate (in Rs./unit)	Proposed project cost (in lakh)	Appraised Project Cost (in lakh)	Central Share	State Govt.	
1	Construction of 50 beded four storied Shelter including Sanitary Plumbing and Internal Electrification.	1	No.	10355564.00	103.56	103.56	77.67	25.89	
2	Cost for furniture and Utensils	1	No.	870500.00	8.71	8.71	6,53	2.18	
3	Service Coneections (WBSEDCL)	1	LS	50000.00	0.50	0.50	0.38	0.13	
4	Fire fighting arrangement	1	LS	40000.00	0.40	0.40	0.30	0.10	
Oner	Total ation and maintenance cost	Cost		美 斯 / 李子 查尔	113.16	113.16	84.87	2829	
	0 & M Cost for maintenance of two shelter for five year	5	Yrs	602000.00	30.10	30.10	22,50	7.60	
)the	Cost	-							
1	DPR Preparation, project management, supervision & Quality control	% total cost		3%	3.39	3.39	2.55	0.85	
2	Contingency	% total cost		3%	3.39	3.39	2.55	0.85	
ALC:	经济的种类的		A PLACE	irand Total =	150.05	150.05	112.46	37.59	

Assistant Engineer
Durgapur Municipal Corporation

Commissioner

Durgapur Municipal Corporation

COOCH BEHAR MUNICIPALITY

FAX: 03582-222656 COOCH BEHAR PHONE: 03582-222286

Memo No.- PWD /

/17

Date-

From: The Chairperson,

Coochbehar Municipality

Coochbehar

To

: The Executive Engineer, M.E. Directorate,

Cooch Behar Division,

Sub: Monthly Status Report of Construction of Shelter for Urban homeless under DAY-NULM As on 17h April'2017

Sir,

Enclosed please find here with the Monthly Status Report as on 17th April'2017 of "Construction of Shelter for Urban Homeless (S.U.H.) under DAY-NULM of this Municipality as required.

Yours faithfully

Chairperson Cooch Behar Municipality Cooch Behar

Memo No.: PWD./ 126

/1(1)/17

Date- 18-04-17

Copy forwarded for information and necessary action to:-

The Director, State Urban Development Agency (SUDA), H-C Block, Sector - III, ILGUS BHAWAN, Bidhan Nagar, Kolkata - 106 -along with a copy of MPR

> Chairperson Cooch Behar Municipality
> Cooch Behar Municipality Cooch Behar

CONST. OF SUH BUILDING UNDER DAY-NULM AT COOCH BEHAR

Status as on:

17/04/2017

COOCH BEHAR MUNICIPALITY

ame of the

Shantiban, Ward No. 10	Location of the Shelter
50	Capacity of each shelter (beds)
7/31/2015	Date of approval by PSC
106.45	Civil & Electrification Cost (in Lakh) (with 3% Contingency) a
16.57	Others Cost (in Lakh) (Cost of utensiles & Furniture etc.) (b)
6.02	O&M Cost per year (in Lakh)
123.02	Total Project cost (a+b) (in Lakh)
18/01/2016	Date of Commencement of Work
31.05.2017	Excepted date of completion
64.76	Fund re
30.86	Fund received (in Lakh) entral State Tota
95.62	Lakh) Total
Rs. 60.06	Total expenditure incurred (in Lakh)
All structural works are almost completed. Outside Plastering work is in progress. Internal Elecrification work started. Service Connection from WBSEDCL will be applied very shortly.	Physical progress achieved in details (Photograph annexed of applicable)

Sub-Assivant Engineer Cooch Behar Municipality
Cooch Behar Municipality
Cooch Behar Municipality
Cooch Behar Municipality

Cooch Behar Municipality
Cooch Behar Municipality
Cooch Behar Municipality
Cooch Behar Municipality
Cooch Behar

Cooch Behar Municipality
Cooch Behar Municipality
Cooch Behar Municipality

Executive Engineer
MEDte., Cooch Behar Division
Govt. of west Bengal

Format for Monthly status of SUH, A component under DAY-NULM

Name of ULB :		Location of Shelter	KUTHIR MATH, CHANDERNAGORE
		Capacity of each Shelter (beds)	50
Chandernagore		Date of approval by PSC	16/12/2015
re		Civil & Electrification Cost (With 3% contingency)	108.28
		Civil & Civil & Civil & Date of Electrification Other Cost (Cost O & M Total Date of approval by Cost (With 3% of utensiles & Cost per Project Cost comencement PSC contingency) Furniture etc) "b" year (a + b) of work	16.68
		O & M Cost per year	6.02
		Total Project Cost (a + b)	124.96
		Date of comencement of work	15/11/2016
		Expected date of completion	15/11/2016 15/12/2017
Status as on		Central	36.23
on:	Fund Received	State	12.08
	ed	Total	48.30
		Total Expenditure incurred	7.53
05/04/2017 Amount Rs. in Lakh	Physical Pograce	achieved in details (Photograph annexed if applicable)	Column lifting upto lintel level.

huser (2/4)1"

Executive Engineer
Municipal Engineering Department

Executive Engineer
Hooghly Division
M.E. Directorate, Deptt. of M.A.
C.V.L. of West Bengal

Reakmis

Chandernagore Municipal Corporation

Mayor

Chandernagore

Municipal Corporation

Christ

41/h/21 LT02/100/



NICIPAL COUNCILLORS

UNICIPALITY, MALDA.

ad, Malda. Pin-732101

armunicipality.com Office:(EPABX): 03512-252029 Fax: 03512-25

E-ma

Date 31.03:20

Homeless at Englishbazar Municipality, Malda. dated on 20.03.2017

you that e-tender for the Shelter for Urban Homeless done. The physical work wills be started as soon as viscocess as per NULM Guideline.

necessary action.

Chairman

Englishbazar Municipality, Malda date.....

iking necessary action

an apail Engineering Directoral Bikash Bhavan, South Block (1st Bellianna ar, Kolkata-700091

Engineer, MED, Central Circle, N.S Road, Malda

meer, MED, Malda Division, Malda

icer, Englishbazar Municipality, Malda

& I., NULM Englishbazar Municipality. Malda

bazar Municipality, Malda

Englishbazar Municipality, Malda

Chairman Engl hbazar Municipality, Malda



রাজ্য নগর উন্নয়ন সংস্থা



STATE URBAN DEVELOPMENT AGENCY

"ইলগাস ভবন", এইচ-সি ব্লক, সেক্টর-৩, বিধাননগর, কলকাতা-৭০০ ১০৬, পশ্চিমবঙ্গ "ILGUS BHAVAN", H-C Block, Sector - III, Bidhannagar, Kolkata - 700 106, West Bengal

SUDA- 23/2014(Pt)/ 3093

31.03.2017 তারিখ

ক্রমিক নং

From: Jt. Director, SUDA

&

Jt. Mission Director, WBSULM

To: Chairman, Titagarh Municipality

Sub: Present progress of Shelter for Urban Homeless (SUH) under DAY NULM

Sir,

You may be aware that a 50 bedded **Shelter for Urban Homeless (SUH)** unit was sanctioned by Project Sanction Committee (PSC) in its 7 th meeting held on 04.10.2016 with an amount of Rs. 120.52 Lakh in favour of your ULB. Fund for the tune of Rs. 48.21 Lakh was released in favour of your ULB vide memo no. SUDA-109/16/2346 dated: 05.01.2017.

From the record it is noticed that any physical progress of construction work is not reported to this office till now.

You are therefore requested to inform about the progress of SUH at the earliest.

Yours faithfully,

Jt. Director, SUDA

&

Jt. Mission Director, WBSULM

Memo No. SUDA/23/2014(Pt)/ 3093//

Date: 31.03.2017

Copy forwarded for information to;

1. Chief Engineer, MED

Jt. Director, SUDA

&

Jt. Mission Director, WBSULM

90

Account Section: 2358 6408



রাজ্য নগর উন্নয়ন সংস্থা STATE URBAN DEVELOPMENT AGENCY



"ইলগাস ভবন", এইচ-সি ব্লক, সেক্টর-৩, বিধাননগর, কলকাতা-৭০০ ১০৬, পশ্চিমবঙ্গ "ILGUS BHAVAN", H-C Block, Sector - III, Bidhannagar, Kolkata - 700 106, West Bengal

	SUDA-	23/2014(Pt)/	3093	
484				

31.03.2017

ক্রমিক নং

তারিখ

From: Jt. Director, SUDA

&

Jt. Mission Director, WBSULM

To: Chairman, Titagarh Municipality

Sub: Present progress of Shelter for Urban Homeless (SUH) under DAY NULM

Sir,

You may be aware that a 50 bedded **Shelter for Urban Homeless (SUH)** unit was sanctioned by Project Sanction Committee (PSC) in its 7 th meeting held on 04.10.2016 with an amount of Rs. 120.52 Lakh in favour of your ULB. Fund for the tune of Rs. 48.21 Lakh was released in favour of your ULB vide memo no. SUDA-109/16/2346 dated: 05.01.2017.

From the record it is noticed that any physical progress of construction work is not reported to this office till now.

You are therefore requested to inform about the progress of SUH at the earliest.

Yours faithfully,

Jt. Director, SUDA

&

Date: 31.03.2017

Jt. Mission Director, WBSULM

Memo No. SUDA/23/2014(Pt)/ 3093//

Copy forwarded for information to;

1. Chief Engineer, MED

Jt. Director, SUDA

R

Jt. Mission Director, WBSULM

90

দ্রভাষ ঃ ২৩৫৮ ৬৪০০ / ৫৭৬৭, ফ্যাক্স ঃ ২৩৫৮ ৫৮০০

Tel: 2158 6403/5767, Fax: 2158 5800, E-mail: wbsudedir@gmail.com

Account Section: 2358 6408

Phone No.: 03216 270572 Fax No.: 03216 237031



HABRA MUNICIPALITY

(ESTD.-1979)

POURA BHAWAN

PROMODE DASGUPTA SARANI, P.O. HABRA, NORTH 24 PARGANAS, PIN-743263 e-mail: habramunicipality@yahoo.com

Ref. No. HM / 2681 / NULM / 17

To,
Director SUDA &
Mission Director, WBSULM
ILGUS BHAVAN
Salt lake, Kolkata 700106



Date. 20/09/2013....

Sub: Present Progress of Shelter for Urban Homeless(SUH)under DAY-NULM

Ref: Memo No.: SUDA-23/2014(Pt)/2966

Sir,

With reference to the above mentioned memorandum no. the 50 bedded Shelter for Urban Homeless (SUH) unit, which was sanctioned by Project Sanction Committee (PSC), is under tender procedure and yet to be opened.

Thanking You.

Yours faithfully

Chairman

Habra Municipality

CHAIRMAN HABRA MUNICIPALITY

COMPOSE

Fwd: Status report on DAY-NULM Inbox x

Inbox (631)

Gmail

Starred

Sent Mail

Drafts (608)

29 CLC Inaugration

Annual Action Plan...

CLC Report

CLSC Meeting

ESTP

ESTP PROPOSAL...

IEC Feeds-Case

MIS DEO

MIS Questions



Tarakeswar Muni... Sent a message





Mrinal Rano

to me

----- Forwarded message -----

From: Mrinal Rano < numalrano@umail.com>

Date: Fri, Feb 10, 2017 at 4:08 PM

Subject: Re: Status report on DAY-NULM

To: Santanu Das JS MA WB < jsmawb2016@gmail.com>

Please find the attachment, M.K. Rano

On Fri, Feb 10, 2017 at 1:06 PM, Santanu Das JS MA WB < ismawb2016@please see the two attachments



W STATUS OF SHEL.

STATUS OF SHELTER FOR URBAN HOMELESS UNDER DAY-NULM in West Bengal

SI no.	Shelters Sanctioned Since inception	Shelters Planned Since	Shelters Operational till date						
		inception	Under DAY- NULM	Other than NULM					
1	28	43	1	43					

In response to D.O.No. 3/8/2017-ZCS(E) dated: 20.01.2017 addressed to Chief Secretary Govt. Of West Bengal

GOVERNMENT OF WEST BENGAL URBAN DEVELOPMENT & M A DEPARTMENT (MUNICIPAL AFFAIRS BRANCH) POURA PRASHASAN BHAWAN DD-I, SECTOR-I, SALT LAKE, KOLKATA-700 064 J8(M)

No. 219/MA/P/C-10/3S-15/2017.

Dated, Kolkata, the 23rd March, 2017.

From: The Joint Secretary to the Government of West Bengal.

To: The Director,

State Urban Development Agency, ILGUS Bhavan, Block-HC, Sector-III, Salt Lake City, Kolkata-7100106.

Sub: Establishment of Shelters for Urban Homeless under DAY-NULM

Sir,

With reference to above, I am directed to forward a copy of D.O. No.3./8/2017 ZCSE, dated 20.01.2017 addressed to the Chief Secretary by Additional Secretary and Adviser, Inter-state Council Secretariat, Ministry of home Affairs, Government of India and to request you to furnish a status report on the above quoted subject at the earliest for its onward transmission to the Chief Secretary.

Enclos: As stated above.

Yours faithfully,

Joint Secretary to the Government of West Bengal.

रोलखूमलेन बुहरिल, आई.ए.एस. 08.02.17 अपर्-मधिव एवं परामर्शी

Rusikhumlien Buhril, I.A.S. Addl. Secretary & Adviser



अन्तर्राज्य परिषद सचिवालय गृह मंत्रालय, भारत सरकार Inter-State Council Secretariat Ministry of Home Affairs Government of India

D.O. No. 3/8/2017-ZCS (E)

Dated the 20th January, 2017

Dear Shui Bornold Sanger,

The Ministry of Housing and Urban Poverty Alleviation has sponsored an item "Establishment of Shelters for Urban Homeless under DAY-NULM" for inclusion in the agenda of the next (23rd) meeting of the Eastern Zonal Council. The Explanatory Memorandum received from the Ministry in this regard is enclosed for your kind perusal.

We shall be grateful if you could kindly furnish the comments of your State Government on the aforesaid issue to us at an early date.

Suman see shall

With regards

Yours Sincerely,

(R. BUHRIL)

2800117

Shri Basudeb Banerjee Chief Secretary, Government of West Bengal, KOLKATA-700001.

Secretary MA 4 UD depth

Room No. 346, 2nd Floor, Vigyan Bhavan Annexe, Maulana Azad Road, New Delhi- 110 011 Telefax: 011-23022237 E-mail: adviser.iscs@nic.in

Item No. 9 Establishment of Shelters for Urban Homeless under DAY-NULM (Sponsored by Ministry of Housing and Urban Poverty Alleviation)

Ministry of Housing and Urban Poverty Alleviation has been pursuing with the member States on establishment of shelters for Urban Homeless under DAY-NULM.

Present status of implementation by States of Eastern Zone

State	Shelters Sanctioned	Shelters Planned	Shelters Operational
	26	10	2
Odisha		13	13
Jharkhand	35	24	25
Bihar	114	34	(03)
West Bengal	50	10	(31)

The States of Odisha, Jharkhand, Bihar and West Bengal are to speed up operationalizing the shelters already sanctioned during 2014-15 and 2015-16. The shelters planned for the year 2016 are to be sanctioned expeditiously.

Action: The Member States to respond about the progress of implementation.

			١.
۲.		τ.	А.
	۳.	ъ	
	- 1	ъ	
		п	7
٦,		_	•

To:	Γ	ł	1	E	2)	i.	S	t	ľ	j	(-	t	ľ	V	1	1	3	8	3	1	>	t	r	4	3	t	:6	١,					
) į	S	t	r	i	C

Sub: Functionalization of newly constructed Shelters under the scheme Shelter for Urban Homeless (SUH) under the Programme NULM in the Urban Local Bodies in West Bengal

Department of Urban Development and Municipal Affairs (UDMA) has sanctioned 28 sheltersunder the scheme Shelter for Urban Homeless under National Urban Livelihoods Mission (NULM) in different Urban Local Bodies in West Bengal. Out of these 28 shelters One shelter in East Medinipur District and Two shelters in Nadia District have already been completed. Another 1 shelter in Burdwan District, 1 shelter in North 24 paragana District and1 in Coochbehar District are in various stages and are expected to be completed within the stipulated time.

You are requested to take suitable action to guide the ULBs to make all these shelter functional as soon as the construction work is completed.

In this connection it may be informed that in pursuance of the Hon'ble Supreme Court a Committee has been formed for physical verification of the available shelters for Urban Homeless and the Committee will submit a report to the Hon'ble Supreme Court.

Chief Secretary Govt. of West Bengal

HOWRAH MUNICIPAL CORPORATION

Monthly status of SUH, a component under DAY-NULM

			3.8
		9, Koipekur Lane	Name of the Shelter
		EPOST CONTRACTOR OF THE PARTY O	Capaci y of each shelter (beds)
		50 20.08.2016 107.19 8.705	St. Name of the yellow approval by coast (Frill St. Shelter shelter than the coast (Frill St. Itensited & coast (Frill St. Itensited
		107 19	Civil de Coher Class Electrification cont of cont (with 3% atensited de contingency) Farminate of a (lo Lakke) b (m Lakku
		8.705	Other time (
	音楽を		O EM
		115.895	Total Project Cost (9+5) (In Lakha)
		115.895 01.08,2016 01.08.2017	One of Commentment of Work
		01.08.2017	Excepted date find real complition Central
			Fand received Central State
		IDIAS advance for 2 shelters	(caldes)
The state of the s		186	Total expenditure insured (In Lahly)
		1st Floor Roof pasted & 2nd Floor Staircase casted	Physical progress archived in depols (Physical progress archived in depols (Physical pays archive)

Transport of

Likely word

Executive Engineer
Hooghly Division
M.E. Directorate, Deptt. of M.A.
Govt. of West Bengal

Commissioner aloly

Commissioner H. M.C. &

HOWRAIT MUNICIPAL CORPORATION

Monthly status of SUH, a component under DAY-NUM

	15					100		PO E E PO
							n Neighbar Lane	South of the
							2	Control of the contro
							20.08.00.6 197.19	Variety of the state of the sta
							19719	Facerdication rost paids 3% contingency a 65 Ladey
							0	cost of outers described by the Lin Fields of th
								near tast beta W W O
							115,895	Fotal Project Cost (a+b) (In Lakis)
							115,895 01.08,2016 01.08,2017	Date of Commendations of Work
							01.08.2017	Excepted date of completion
								Fund received (Lakhs) Contral State Total
							50(As advance for 2 shelters)	(Lokhs) Tepd
							169	Total expenditure incurred (in Ladher
	1						Int Floor Roof tastest & Ind Floor Staircase unsted	Obvious progress school and to details a Shangraght annexed of application.

Executive Engineer
Hooghly Division
M.E. Directorate, Deptt. of M.A.
Govt. of West Bengal

Commissioner (A)



STD No.: 03215

Phone: 255021 257387 Fax: 257641 E-mail: chairmanbm@gmail.com

Website www.bongaonmunicipality.org

Office of the Bongaon Municipality

BONGAON, NORTH 24 PARGANAS.

Sri. Sankar Addhya

BONGAON MUNICIPALITY

M.: 9002004688

Ref. No.: Nemmur B.M. 5'20

Dated: 06.03 17

To

The Executive Engineer

24-Parganas Division

Municipal Engineering Directorate

7, K.B.Bose Rd. (2nd floor) Barasat, North 24 Parganas

Kolkata - 700124

Sub: Submission of Monthly Status of SUH with site Photograph, a component under DAY-NULM upto the month of January, 2017.

The under signed is sending the monthly Status of SUH with site Photograph, a component Sir, under DAY-NULM upto the month of January, 2017.

You are requested to take necessary action from your end.

Thanking you,



Enclo:- As stated above



Yours faithfully

Bongaon Municipality
